



রাজ্য নগর উন্নয়ন সংস্থা
STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ
“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-Health/NUHM/421/15/10376

21.04.2020

ক্রমিক নং

তারিখ

MEMORANDUM

Funds are hereby released electronically in favour of your ULB as per details enclosed herewith for implementation of National Urban Health Mission (NUHM).

The expenditure shall be incurred as per the annexed activities abiding by the standard norms of NUHM. Statement of Expenditure (SOE) & Utilization Certificate (UC) may please be sent monthly and quarterly respectively. Utilization Certificate (UC) may be uploaded in SUDA website at sudawb.org-> e-services within 60 days.

Encl: As stated.

Finance Officer, SUDA

Memo No. SUDA-Health/NUHM/421/15/10376/1(4)

21.04.2020

CC

1. The Mayor, Durgapur Municipal Corporation
2. Additional Director, SUDA & Joint Secretary, UD&MA Department
3. The Commissioner, Durgapur Municipal Corporation
4. The Nodal Officer, NUHM, Durgapur Municipal Corporation

Finance Officer, SUDA

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408

**SUDA**

রাজ্য নগর উন্নয়ন সংস্থা

STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-Health/NUHM/421/15/

22.04.2020

ক্রমিক নং

তারিখ

From : Finance Officer, SUDA

To : The Branch Head,
Axis Bank Limited,
Chetla Branch,
29/6C, Chetla Central Road,
Chetla, Ward No.82,
Kolkata - 700 027.

Sub.: Electronic Transfer of Fund from our A/C No.918010003016076

National Urban Livelihood Mission (NUHM)

Sir,

You are requested to kindly arrange for electronic transfer of funds as per details given below debiting the amount from this office Savings Account No.918010003016076 lying with your branch in respect of National Urban Livelihood Mission (NUHM).

Sl.	Name of Payee	Amount in Rs.	Bank Details
01.	Durgapur Municipal Corporation	81,48,333.00	Punjab National Bank, Benachity (Durgapur) Branch, A/C No.0158000102449998 IFS Code.PUNB0015800

(Rupees Eighty One Lakh Forty Eight Thousand Three Hundred Thirty Three only)

(Petrus Anuranjan Soreng)
Finance Officer
SUDA

(Goutam Hore)
Finance Officer
SUDA

22-04-2020

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408

12.06.20



STATE URBAN DEVELOPMENT AGENCY-NUHM

Statement Generated By :- 4680

Joint Holder :-
 STATE URBAN DEVELOPMENT AGENCY
 HC BLOCK SECTOR 111 BIDHANNAGAR KOLKATA
 700106 NEAR PANCHAYAT BHAVAN CITY SALT LAKE
 WEST BENGAL
 700106

Customer No :863033113
 Scheme :SB-GOVT.ORGANISATIONS
 Currency :INR

Statement of Account No :918010003016076 for the period (From : 01-04-2020 To : 15-06-2020)

Tran Date	Chq No	Particulars	Debit	Credit	Balance	Init. Br
		OPENING BALANCE			210422789.00	
23-04-2020		RTGS/SK/UTIBR52020042300350650/2793/DU RGAPU/PUNJA	8148333.00		202274456.00	2793
		TRANSACTION TOTAL	8148333.00	.00		
		CLOSING BALANCE			202274456.00	

Unless the constituent notifies the bank immediately of any discrepancy found by him/her in this statement of Account, it will be taken that he/she has found the account correct.

The closing balance as shown/displayed includes not only the credit balance and / or overdraft limit, but also funds which are under clearing. It excludes the amount marked as lien, if any. Hence the closing balance displayed may not be the effective available balance. For any further clarifications, please contact the Branch.

We would like to reiterate that, as a policy, Axis Bank does not ask you to part with/disclose/revalidate of your iConnect passord,login id and debit card number through emails OR phone call Further,we would like to reiterate that Axis Bank shall not be liable for any losses arising from you sharing/disclosing of your login id, password and debit card number to anyone. Please co-operate by forwarding all such suspicious/spam emails, if received by you, to customer.service@axisbank.com

REGISTERED OFFICE - AXIS BANK LTD,TRISHUL,Opp. Samartheswar Temple, Near Law Garden, Ellisbridge, Ahmedabad . 380006.This is a system generated output and requires no signature.


Legends :

- ICONN - Transaction trough Internet Banking
- VMT-ICON - Visa Money Transfer through Internet Banking
- AUTOSWEEP - Transfer to linked fixed deposit
- REV SWEEP - Interest on Linked fixed Deposit
- SWEEP TRF - Transfer from Linked Fixed Deposit / Account
- VMT - Visa Money Transfer through ATM
- CWDR - Cash Withdrawal through ATM
- PUR - POS purchase
- TIP/ SCG - Surcharge on usage of debit card at pumps/railway ticket purchase or hotel tips
- RATE.DIFF - Difference in rates on usage of card internationally
- CLG - Cheque Clearing Transaction
- EDC - Credit transaction through EDC Machine
- SETU - Seamless electronic fund transfer through AXIS Bank
- Int.pd - Interest paid to customer
- Int.Coll - Interest collected from the customer

++++ End of Statement +++++

Release of fund under NUHM
Vide Memo No. SUDA-Health/NUHM/421/15 dt. 21.04.2020

ULB	FMR Code	Budget Head	A/C No. & Bank	Fund Released (Amount in Rs.)
Durgapur MC		Building of new UPHC (9 & 11 - NUHM)	A/C No. 0158000102449998, Punjab National Bank	81,48,333.00


21.04.20.
Finance Officer, SUDA

Search Images Maps Play YouTube Gmail Drive Calendar More » dfidhhw@gmail.com | My Account | Settings | Help | Sign out
 You have been redirected to the basic HTML version because this browser is not supported. To use standard view, please upgrade to a supported browser.

M Gmail Search Mail Search the Web [Show search options](#)
[Create a filter](#)

Compose Mail [Back to inbox](#) Archive Report Spam Delete More Actions... [Newer 15 of about 193 Older](#)
[Print](#) [New window](#)

- Inbox (41)**
- Starred
- Sent Mail
- Drafts
- All Mail
- Spam (1)
- Bin
- Contacts
- Labels
- Unmap/Sent
- Unmap/Trash
- Area Demarca
- Dengue (27)
- Dengue (Nov. ... (295))
- Dengue (Nov. ... (284))
- Dengue (Oct. ... (255))
- Dengue 2018 (3)
- Dengue (Oct. ... (261))
- Dengue (Sept. ... (84))
- Dengue (Sept. ... (251))
- Dengue1 (38)
- Elisa
- Machin... (1)
- February 1st... (239)
- February 2nd... (85)
- Fogging & Sp
- H-to-H Jan ... (148)
- H-to-H Jan 2... (229)
- Inbox/New to
- Inbox/New to...
- Junk
- Man Power CB
- March 1st ro... (72)
- March 2nd ro... (36)
- Micronplan 20... (58)
- Personal PREPAREDNESS
- Receipts
- Travel
- Vector Borne...
- Work
- Edit labels

CODE WISE REFUND AMOUNT 10992

22 March 2018 at 16:29

Atanu Rudra <rudra.atanu81@gmail.com>
 To: dfidhhw <dfidhhw@gmail.com>
[Reply](#) | [Reply to all](#) | [Forward](#) | [Print](#) | [Delete](#) | [Show original](#)

DURGPUR MUNICIPAL CORPORATION		
As per your order no.SUDA-Health/NUHM/413/15/328(06) Dated 16/02/2018, I am the below mentioned amount.		
FMR CODE	ACTIVITY	REFUNDED AMOUNT AS PER YOUR ORDER
2.3.1	SALARY OF STAFF AT CITY PMU	300000
3.5	ORIENTATION OF MAS	550000
4.3.1	RENOVATION AND UPGRADATION OF U-PHC	1600000
4.3.3.1.1	SALARY OF FULL TIME AND PART TIME MO	550000
4.3.3.1.2	SALARY OF STAFF NURSE, PHARMACIST AND LAB TECHNICIAN	300000
4.3.3.2	UPGRADATION OF MATERNITY HOME	5940821
4.3.2	UPGRADATION OF NEW U-PHC	7000000
4.3.5	MEDICINE AND CONSUMABLES FOR U-PHCS	200000
4.4.3	MEDICINE AND CONSUMABLES FOR U-PHCS	250000
4.4.3	UNITED GRANT FOR UCHCS	780000
6.1	MAS	17470821
TOTAL		17470821

Quick Reply
 To: Atanu Rudra <rudra.atanu81@gmail.com> [More Reply Options](#)

Include quoted text with reply

[Back to inbox](#) Archive Report Spam Delete More Actions... [Newer 15 of about 193 Older](#)

Get Gmail on your mobile phone at <http://mail.google.com> using your phone's web browser. [Learn more](#)
 You're currently using 10739 MB (69%) of your 15360 MB
 This account is currently being used in 1 other location at this IP (49.203.216.17). Last account activity: 0 minutes ago on this computer. [Details](#)
[Terms](#) · [Privacy](#) · [Google Home](#)

Page No :

M/S. STATE URBAN DEVELOPMENT AGENCY NURM
 STATE URBAN DEVELOPMENT AGENCY WEST
 BENGAL ILGUS SHAVAN MC BUCK, SECTOR 111, SALT LAKE CITY
 KOLKATA 700196
 WEST BENGAL INDIA

JOINT HOLDERS :

Nomination : Not Registered
 Statement From: 22/03/18

To: 22/03/18

Account Branch : SALT LAKE - SECTOR 1
 Address : CR-154,
 SALT LAKE
 SALT LAKE SECTOR-2
 City : KOLKATA 700106
 State : WEST BENGAL
 Phone No. : 033-6160161
 RTGS/NFT IFSC : HDFC00G1128 MICR: 700240052
 Email : dfidhhw@gmail.com
 OD Limit : 0.00 Currency : INR
 Cust ID : 61276560 Pr.Code : 981 Br.Code : 1128
 Account No : 5020011146861 OTHER
 A/C Open Date : 26/03/2015
 Account Status : Regular

22/03/18	NEFT DR-SBIN0010043-WEST BENGAL STATE HEALTH AND FAMILY WELFARE SAMITI-SALT LAKE SE-N061180501419084	NO81180501419084	22/03/18	59,910.00	711
22/03/18	NEFT CR-FUNB0016600-DURGAPUR URBAN HEALTY SOCIETY-STATE URBAN DEVELOPMENT-FUNB018081444041	FUNB18081444041	22/03/18	17,470,821.00	18,182

STATEMENT SUMMARY

Opening Balance
 771,193.50

Debits	59,910.00	Credits	17,470,821.00	Closing B	18,182
Dr Count	1	Cr Count	1		

Generation Date : 22-Mar-18 10:15

Generated by : A18F14


Requesting Branch Code : 1128


State account branch GSTN:19AAACH2702H123
 HDFC Bank GSTIN number details are available at:
<https://www.hdfcbank.com/personal/making-payments/online-tax-payment/goods-and-service-tax>
 Registered Office Address: HDFC Bank House, Senapati Bapat Marg, Lower Parel, Mumbai 400013
 Contents of this statement will be considered correct if no error is reported within 30 days of receipt of statement.

Fund Status of New Constructions UPHCs under NUHM- Durgapur MC
(as on 29.02.2020)

SI No.	New Construction UPHCs	Vetting Amount (Rs)	Fund Received till (Rs) 29.02.2020	Total Refund to SUDA
1	Durgapur UPHC 9 Ward No.37 Pursha	53,03,333.00		
2	Durgapur UPHC 10 Ward No.13 Ramkrishna Pally	66,61,072.00	47,00,000.00	
3	Durgapur UPHC 11 Ward No.18 Prantika	58,45,246.00	1,00,00,000.00	70,00,000.00
	Total:	1,78,09,651.00	1,47,00,000.00	70,00,000.00


 Account Manager
 NUHM-DMC
 Durgapur MC



 Executive Engineer
 Durgapur Municipal Corporation
 M. E. DTE
 GOVERNMENT OF W.B.
 POSTED AT
 DURGAPUR MUNICIPAL CORPORATION


 Commissioner
 Durgapur Municipal Corporation
 Durgapur Municipal Corporation

Ref. No. NUHM/AMC/450Date : 01.02.2020

To,
The Director
State Urban Development Agency
Govt. of West Bengal

Sub: Fund Requisition for Construction under NUHM

Madam/Sir,

Whereas from the Financial Management Report for the month of Dec'19 it has been found that the fund for construction under NUHM are very low which are depicted below;

SL No	Activity Code	Activities	Amount (Rs.)
1	P.04.03.01	Renovation/ Upgradation of Existing Facility to UPHC NUHM	-46,83,950.00
2	P.04.03.02	Building of New UPHC NUHM	30,136.00

Now, you are requested to allot the necessary fund under the above noted code for smooth running of the activities.

A brief Construction report under NUHM at Asansol MC is hereby annexed herewith for your kind perusal.

Thanking you,

Yours sincerely

*Shanmugy.*Health Officer 01/02/2020

Asansol Municipal Corporation

Date;

Ref. No; NUHM/AMC/450-1(8)

Copy Forwarded for kind information and necessary action please to The;


1. Hon'ble Mayor, Asansol Municipal Corporation
2. Commissioner, Asansol Municipal Corporation
3. State Nodal Officer- NUHM, Govt. of West Bengal
4. Secretary, Asansol Municipal Corporation
5. CMOH, Paschim Bardhaman
6. MMIC (Health), Asansol Municipal Corporation
7. Health Advisor (NUHM), Asansol Municipal Corporation
8. Office Copy


*Shanmugy.*Health Officer 01.02.2020

Asansol Municipal Corporation

Construction Report of Asansol MC under NUHM

Sl. No.	Name of ULB	Field Office	Name of U-PHC / U-CHC / MH with address and Ward No.	Whether Sanctioned for Renovation / New Construction / Upgradation **	Year of sanctioned	Construction Status	Whether functional or not (Yes / No)
1	ASANSOL MC	ASANSOL	HAU at Dharmapally, Ward No. - 51	R	2013-14	100%	Yes
2			HAU at Dildar Nagar, Ward No. - 41	R	2013-14	100%	Yes
3			HAU at Beldanga, Ward No. - 31	R	2013-14	100%	Yes
4			HAU at Dhadka near Water Tank, Ward No. - 21	R	2013-14	100%	Yes
5			HAU at Rahinardihi near Rifle Club, Ward No. - 23	R	2013-14	100%	Yes
6			Dhadka Village, Ward No. - 15	R	2013-14	100%	Yes
7			Mohishilla Village, Ward No. - 07	R	2013-14	100%	Yes
8			HAU at Alam Nagar, Ward No. - 82	R	2013-14	100%	Yes
9			HAU at Nabaghanti, Ward No. - 95	R	2013-14	100%	Yes
10			HAU at Radhanagar Road, Near Chinnamasta Kali Mandir, Ward No. - 56	R	2013-14	100%	Yes
11			HAU at Kulapur, Ward No. - 97	R	2013-14	100%	Yes
12		ESOPD Cum MH at O.K Road, Ward No.- 25	U	2013-14	100%	Yes	
13		ESOPD Cum MH at Vivekananda Palli, Ward No.- 85	U	2013-14	100%	Yes	
14		Jamuria Field Office:	Balanpur beside Balanpur Road and opp Satwik Cement, Ward No.-07 (Plot no.-46, JL No.-36, Mouza-Balanpur)	NC	2014-15	100%	Yes
15		Jamuria 6no. Bye pass road opp Jamuria truck & Taxi stand, Ward No.-4 (Plot No.-1984, JI No.-21, Mouza-Jamuria)	NC	2014-15	100%	Yes	
16		Pariharpur Bagan, Pariharpur, Ward No.-03 (Plot No.-2151, 2149, JL No.-22, Mouza-Pariharpur)	NC	2014-15	85%	No	
17		Raniganj Field Office:	Tewari Para within RS Plot No. 227 Mouza - Egara at ward no-93	NC	2014-15	85%	No
18		Shanti Danga, Plot No.-47 & 49, Mouza- Baktar Nagar, Ward No- 35	NC	2014-15	100%	Yes	
19		Sishu Bagan Area	NC	2014-15	0%	No	
20		Koild Field Office:	Bidyandapur PHC, ward no. 99 (new)	R	2015-16	100%	Yes
21		Sodepur PHC, ward no. 102 (new)	R	2015-16	100%	Yes	
22		Kumardiha PHC, ward no. 59 (new)	R	2015-16	100%	Yes	
23		Dhemomai, ward no. 58 (new)	NC	2015-16	100%	Yes	
24		Dishergarh, ward no. 105 (new)	NC	2015-16	100%	Yes	
25		Barakar, ward no. 67 (new)	NC	2015-16	55%	No	


 03/02/2020
 Executive Engineer
 Asansol Municipal Corporation


 2nd Nodal Officer
 National Urban Health Mission
 Asansol Municipal Corporation

ASANSOL MUNICIPAL CORPORATION
Fund Status for New Construction of UPHC under NUHM

Sl NO	Name of Health Centre	Approved	Estimated Amount (Rs.)	Work Order No	Expenditure Incurred	Scheme Balance(Rs.)	Physical Status	Remarks
1	Balanpur beside Balanpur Road and opp Satwik Cement Ward No.-07 (Plot no.-46, JL No.-36, Mouza-Balanpur)	New Construction	Rs. 62,00,000.00	537/PW/Eng/16 dated 03.08.2016 of Secretary Asansol MC	Rs. 61,99,914.00		100%	✓ 2nd RA Bill of Rs. 4286402 submitted for payment
2	Jamuria 6no. Bye pass road opp Jamuria truck & Taxi stand, Ward No.-4 (Plot No.-1984, JL No.-21, Mouza-Jamuria)	New Construction	Rs. 62,00,000.00	538/PW/Eng/16 dated 03.08.2016 of Secretary Asansol MC	Rs. 19,01,326.00		100%	2nd RA Bill of Rs. 4286402 submitted for payment
3	3)Parharpur Bagan, Parharpur, Ward No.-03 (Plot No.-2151,2149, JL No.-22, Mouza-Parharpur)	New Construction	Rs. 62,00,000.00	539/PW/Eng/16 dated 03.08.2016 of Secretary Asansol MC	0		85%	1st RA Bill of Rs. 337985 submitted for payment
4	Tewari Para within RS Plot No. 227 Mouza -Egara at ward no-93, Raniganj	New Construction	Rs. 62,02,808.00	1213/9/PW/Eng/16 dated 14.12.2016 of Secretary Asansol MC	Rs. 19,48,267.00		85%	
5	Jhanti Danga, Plot No.-47 & 49, Mouza- Baklar Nagar, Ward No-35, Raniganj	New Construction	Rs. 62,02,808.00	761/PW/Eng/17 dated 07.07.2017 of Secretary Asansol MC	Rs. 26,53,484.00	Rs. 30,136.00	100%	2nd RA Bill of Rs. 2702644 submitted for payment
6	Sishu Bagan Area, Raniganj	New Construction		Vetting Completed			0%	
7	Bidyandadapur PHC, ward no. 99 (new)	New Construction					100%	
8	Sodepur PHC, ward no. 102 (new)	New Construction	Rs. 24,82,839.00	1280/PW/Eng/16 dated 21.01.2016	Rs. 23,74,815.00		100%	
9	Kumardaha PHC, ward no. 59 (new)	New Construction					100%	
10	Dhemomain, ward no. 58 (new)	New Construction	Rs. 69,80,272.00	4277/PW/Eng/16 dated 04.03.2016 of Secretary, Asansol MC	Rs. 59,20,409.00		100%	
11	Dishergarb, ward no. 105 (new)	New Construction	Rs. 69,80,272.00	1983(7)/PW/Eng/16 dated 03.03.2016 of Secretary, Asansol MC	Rs. 64,01,163.00		100%	
12	Barakar, ward no. 67 (new)	New Construction	Rs. 62,00,000.00	724/8/PW/Eng/2018 dated 21.06.2018 of Secretary, Asansol MC	0		55%	
Total						Rs. 2,73,99,378.00	Rs. 30,136.00	


Dr. 12.03.2020

[Signature]
Health Officer
Asansol Municipal Corporation

New construction UPHCS Asansol Municipal Corporation

Name of UPHC with ward no.	Physical progress as on 30.11.2019	Total project cost	Fund received from State from inception till Sept. 2019	Total expenditure till 30.11.2019	Refund to DHPW	Fund lying unspent with MC
Balanpur beside Balanpur Road and opp Sawtik Cement Ward No-07 (Plot no.-46, JI No.-36, Mouza-Balanpur) (New)	100% ✓	Rs. 62,00,000.00		Rs. 61,99,914.00	0	
Jamuria 6no. Bye pass road opp Jamuria truck & Taxi stand, Ward No.-4 (Plot No.-1984, JI No.-21, Mouza-Jamuria) (New)	100% ✓	Rs. 62,00,000.00		Rs. 19,01,326.00	0	
3) Partharpur Bagan, Partharpur, Ward No.-03 (Plot No.-2151, 2149, JI No.-22, Mouza-Partharpur) (New)	85% ✓	Rs. 62,00,000.00		0	0	
Tewari Para within RS Plot No. 227 Mouza - Egara at ward no-93, Raniganj (New)	85% ✓	Rs. 62,02,808.00	Rs. 2,74,29,514.00	Rs. 19,48,267.00	0	Rs. 30,136.00
Jhanti Danga, Plot No.-47 & 49, Mouza-Baktar Nagar, Ward No-35, Raniganj (New)	100% ✓	Rs. 62,02,808.00		Rs. 26,53,484.00	0	
Sislu Bagan Area, Raniganj (New)	0% ✓	0		0	0	
Bidyandandapur PHC, ward no. 99 (new)	100% ✓	0		0	0	
Sodepur PHC, ward no. 102 (new)	100% ✓	Rs. 24,82,839.00		Rs. 23,74,815.00	0	
Kumardha PHC, ward no. 59 (new)	100% ✓	Rs. 69,80,272.00		Rs. 59,20,409.00	0	
Dhemomain, ward no. 58 (new)	100% ✓	Rs. 69,80,272.00		Rs. 64,01,163.00	0	
Dishergarh, ward no. 105 (new)	100% ✓	Rs. 69,80,272.00		Rs. 64,01,163.00	0	
Barakar, ward no. 67 (new)	55% ✓	Rs. 62,00,000.00		0	0	
Total		Rs. 5,36,48,999.00	Rs. 2,74,29,514.00	Rs. 2,73,99,378.00		Rs. 30,136.00

Sawtik
12.03.2019


 Health Officer
 Asansol Municipal Corporation
 12.03.2019

N.U.H.M.
DURGAPUR URBAN HEALTH SOCIETY

C/O. DURGAPUR MUNICIPAL CORPORATION
CITY CENTRE, DURGAPUR - 713216

Ref. No. DUHS/242.....

Date. 27/01/2020.....

To
The Director
State Urban Development Agency
Ilgus Bhavan
H-C Block, Sec III
Kolkata, WB

Sub: Prayer for Fund regarding new construction of UPHCs under NUHM- Durgapur MC

Madam,

This is to inform you that presently we are suffering from serious crisis of fund in respect to new construction of UPHCs under NUHM- Durgapur MC. Currently construction of two UPHC new buildings have been completed and other one has been completed up to 85 % for what I am sending the physical progress along with financial requirement as annexure I with this letter.

This will be kind enough if you sanction fund as per our requirement.

Thanks and regards

Sincerely

P m G
27/1/2020
ds
Commissioner
Durgapur Municipal Corporation
&
Vice Chairman, DUHS
Commissioner
Durgapur Municipal Corporation

Durgapur Urban Health Society
City Centre, Durgapur, Paschim Bardhaman
NUHM- Durgapur MC

New construction Status of UPHCs under NUHM, Durgapur Municipal Corporation (27.01.2020)

Name of UPHC with ward no.	Physical progress as on 30.11.2019	Total project cost	Total expenditure till 27.01.2020	Date of functional of UPHC	Expected date of functional of UPHC	Fund Required (Rs.)
Durgapur UPHC 9 Ward No.37 Pursha	100%	6500000.00	3510080.00	8.11.2018	NA	13247461.00
Durgapur UPHC 10 Ward No.13	85%	6500000.00	2125624.00	NA	31.03.2020	
Ramkrishna Pally Durgapur UPHC 11 Ward No.18 Prantika	100%	6500000.00	3618852.00	22.08.2019	NA	

Signature
27/01/2020

Accounts Manager
NUHM-BMC



Signature
27/01/2020

Executive Engineer
Durgapur MC ENGINEER

M. F. DTE
GOVERNMENT OF W.B.
POSTED AT
DURGAPUR MUNICIPAL CORPORATION

Signature
27/1/2020

Commissioner
Durgapur MC

Commissioner
Durgapur Municipal Corporation

New Construction (As on January 2020)

		(Amount in Rs.)								
ULBS	Sanctioned No.	Requirement @ Rs. 75 Lakh	Fund released to ULBS	Refund to DHFW	SOE submitted					
					2019-20 (upto January 2020)	2018-19	2017-18	2016-17	2015-16	Total
DMC	3	2,25,00,000.00	1,47,00,000.00	70,00,000.00	14,53,395.00	46,97,776.00	9,08,255.00	6,46,508.00	-	77,05,934.00
AMC	12	9,00,00,000.00	3,06,41,274.00	-	95,57,268.00	67,84,434.00	1,42,69,436.00	-	-	3,06,11,138.00

[Handwritten Signature]

status as in December - 2019 .

Infrastructure Strengthening	AMC				DMC			
	Annual Approval (As per RoP)	Construction Not Yet Initiated	Under Construction / Renovation	Completed / Functional	Annual Approval (As per RoP)	Construction Not Yet Initiated	Under Construction / Renovation	Completed / Functional
9.1.1) New Construction	12	1	3	8	3	0	2	1
9.1.2) New UPHC in government building	0	0	3	8	0	0	0	2
9.1.3) New UPHC in rented building	12	0	0	0	3	0	0	0
9.1.4) Upgradation / Renovation of existing facilities strengthened	11	0	0	11	8	0	0	8
9.1.5) No. of UPHCs functional with minimum staffing & service package				19				11

Handwritten signature

ULB	New Construction of U-PHC	Total Project Cost (Rs.)	Actual Fund Released from State(Considering refund) (Rs.)	Fund to be remain Post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto Sept, 19 since inception (in tune with FMR Sept, 19) (Rs.)	Scheme Balance against Fund Released (30.09.2019) (Rs.)	Physical progress up to September, 2019	Expected completion of
Asansol MC	12	90000000.00	74700000.00	15300000.00	30057360.00		100%	
Asansol MC							100%	
Asansol MC							100%	
Asansol MC							100%	
Asansol MC							100%	
Asansol MC							100%	
Asansol MC							100%	
Asansol MC							85%	Not submitted by MC
Asansol MC							55%	Not submitted by MC
Asansol MC							0%	Not submitted by MC
Asansol MC							100%	
Bidhannagar MC							5	37500000.00
Bidhannagar MC	25%	Rs. 17,47,642.00 has been booked for payment. Date of completion and operational will be 31.03.2020						
Bidhannagar MC	0%	Date of completion and operational will be 31.03.2020						
Bidhannagar MC	3	19500000.00	13247461.00	6252539.00	6805934.00		0%	Date of completion and operational will be 31.03.2020
Bidhannagar MC							100%	
Bidhannagar MC							100%	
Durgapur MC	3	19500000.00	13247461.00	6252539.00	6805934.00		70%	30-12-2019
Durgapur MC							100%	

UPHC wise break up of fund requirement for new construction of 5 MCs

Name of the MC	Sanctioned no. of new construction UPHC	Initial fund released	Physical progress as on date	Fund to be required in 2019-20	Expected date of completion
SMC	UPHC 1	10,00,000	70%	65,00,000.00	30.07.2019
Total		10,00,000		65,00,000.00	

Name of the MC	Sanctioned no. of new construction UPHC	Initial fund released	Physical progress as on date	Fund to be required in 2019-20	Expected date of completion
BMC	UPHC 1	32,50,000.00	85%	42,50,000.00	01.12.2019
	UPHC 2	-	25%	75,00,000.00	31.12.2019
	UPHC 4	60,00,000.00	100%	15,00,000.00	completed
Total		92,50,000.00		1,32,50,000.00	

Name of the MC	Sanctioned no. of new construction UPHC	Initial fund released	Physical progress as on date	Fund to be required in 2019-20	Expected date of completion
Durgapur MC	UPHC 1	36,14,913.00	100%	28,85,087.00	completed
	UPHC 2	15,90,427.00	70%	49,09,573.00	30.07.2019
	UPHC 3	10,47,199.00	25%	54,52,801.00	24.11.2019
Total		62,52,539.00		1,32,47,461.00	

Name of the MC	Sanctioned no. of new construction UPHC	Initial fund released	Physical progress as on date	Fund to be required in 2019-20	Expected date of completion
Howrah MC	UPHC 13	10,00,000.00	35%	65,00,000.00	31.10.2019
	UPHC 15	45,00,000.00	100%	30,00,000.00	Completed & functional
	UPHC 17	45,00,000.00	100%	30,00,000.00	Completed & functional
	UPHC 18	10,00,000.00	40%	65,00,000.00	31.10.2019
	UPHC 22	-	55%	75,00,000.00	30.09.2019
	UPHC 23	35,00,000.00	100%	40,00,000.00	Completed & functional
Total		1,45,00,000.00		3,05,00,000.00	

Name of the MC	Sanctioned no. of new construction UPHC	Initial fund released	Physical progress as on date	Fund to be required in 2019-20	Expected date of completion
Asansol MC	UPHC 1 - Ward No. 7	37,50,000.00	100%	28,00,000.00	Completed
	UPHC 2 - Ward No. 4	37,50,000.00	100%	14,00,000.00	Completed
	UPHC 3 - Ward No. 3	37,50,000.00	85%	55,00,000.00	09-01-2019
	UPHC 4 - Ward No. 93	37,50,000.00	85%	55,00,000.00	30/06/2019
	UPHC 5 - Ward No. 35	37,50,000.00	100%	28,00,000.00	Completed
	UPHC 7 - Ward No. 99	37,50,000.00	100%	17,00,000.00	Completed
	UPHC 8 - Ward No. 102	37,50,000.00	100%	17,00,000.00	Completed
	UPHC 9 - Ward No. 59	37,50,000.00	100%	17,00,000.00	Completed
	UPHC 10 - Ward No. 58	37,50,000.00	100%	17,00,000.00	Completed
	UPHC 11 - Ward No. 67	37,50,000.00	40%	32,00,000.00	31/01/2020
	UPHC 12 - Ward No. 105	37,50,000.00	100%	17,00,000.00	Completed
	Total		4,12,50000		2,97,00000

Grand total –

Rs. 9,31,97,471

Name of Municipal Corporation: Bidhanagar Municipal Corporation																						
Sl. No.	Name of Work	Whether Sanctioned for Renovation/Repair/Construction/Upgradation etc.	Year of sanction	Amount sanctioned (Rs. in Lakh)	Fund Allotted (Rs. in Lakh)	Expenditure for the month (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance as on 31.10.18 (Rs. in Lakh)	Total amount (Rs. in Lakh)	Percentage of completion (Till 31.10.18)	Tender process completed (Yes/No)	Whether work order placed (Yes/No)	Construction completed up to 10 %	Construction completed up to 25 %	Construction completed up to 40 %	Construction completed up to 55 %	Construction completed up to 70 %	Construction completed up to 85 %	Construction completed up to 100 %	Whether sanctioned for (Yes/No)	Remarks	
																						Description of Percentage for New Construction
Bidhanagar Corporation																						
1	Bidhanagar UPHC 1 Ward No. 28 podante Kuchumbhat UPHC	MC	2015-16	75	75	1.75	33.827	41.179	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	
2	Bidhanagar UPHC 2 Ward No. 36 Bidhanagar UPHC	MC	2015-16	75	10	17.48	17.48	57.52	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	The work stopped due to land dispute after some completion.
3	Bidhanagar UPHC 3 Ward No. 28 Mahabubpur UPHC	MC	2015-16	10	10	0	11.08	-1.08	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	
4	Bidhanagar UPHC 4 Ward No. 39 near DA block	MC	2015-16	75	75	4.38	70.54	4.46	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	
5	Bidhanagar UPHC 5 Ward No. 4 Rajarhat Gopalpur Babatola Narayanpur	R	2014-15	10	10	0	0	0	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	
6	Bidhanagar UPHC 5 Ward No. 12 Rajarhat Gopalpur Babatola Bahara	R	2014-15	10	10	0	11	-1	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	
7	Bidhanagar UPHC 7 Ward No. 19 Rajarhat Gopalpur Asoni Nagar Bagulhat	R	2014-15	10	10	0	10.1	-0.1	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	
8	Bidhanagar UPHC 8 Ward No. 26 Rajarhat Gopalpur Samar sarai Kestopur	R	2014-15	10	10	0	11.59	-1.59	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	
9	Bidhanagar UPHC 9 Ward No. 14 Rajarhat Gopalpur Saradamall Bahara	R	2014-15	10	10	0	11.1	-1.1	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	
10	Bidhanagar UPHC 10 Ward No. 21 Rajarhat Gopalpur Mohanraji Bahara	R	2014-15	10	10	0	5	5	0	0	Y	Y	Y	Y	Y	Y	Y	Y	Y	Y	no	
11	Bidhanagar UPHC 11 Ward No. 7 Rajarhat Gopalpur Mohanraji Bahara	MC	2014-15	75	0	0	0	0	0	0	no	no	no	no	no	no	no	no	no	no	no	
12	Bidhanagar UPHC 12 Ward No. 8 Rajarhat Gopalpur Bidhanagar	MC	2014-15	75	0	0	0	0	0	0	no	no	no	no	no	no	no	no	no	no	no	
Indicators for monitoring of Physical Progress																						
1	Construction completed up to 15 %	Funds work sanctioned and material procurement up to finish level																				
2	Construction completed up to 25 %	Foundation up to finish level																				
3	Construction completed up to 40 %	Structural work up to roof level																				
4	Construction completed up to 55 %	Structural work with bids work and plastering																				
5	Construction completed up to 70 %	Total building work																				
6	Construction completed up to 85 %	SfB and electrical work completed																				
7	Construction completed up to 100 %	Tid finishing and ready to handed over																				
Description of Percentage for New Construction																						
1. Foundation up to finish level 2. Foundation up to finish level 3. Structural work up to roof level 4. Structural work with bids work and plastering 5. Total building work 6. SfB and electrical work completed 7. Tid finishing and ready to handed over																						
Total expenditure Rs. 12,85,624/-																						
Note: not yet finished is having to a amount date at the end of the month 02.11.2018 Report @ Rs. 15,000/- per month at Vastak Sampah Jalpaiguri Street 07.08.2018																						

Asansol Municipal Corporation

FMR Code	Name of UEB	Name of U-PHC / U-CHC / MA with address and Ward No.	Whether Sanctioned for Renovation / New Construction / Upgrade on	Year of sanction	Amount sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to UEB (Rs. in Lakh)	Expenditure		Balance at		Total unspent (Rs. in Lakh)	Preparation of plan estimate (Yes/No)	Physical progress						Whether functional or not (Yes/No)						
								Expenditure for the month (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	URB level (Rs. in Lakh)	SUDA (Rs. in Lakh)			Plan estimate submitted to MED for vetting (No.)	Plan estimate Approved by DHS/CMS (No.)	Tender process completed (Yes/No)	Whether work order issued (Yes/No)	Construction completed up-to 10%	Construction completed up-to 25%		Construction completed up-to 40%	Construction completed up-to 55%	Construction completed up-to 70%	Construction completed up-to 85%	Construction completed up-to 100%	
1	2	HAU at Dharmapally, Ward No - 51	R	2013-14	10.00	5.00	5.00	0	6.78975	-1.78975	Unknown	-1.78975	NA	18	18	20	21	22	23	24	25	26	27	Yes		
		HAU at Dikar Nagar, Ward No. - 41	R	2013-14	10.00	5.00	5.00	0	6.88889	-1.88889	Unknown	-1.88889	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		HAU at Bakdanga, Ward No. - 31	H	2013-14	10.00	5.00	5.00	0	7.18714	-2.18714	Unknown	-2.18714	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		HAU at Dhadka near Water Tank, Ward No - 21	R	2013-14	10.00	5.00	5.00	0	6.8824	-1.8824	Unknown	-1.8824	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		HAU at Raharshahi near Bhaba Club, Ward No. - 23	R	2013-14	10.00	5.00	5.00	0	8.23024	-3.23024	Unknown	-3.23024	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		Dhadka Village, Ward No. - 13	R	2013-14	10.00	5.00	5.00	0	6.46038	-1.46038	Unknown	-1.46038	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		Mokshila Village, Ward No. - 87	R	2013-14	10.00	5.00	5.00	0	7.88181	-2.88181	Unknown	-2.88181	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		HAU at Alam Nagar, Ward No. - 82	R	2013-14	10.00	5.00	5.00	0	8.72051	-3.72051	Unknown	-3.72051	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		HAU at Nalbaghanti, Ward No. - 95	R	2013-14	10.00	5.00	5.00	0	6.74228	-1.74228	Unknown	-1.74228	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		HAU at Dhanbar Road, Near Chaman Kali Mandir, Ward No. - 95	R	2013-14	10.00	5.00	5.00	0	6.41158	-1.41158	Unknown	-1.41158	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		HAU at Kollinger, Ward No. - 82	R	2013-14	10.00	5.00	5.00	0	6.56885	-1.56885	Unknown	-1.56885	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		SSOPD Cum MH at O K Road, Ward No. - 25	U	2013-14	50.00	37.50	37.50	0	32.35778	5.14222	Unknown	5.14222	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		SSOPD Cum MB at Vivekananda Pali, Ward No. - 85	U	2013-14	50.00	37.50	37.50	0	30.10558	7.89442	Unknown	7.89442	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	Yes		
		Sanitary Field Office																								
		Underpass beside Balapur Road and opp Sitwick Garden, Ward No. - 87 (Plot No. - 46, J.L. No. - 30, Mouza - Balapur)	MC	2014-15	75.00	0	26.02754	0	26.02754	-20.02754	Unknown	-20.02754	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	100%	No	
		Jaraini Goo. Dye pass road opp Jaraini truck & Taxi stand, Ward No. - 4 (Plot No. - 198, J.L. No. - 21, Mouza - Jaraini)	MC	2014-15	75.00	0	18.00326	0	18.00326	-18.00326	Unknown	-18.00326	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	85%	No
		3rd Jarainpur Baglan, Jarainpur, Ward No. - 03 (Plot No. - 2151, 2149, J. No. - 10, Mouza - Jarainpur)	MC	2014-15	75.00	0	0	0	0	0	Unknown	0	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	50%	No
		Sanitary Field Office																								
		Levanti Pass within BS Pipe No. 227 Mouza - Egara at ward no-93	MC	2014-15	75.00	0	0	0	0	0	Unknown	0	YES	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	Yes	85%	No
		Jarain Design. Plot No. - 47 & - 49, Mouza - Baktar Nagar, Ward No. - 35	MC	2014-15	75.00	0	0.26607	0	26.82240	-46.17443	Unknown	-46.17443	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
		Sisla Bagra Aree	MC	2014-15	75.00	0	0	0	0	0	Unknown	0	No	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA

S. No.		Indicators for monitoring of physical		Description of Percentage (for New Construction only)		Status		Remarks		Financials		Compliance		
S. No.		Indicators for monitoring of physical		Description of Percentage (for New Construction only)		Status		Remarks		Financials		Compliance		
4.3.2	1	Construction completed up-to 10 %	10%	Earth work, excavation and material procurement up to Plinth level	NA	NA	NA	NA	NA	NA	NA	NA	100%	NA
4.3.2	2	Construction completed up-to 25 %	25%	Structural work up to first level	NA	NA	NA	NA	NA	NA	NA	NA	100%	NA
4.3.2	3	Construction completed up-to 40 %	40%	Structural work up to roof level	NA	NA	NA	NA	NA	NA	NA	NA	100%	NA
4.3.2	4	Construction completed up-to 55 %	55%	Total finishing work	NA	NA	NA	NA	NA	NA	NA	NA	100%	NA
4.3.2	5	Construction completed up-to 70 %	70%	Water and electrical work completed	NA	NA	NA	NA	NA	NA	NA	NA	100%	NA
4.3.2	6	Construction completed up-to 85 %	85%	SAP and electrical work completed	NA	NA	NA	NA	NA	NA	NA	NA	100%	NA
4.3.2	7	Construction completed up-to 100 %	100%	Full finishing and ready to handed over	NA	NA	NA	NA	NA	NA	NA	NA	100%	NA

** Mention "R" for Renovation, "NC" for New Construction and "UP" for Upgradation in Column No. 4

Qualifiers for reporting of physical progress noted below:

S. No.	Indicators for monitoring of physical	Description of Percentage (for New Construction only)	Status	Remarks	Financials	Compliance
1	Construction completed up-to 10 %	Earth work, excavation and material procurement up to Plinth level	NA	NA	NA	NA
2	Construction completed up-to 25 %	Structural work up to first level	NA	NA	NA	NA
3	Construction completed up-to 40 %	Structural work up to roof level	NA	NA	NA	NA
4	Construction completed up-to 55 %	Total finishing work	NA	NA	NA	NA
5	Construction completed up-to 70 %	Water and electrical work completed	NA	NA	NA	NA
6	Construction completed up-to 85 %	SAP and electrical work completed	NA	NA	NA	NA
7	Construction completed up-to 100 %	Full finishing and ready to handed over	NA	NA	NA	NA

Durgpur Municipal Corporation

S. No.	Indicators for monitoring of physical	Description of Percentage (for New Construction only)	Status	Remarks	Financials	Compliance
4.3.2	1	Construction completed up-to 10 %	10%	Earth work, excavation and material procurement up to Plinth level	NA	NA
4.3.2	2	Construction completed up-to 25 %	25%	Structural work up to first level	NA	NA
4.3.2	3	Construction completed up-to 40 %	40%	Structural work up to roof level	NA	NA
4.3.2	4	Construction completed up-to 55 %	55%	Total finishing work	NA	NA
4.3.2	5	Construction completed up-to 70 %	70%	Water and electrical work completed	NA	NA
4.3.2	6	Construction completed up-to 85 %	85%	SAP and electrical work completed	NA	NA
4.3.2	7	Construction completed up-to 100 %	100%	Full finishing and ready to handed over	NA	NA

Asansol Municipal Corporation

Name of Municipal Corporation: Asansol District: Paschim Bardhaman		Report completed for: May 2019 By: A.M.C.		Report completed for: May 2019 By: A.M.C.		Reporting for the month March- 2019																					
S.No	FMR Code	Name of U-PHC / U-CHC / MH with address and Ward No.	Whether Renovation / New Constructed on / Upgraded on	Year of sanction	Amount sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Expenditure			Balance at		Total unspent (Rs. in Lakh)	Preparation of plan estimate (Yes/No)	Plan estimate submitted to MED for vetting (No.)	Plan estimate vetted by MED (No.)	Plan estimate approved by OHS/MS (No.)	Tender process completed (Yes/No)	Whether work order issued (Yes/No)	Physical progress							Whether functional or not (Yes/No)
								Expenditure for the month (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	ULB level (Rs. in Lakh)	SUDA (Rs. in Lakh)	10								11	12	13	14	15	16	17	
1	3	HAI at Dharmapally, Ward No - 31	R	2013-14	6.00	5.00	5.00	0	6.7975	-1.7975	Unknown	-1.7975	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		HAI at Dshier Nagar, Ward No - 41	R	2013-14	10.00	5.00	5.00	0	6.6999	-1.6999	Unknown	-1.6999	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		HAI at Daldanga, Ward No - 11	R	2013-14	10.00	5.00	5.00	0	7.5974	-2.5974	Unknown	-2.5974	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		HAI at Thakur near Water Tank, Ward No - 21	R	2013-14	10.00	5.00	5.00	0	6.8924	-1.8924	Unknown	-1.8924	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		HAI at Bahadur near Rice-Club, Ward No - 33	R	2013-14	10.00	5.00	5.00	0	8.13024	-3.13024	Unknown	-3.13024	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		Dhanku Village, Ward No - 15	R	2013-14	10.00	5.00	5.00	0	6.4809	-1.4809	Unknown	-1.4809	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		Mokshila Village, Ward No - 87	R	2013-14	10.00	5.00	5.00	0	7.9681	-2.9681	Unknown	-2.9681	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		HAI at Adam Nagar, Ward No - 82	R	2013-14	10.00	5.00	5.00	0	8.72051	-3.72051	Unknown	-3.72051	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		HAI at Indraprastha, Ward No - 95	R	2013-14	10.00	5.00	5.00	0	6.7952	-1.7952	Unknown	-1.7952	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		HAI at Badshahpur Road, Near Chinnamra, Kailash, Ward No - 35	R	2013-14	10.00	5.00	5.00	0	6.4158	-1.4158	Unknown	-1.4158	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		HAI at Kailash, Ward No - 25	R	2013-14	10.00	5.00	5.00	0	6.5985	-1.5985	Unknown	-1.5985	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		ESOPD Cum MH at O.R. Road, Ward No - 25	U	2013-14	50.00	37.50	37.50	0	50.30778	3.4222	Unknown	3.4222	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		ESOPD Cum MH at Vishwananda Park, Ward No - 85	U	2013-14	50.00	37.50	37.50	0	50.10555	7.3944	Unknown	7.3944	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		Balapur, Janda Balapur Road and G.P. Sample, Ward No.47 (P/O no.46, JI. No.36, Khera Balapur)	NC	2014-15	75.00	0	0	20.8734	20.8734	-20.8734	Unknown	-20.8734	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		Jamuna Goo Bye pass road opp. Jansari DUK & Text Zone, Ward No-4 (P/O No. 198, JI. No-21, Maza- Jamuna)	NC	2014-15	75.00	0	0	19.0135	19.0135	-19.0135	Unknown	-19.0135	Yes	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		Shyambpur Bagan, Panchapur, Ward No-01 (P/O No-215,214B, A. No-22)Maza-Paripurul	NC	2014-15	75.00	0	0	0	0	0	Unknown	0	Yes	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		Tennis Park within 65 Plot No. 277 Maza- Jagan at ward no-53	NC	2014-15	75.00	0	0	0	0	0	Unknown	0	YES	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		Mani Danga, Plot No-47 & 49, Maza- Babar Nagar, Ward No- 35	NC	2014-15	75.00	0	0	0.28007	26.6256	-46.1746	Unknown	-46.1746	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes
		Situa Bagan Area	NC	2014-15	75.00	0	0	0	0	0	Unknown	0	NA	15	16	17	18	19	20	21	22	23	24	25	26	27	Yes

4.3.1.1	4.3.1.2	4.3.1.3	4.3.1.4	4.3.1.5	4.3.1.6	4.3.1.7	4.3.1.8	4.3.1.9	4.3.1.10	4.3.1.11	4.3.1.12	4.3.1.13	4.3.1.14	4.3.1.15	4.3.1.16	4.3.1.17	4.3.1.18	4.3.1.19	4.3.1.20	4.3.1.21	4.3.1.22	4.3.1.23	4.3.1.24	4.3.1.25	4.3.1.26	4.3.1.27	4.3.1.28	4.3.1.29	4.3.1.30	4.3.1.31	4.3.1.32	4.3.1.33	4.3.1.34	4.3.1.35	4.3.1.36	4.3.1.37	4.3.1.38	4.3.1.39	4.3.1.40	4.3.1.41	4.3.1.42	4.3.1.43	4.3.1.44	4.3.1.45	4.3.1.46	4.3.1.47	4.3.1.48	4.3.1.49	4.3.1.50	4.3.1.51	4.3.1.52	4.3.1.53	4.3.1.54	4.3.1.55	4.3.1.56	4.3.1.57	4.3.1.58	4.3.1.59	4.3.1.60	4.3.1.61	4.3.1.62	4.3.1.63	4.3.1.64	4.3.1.65	4.3.1.66	4.3.1.67	4.3.1.68	4.3.1.69	4.3.1.70	4.3.1.71	4.3.1.72	4.3.1.73	4.3.1.74	4.3.1.75	4.3.1.76	4.3.1.77	4.3.1.78	4.3.1.79	4.3.1.80	4.3.1.81	4.3.1.82	4.3.1.83	4.3.1.84	4.3.1.85	4.3.1.86	4.3.1.87	4.3.1.88	4.3.1.89	4.3.1.90	4.3.1.91	4.3.1.92	4.3.1.93	4.3.1.94	4.3.1.95	4.3.1.96	4.3.1.97	4.3.1.98	4.3.1.99	4.3.1.100
4.3.1.1	4.3.1.2	4.3.1.3	4.3.1.4	4.3.1.5	4.3.1.6	4.3.1.7	4.3.1.8	4.3.1.9	4.3.1.10	4.3.1.11	4.3.1.12	4.3.1.13	4.3.1.14	4.3.1.15	4.3.1.16	4.3.1.17	4.3.1.18	4.3.1.19	4.3.1.20	4.3.1.21	4.3.1.22	4.3.1.23	4.3.1.24	4.3.1.25	4.3.1.26	4.3.1.27	4.3.1.28	4.3.1.29	4.3.1.30	4.3.1.31	4.3.1.32	4.3.1.33	4.3.1.34	4.3.1.35	4.3.1.36	4.3.1.37	4.3.1.38	4.3.1.39	4.3.1.40	4.3.1.41	4.3.1.42	4.3.1.43	4.3.1.44	4.3.1.45	4.3.1.46	4.3.1.47	4.3.1.48	4.3.1.49	4.3.1.50	4.3.1.51	4.3.1.52	4.3.1.53	4.3.1.54	4.3.1.55	4.3.1.56	4.3.1.57	4.3.1.58	4.3.1.59	4.3.1.60	4.3.1.61	4.3.1.62	4.3.1.63	4.3.1.64	4.3.1.65	4.3.1.66	4.3.1.67	4.3.1.68	4.3.1.69	4.3.1.70	4.3.1.71	4.3.1.72	4.3.1.73	4.3.1.74	4.3.1.75	4.3.1.76	4.3.1.77	4.3.1.78	4.3.1.79	4.3.1.80	4.3.1.81	4.3.1.82	4.3.1.83	4.3.1.84	4.3.1.85	4.3.1.86	4.3.1.87	4.3.1.88	4.3.1.89	4.3.1.90	4.3.1.91	4.3.1.92	4.3.1.93	4.3.1.94	4.3.1.95	4.3.1.96	4.3.1.97	4.3.1.98	4.3.1.99	4.3.1.100

** Attention: "Y" for Renovation, "N" for New Construction and "U" for Upgrade in Column No. 4
 * Statistics for reporting of physical progress method below:

Sl. No.	Indicators for monitoring of	Description of Percentage (By New Construction only)
1	Construction completed up-to 10	50% work execution and material procurement up to 70% (from work)
2	Construction completed up-to 25	Structural work up to 40% and
3	Construction completed up-to 50	Structural work up to 70% and
4	Construction completed up-to 75	Structural work up to 90% and
5	Construction completed up-to 90	Final finishing work
6	Construction completed up-to 95	50% and electrical work completed
7	Construction completed up-to 100	Full finishing and ready to handover

Name of the MC	Sanctioned no. of new construction UPHC	Initial fund released	Fund released in 2019-20	Total fund released	Fund to be released
BMC	UPHC1	32,50,000.00	42,50,000.00	75,00,000.00	0
	UPHC2	0	75,00,000.00	75,00,000.00	0
	UPHC4	60,00,000.00	15,00,000.00	75,00,000.00	

**SUDA**

রাজ্য নগর উন্নয়ন সংস্থা

STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ
“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নংSUDA-Health/NUHM/421/15/ 6865

তারিখ01.10.2019.....

MEMORANDUM

Funds are hereby released electronically in favour of your ULB as per details enclosed herewith for implementation of National Urban Health Mission (NUHM).

The expenditure shall be incurred as per the annexed activities abiding by the standard norms of NUHM. Statement of Expenditure (SOE) and Utilization Certificate (UC) may please be sent monthly & quarterly respectively.

Yours faithfully,

Encl. : As stated.

Finance Officer, SUDA

SUDA-Health/NUHM/421/15/6865/1(8)

Dt. .. 01.10.2019

CC

1. The Mayor, Bidhannagar / Howrah / Siliguri Municipal Corporation
2. The Commissioner, Bidhannagar / Howrah / Siliguri Municipal Corporation
3. The Nodal Officer, NUHM, Bidhannagar / Howrah / Siliguri Municipal Corporation
4. The Chief Public Health Officer, SUDA

Finance Officer, SUDA

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408

Release of fund under NUHM
vide Memo No. SUDA-Health/NUHM/421/15/

dt. 01.10.2019

ULB	FMR Code	Budget Head	A/C No. & Bank	Fund Released (Amount in Rs.)
Bidhannagar	P.4.3.2	Building of	A/C No. 424910210000011, Bank of India	1,32,50,000
Howrah		New	A/C No. 27750100008404, Bank of Baroda	3,05,00,000
Siliguri		UPHC- NUHM	A/C No. 429110110007693, Bank of India	65,00,000



Finance Officer, SUDA

**SUDA**

রাজ্য নগর উন্নয়ন সংস্থা

STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নং SUDA-Health/NUHM/421/15/6655

তারিখ 25..... 24.09.2019

From : Director, SUDA

To : The Branch Head,
Axis Bank Limited,
Chetla Branch,
29/6C, Chetla Central Road,
Chetla, Ward No.82,
Kolkata - 700 027.

**Sub.: Electronic Transfer of Fund from our A/C No.918010003016076
under National Urban Health Mission (NUHM)**

Sir,

You are requested to kindly arrange for electronically transfer of the amounts as per details given in Page-02 debiting the amount from this office Account No.918010003016076 lying with your branch in respect of National Urban Health Mission (NUHM).

(Petrus Anuranjan Soreng)
Finance Officer
SUDA

(Debarati Datta Gupta)
Director
SUDA


দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০


Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com


Account Section : 2358 6408

Sl. No.	Name of the ULBs	Amount (in Rs.)	Name of the Bank	Branch Name	Account Number	IFS Code
1	Bidhannagar MC	1,32,50,000.00	Bank of India	Salt Lake	424910210000011	BKID0004249
2	Siliguri MC	65,00,000.00	Bank of India	Sevoke Road, Siliguri	429110110007693	BKID0004291
3	Howrah MC	3,05,00,000.00	Bank of Baroda	M.G. Road, Howrah	27750100008404	BARB0HOWECX
Total		5,02,50,000.00				

(Rupees Five Crore Two Lakh Fifty Thousand only)


(Petrus Anuranjan Soreng)
Finance Officer
SUDA


(Debarati Datta Gupta)
Director
SUDA


24-09-19

Name of District: HOWRAH

Monthly reporting format for Monitoring of construction works under MCHM

Reporting for the month: Aug 19

Sl. No.	Name of U-PHC / U-CHC / MH with address and Ward No.	Whether Sanctioned for Renovation / New Construction / Upgradation	Year of sanction	Amount sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Expenditure (Rs. in Lakh)			Balance at			Total Unspent (Rs. in Lakh)	Prepared on of plan estimate (Yes/No)	Plan estimate submitted to MED for vetting (No.)	Plan estimate vetted by MED (No.)	Plan estimate approved by DISTFW S (No.)	Tender process completed (Yes / No)	Physical progress							Whether functional or not (Yes / No)	Remarks											
							Expenditure for the month (Rs. in Lakhs)	Cumulative Expenditure (Rs. in Lakh)	ULB level (Rs. in Lakh)	DRI&F WS (Rs. in Lakh)	Prepared on of plan estimate (Yes/No)	Plan estimate submitted to MED for vetting (No.)							Plan estimate vetted by MED (No.)	Plan estimate approved by DISTFW S (No.)	Tender process completed (Yes / No)	Whether work order issued (Yes/No)	Construction completed up-to 10 %	Construction completed up-to 25 %	Construction completed up-to 40 %			Construction completed up-to 55 %	Construction completed up-to 70 %	Construction completed up-to 85 %	Construction completed up-to 100 %							
1	MUNICIPAL CORPORATION																																					
	Hemra U-CHC 14 Ward No. 2 & Kolar Road	MC	2015-16	15	0	0	0	0	0	0	15																											
	Hemra U-CHC 15 Ward No. 10 Bhabani Lane	MC	2015-16	75	29	54	0.51	27.51		22.16	0	22.16																										
	Hemra U-CHC 16 Ward No. 41 Padmalaya	MC	2015-16	75																																		
	Hemra U-CHC 17 Ward No. 10 SBM Nadi Bari	MC	2015-16	75	75	75	0.23	87.65		81.94	0	32.96																										
	Hemra U-CHC 18 Ward No. 20 Durgam Lal	MC	2015-16	75																																		
	Hemra U-CHC 19 Ward No. 23 Bidan	MC	2015-16	75																																		
	Hemra U-CHC 20 Ward No. 26 Anandaram	MC	2015-16	75																																		
	Hemra U-CHC 21 Ward No. 27 Santal Ward	MC	2015-16	75																																		
	Hemra U-CHC 22 Ward No. 56 Bidan Bari	MC	2014-15	75																																		
	Hemra U-CHC 23 Ward No. 61 Sibi-GT Bar Manza	MC	2014-15	75	59	59	0.48	28.59		48.35																												
	Hemra U-CHC 24 Ward No. 47 Damra Gora	MC	2015-16	75																																		
	Hemra U-CHC 25 Ward No. 7 B Barid	MC	2015-16	75																																		
	Hemra U-CHC 26 Ward No. 44 Bagpara	MC	2015-16	75																																		
	Hemra U-CHC 27 Ward No. 23 Chinsara	MC	2015-16	75																																		
				290	295			213.99		160.245		50.74																										

** Multiple 'X' for Renovation, 'Y' for New Construction, 'N' for reporting of

1	Construction					
2	Renovation					
3	Construction					
4	Renovation					
5	Construction					
6	Renovation					
7	Construction					
8	Renovation					
9	Construction					
10	Renovation					

Description of Percentage for New Construction work

1	Foundation work up to 20% level	
2	Plinth work up to 20% level	
3	Work up to 20% level	
4	Roof work up to 20% level	
5	Roof work up to 20% level	
6	Roof work up to 20% level	
7	Roof work up to 20% level	
8	Roof work up to 20% level	
9	Roof work up to 20% level	
10	Roof work up to 20% level	

Lipab Ranj
Sub-Asst. Engineer,
Howrah Municipal Corporation

BMC.

SUDA	U.B	No. of New Construction of U.PHC	Total Project Cost (Rs.)	Actual Fund Released from State considering retent (Rs.)	Amount to be remain Total Project Cost (Rs.)	Cumulative Expenditure upto March, 19 since inception (in case with PM Mar 19) (Rs.)	Scheme Balance against Fund Released (1.03.19) (Rs.)	Physical Progress as on Mar - 19 (%)	Fund to be required in 2019-20 (Rs.)	Date of completion as per work order (DD-MM-YYYY)	Expected date of completion & operational (DD-MM-YYYY)	Remarks
SUDA, West Bengal	Asansol MC	12	90000000.00	45000000.00	45000000.00	3541296.00	9587404.00	100-0%	35000000.00	05.02.2019 05.02.2019 05.02.2019	10.03.2019 10.08.2019 30.08.2019	
	Durgapur MC	3	15000000.00	0.00	15000000.00	628587.00	4731350.00	100-100%	11500000.00	13.07.2019 15.07.2019 14.03.2020	23.08.2019 15.11.2019 14.03.2020	
	Bidhanagar MC	5	37100000.00	9250000.00	28250000.00	9821710.00	573710.00	UPHC 4 - 100% UPHC 1 - 85% UPHC 2 - 25% UPHC 11 - 0% UPHC 12 - 0%	28250000.00	01.08.2019 11.11.2019 31.12.19 31.12.19 31.12.19	UPHC 4 - 08.04.19 UPHC 1 - 1.12.19 UPHC 2 - 31.12.19 UPHC 11 - 31.12.19 UPHC 12 - 31.12.19	UPHC 4 - 15.00.000 UPHC 1 - 4.25.000 UPHC 2 - 7.00.000 UPHC 11 - 7.50.000 UPHC 12 - 7.50.000
	Chandernagore MC	1	6500000.00	0.00	6500000.00	380569.00	286569.00	100%		31.07.2017	NA (already Operational)	
	Siliguri MC	1	6500000.00	0.00	6500000.00	0.00	0.00	70%		18th October, 2018	22nd June, 2019	
TOTAL			251500000.00	64250000.00	187250000.00	54795587.00	9954415.00					

Handwritten signature
19/09/19

Handwritten signature
19/9/19

Chief Health Officer
Bidhanagar Municipal Corporation
Bidhanagar, Kolkata

Assistant Engineer
Bidhanagar
Municipal Corporation

The completion of work delayed
due to non-availability of
freighted material in that period

SUDA	ULB	No. of New Construction of U-PHC	Total Project Cost (Rs.)	Actual Fund Released from State considering refund (Rs.)	Fund to be remain Post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against Fund Released (31.03.19) (Rs.)	Physical Progress as on Mar - 19 (%)	Fund to be required in 2019-20 (Rs.)	Date of completion as per work order (DD-MM-YYYY)	Expected date of completion & operational (DD-MM-YYYY)	Remarks
SUDA, West Bengal	Siliguri MC	1	65000000.00	0.00	65000000.00	0.00	0.00	70%	65000000.00	18th October, 2018	30th June, 2019	The completion of work delayed due to non availability of riverbed material in that period (more than 75% work has been done)
TOTAL			65000000.00	0.00	65000000.00	0.00	0.00		65000000.00			

Health Officer
Siliguri Municipal Corporation

Finance Officer
Siliguri Municipal Corporation

Commissioner
Siliguri Municipal Corporation



Sunanda Basu <sunandabasu101@gmail.com>

Signed copy of physical progress of UPHCS with FMR

1 message

Sunanda Basu <sunandabasu101@gmail.com>

Fri, Sep 6, 2019 at 2:49 PM

To: NUHM AMC <nuhm.amc@gmail.com>, Health HMC <health.hmc@gmail.com>, NUHM DMC

<nuhm.dmc@gmail.com>, bidhannagarnuhm@gmail.com, smc.health.slg@gmail.com

Cc: debaratidattagupta@gmail.com, Malay Patra <dr.malay2014@gmail.com>, "State Program Management Unit(NUHM)" <spmu.nuhm@gmail.com>

Dear All,

You are requested to send a copy of construction format with FMR (Aug 2019) duly signed by the concerned engineering authority of your Corporation/MED/District NUHM Cell involved with the construction process of new UPHCS. This is required by the higher authority for release of fund for renovation/new construction of UPHC. **This may be treated as most urgent.**

You are also requested to send the FMR in new format (scanned signed copy and soft copy in excel format) within **9th Sept. 2019** positively.

--

Dr. Sunanda Basu,
PHO, SUDA



GOVERNMENT OF WEST BENGAL
Health & Family Welfare Department
National Health Mission

Swasthya Sathi, Swasthya Bhawan Premises
GN-29, 4th Floor, Sector - V

Salt-Lake, Bidhannagar, Kolkata - 7000091

(033) 2333 0123 (Phone); (033) 2357 7930 (Fax)

Email: amdnhmwb.sg@gmail.com

Web: www.wbhealth.gov.in



Memo No. HFW-27038/58/2018-NHM SEC-Dept. of H&FW/2736

Date: 13/08/2019

ORDER

Administrative Approval and Financial Sanction (AA&FS) is hereby accorded for an amount of Rs. 9,31,97,461.00 (Rupees Nine Crore Thirty One Lakh Ninety Seven Thousand Four Hundred Sixty one) only in favour of State urban Development Agency, (SUDA), West Bengal for construction of U-PHCs in five (05) Municipal Corporations out of NUHM fund under budget head of **Building of new UPHC-NUHM of Tally Code P.04.03.02.**

2. Accordingly, Rs. 9,31,97,461.00 (Rupees Nine Crore Thirty One Lakh Ninety Seven Thousand Four Hundred Sixty one) only is hereby released in favour of State urban Development Agency, (SUDA), West Bengal for the said purpose as per breakup of allocation given below.


Sl No.	MC	No. of New Construction of U-PHC	Total Project Cost (Rs.)	Actual Fund Released in earlier occasion from State considering refund (Rs.)	Fund to be released (Rs.)
1	Bidhannagar MC	5	37500000.00	9250000.00	13250000.00
2	Durgapur MC	3	19500000.00	0.00	13247461.00
3	Howrah MC	15	99500000.00	10500000.00	30500000.00
4	Siliguri MC	1	6500000.00	0.00	6500000.00
5	Asnasoil MC	12	90000000.00	45000000.00	29700000.00
TOTAL		36	253000000.00	64750000.00	93197461.00

3. Sr. Accounts Officer, NHM will act as Drawing & Disbursing Officer for the purpose.

4. The expenditure will be incurred under budget head of **Building of new UPHC-NUHM** as per norms and to be booked under Tally Code P.04.03.02.


5. This order has been issued with the approval of Mission Director, NHM & Secretary, Health & Family Welfare Department, Government of West Bengal.

6. All concerned are being informed.


Additional Mission Director, NHM
Govt. of West Bengal

Copy forwarded for information and necessary action to-

1. **Director, State Urban Development Agency, West Bengal**
2. **Director, State FMG, NHM, Health & Family Welfare Department, Swasthya Bhawan**
3. **Sr. Accounts Officer, NHM, Health & Family Welfare Department, Swasthya Bhawan with the request to release Rs. 9,31,97,461.00 (Rupees Nine Crore Thirty One Lakh Ninety Seven Thousand Four Hundred Sixty one) only in favour of State urban Development Agency, (SUDA), West Bengal**
4. **Municipal Commissioner (Howrah MC / Asnasol MC / Bidhannagar MC / Durgapur MC / Siliguri MC)**
5. **IT Cell, Swasthya Bhawan for web-posting**


**Additional Mission Director, NHM
Govt. of West Bengal**



o/c



রাজ্য নগর উন্নয়ন সংস্থা

STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-Health/NUHM/421/15/4808

18.07.2019

২৩

ক্রমিক নং

তারিখ

From: Director
To: Additional Mission Director, (NHM)
Department of Health & Family Welfare
Government of West Bengal
Swasthya Bhavan, Kolkata

Sub: **Submission of requisition of fund under the heading “Construction of UPHCs”
under NUHM during the FY 2019-20**

Sir,

In response to the letter received from your office memo no. FW-27038/58/2018-NHM SEC-Dept. of H&FW/2451 dated 17.07.2019 in respect of requisition of fund received from 5 MCs under construction of UPHCs under NUHM for the FY 2019-20 and after receiving the status of the physical progress from all these 5 MCs a fund requisition statement is being prepared as per the format sent from your end, copy of which is placed as enclosure for ready reference.

Sl. No.	Name of MC	Amount (Rs.)
1	Asansol MC	Rs. 2,97,00,000
2	Bidhannagar MC	Rs. 1,32,50,000
3	Durgapur MC	Rs. 1,32,47,461
4	Howrah MC	Rs. 3,05,00,000
5	Siliguri MC	Rs. 65,00,000
Grand Total		Rs. 9,31,97,461

I, therefore request you to allot Rs. 9,31,97,461 under NUHM so that it may be sub allotted to all 5 MCs as mentioned above.

Contents not verified
Received on: *S. Samaddar*
National Health Mission *20/07/19*
Health and Family Welfare Department
Government of West Bengal

Yours faithfully,

Sdf 18/7/19
Director, SUDA

Encl: As stated

SUDA-Health/NUHM/421/15/4808(2)

Date: 18.07.2019

২৩

Copy forwarded for kind information to:

1. Dr. Tapan Saha, State Nodal Officer, NHM
2. The Sr. PA to the Pr. Secretary, UD&MA Department, Govt. of West Bengal

Sdf 18/7/19
Director, SUDA

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408



Director, SUDA <wbsudadir@gmail.com>

Submission of requisition of fund under Construction of UPHCs.

1 message

Director, SUDA <wbsudadir@gmail.com>

Tue, Jul 23, 2019 at 12:32 PM


To: spmu.nuhm@gmail.com, amdnhmwbhealth@gmail.com, Urban Development & Municipal Affairs Department <secy.ma-wb@gov.in>

Cc: sunandabasu101@gmail.com

Sir,

Please find the attached document.

For**Debarati Datta Gupta, WBCS (EXE.)****Director SUDA W.B**

 **Requisition of fund under UPHCs..pdf**
1194K



রাজ্য নগর উন্নয়ন সংস্থা

STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ
“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-Health/NUHM/421/15/1808

18.07.2019

২৩

ক্রমিক নং

তারিখ

From: Director
To : Additional Mission Director, (NHM)
Department of Health & Family Welfare
Government of West Bengal
Swasthya Bhavan, Kolkata

Sub: **Submission of requisition of fund under the heading “Construction of UPHCs”
under NUHM during the FY 2019-20**

Sir,

In response to the letter received from your office memo no. FW-27038/58/2018-NHM SEC-Dept. of H&FW/2451 dated 17.07.2019 in respect of requisition of fund received from 5 MCs under construction of UPHCs under NUHM for the FY 2019-20 and after receiving the status of the physical progress from all these 5 MCs a fund requisition statement is being prepared as per the format sent from your end, copy of which is placed as enclosure for ready reference.

Sl. No.	Name of MC	Amount (Rs.)
1	Asansol MC	Rs. 2,97,00,000
2	Bidhannagar MC	Rs. 1,32,50,000
3	Durgapur MC	Rs. 1,32,47,461
4	Howrah MC	Rs. 3,05,00,000
5	Siliguri MC	Rs. 65,00,000
Grand Total		Rs. 9,31,97,461

I, therefore request you to allot Rs. 9,31,97,461 under NUHM so that it may be sub allotted to all 5 MCs as mentioned above.

Yours faithfully,

[Signature] 18/7/19

Director, SUDA

Encl: As stated

SUDA-Health/NUHM/421/15/1808(2)

Date: 18.07.2019

২৩

Copy forwarded for kind information to:

1. Dr. Tapan Saha, State Nodal Officer, NHM
2. The Sr. PA to the Pr. Secretary, UD&MA Department, Govt. of West Bengal

[Signature] 18/7/19
Director, SUDA

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408

Format for requisition of fund for construction of New U-PHC building under NUHM

MC	No. of new construction of U-PHC	Total project cost (Rs.)	Actual fund released from State considering refund (Rs.)	Fund to be remain post released against total project cost (Rs.)	Cumulative expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against fund released (31.03.19) (Rs.)	Physical progress as on Mar -19 (%)	Requisition of fund received from MCs FY 2019-20 (Rs.)	Expected date of completion and operational (DD-MM-YYYY)
HMC	15	9,95,00,000.00	1,05,00,000.00	8,90,00,000.00	61,74,291.00	43,25,709.00	UPHC13 - 35% UPHC15 - 100% UPHC17 - 100% UPHC18 - 40% UPHC22 - 55% UPHC23 - 100%	3,05,00,000.00	31.10.2019 Completed Completed 31.10.2019 30.09.2019 Completed

Dr. /s/ 15

Format for requisition of fund for construction of New U-PHC building under NUHM

MC	No. of new construction of U-PHC	Total project cost (Rs.)	Actual fund released from State considering refund (Rs.)	Fund to be remain post released against total project cost (Rs.)	Cumulative expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against fund released (31.03.19) (Rs.)	Physical progress as on Mar -19 (%)	Requisition of fund received from MGS FY 2019-20 (Rs.)	Expected date of completion and operational (DD-MM-YYYY)
AMC	12	9,00,00,000.00	4,50,00,000.00	4,50,00,000.00	3,54,12,596.00	95,87,404.00	UPHC1 - 100% UPHC2 - 100% UPHC3 - 85% UPHC4 - 85% UPHC5 - 100% UPHC7 - 100% UPHC8 - 100% UPHC9 - 100% UPHC10 - 100% UPHC11 - 40% UPHC12 - 100%	2,97,00,000.00	Completed Completed Completed Completed Completed Completed Completed Completed Completed Completed 31.01.2020 Completed

Pl
15/9/19

Format for requisition of fund for construction of New U-PHC building under NUHM

MC	No. of new construction of U-PHC	Total project cost (Rs.)	Actual fund released from State considering refund (Rs.)	Fund to be remain post released against total project cost (Rs.)	Cumulative expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against fund released (31.03.19) (Rs.)	Physical progress as on Mar -19 (%)	Requisition of fund received from MCs FY 2019-20 (Rs.)	Expected date of completion and operational (DD-MM-YYYY)
BMC	5	3,75,00,000.00	92,50,000.00	2,82,50,000.00	98,23,730.00	(-),5,73,730.00	UPHC4 - 100% UPHC1 - 85% UPHC2 - 25%	1,32,50,000.00	Completed 01.12.2019 31.12.2019

Ok
6/12/19

Format for requisition of fund for construction of New U-PHC building under NUHM

MC	No. of new construction of U-PHC	Total project cost (Rs.)	Actual fund released from State considering refund (Rs.)	Fund to be remain post released against total project cost (Rs.)	Cumulative expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against fund released (31.03.19) (Rs.)	Physical progress as on Mar -19 (%)	Requisition of fund received from MCs FY 2019-20 (Rs.)	Expected date of completion and operational (DD-MM-YYYY)
									Completed
DMC	3	1,95,00,000.00	0.00	1,95,00,000.00	62,52,539.00	62,52,540.00	UPHC1 - 100% UPHC2 - 70% UPHC3 - 25%	1,32,47,461.00	30.07.2019
									Completed
									24.11.2019

Shr
6/10/19

Format for requisition of fund for construction of New U-PHC building under NUHM

MC	No. of new construction of U-PHC	Total project cost (Rs.)	Actual fund released from State considering refund (Rs.)	Fund to be remain post released against total project cost (Rs.)	Cumulative expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against fund released (31.03.19) (Rs.)	Physical progress as on Mar -19 (%)	Requisition of fund received from MCs FY 2019-20 (Rs.)	Expected date of completion and operational (DD-MM-YYYY)
SMC	1	65,00,000.00	0.00	65,00,000.00	0.00	0.00	UPHCI - 70%	65,00,000.00	30.07.2019

Shri
6/7/18



GOVERNMENT OF WEST BENGAL
Health & Family Welfare Department
National Health Mission

Swasthya Sathi, Swasthya Bhawan Premises
GN-29, 7th Floor, Sector - V

Salt-Lake, Bidhannagar, Kolkata - 7000091
(033) 2333 0123 (Phone); (033) 2357 7930(Fax)

Email: amdnhmwbhealth@gmail.com; Web: www.wbhealth.gov.in



Memo No. FW-27038/58/2018-NHM SEC-Dept. of H&FW/2451

Date: 17.07.2019

From : Additional Mission Director, NHM &
Joint Secretary to the Government of West Bengal
Health & Family Welfare Department

To : Director,
State Urban Development Agency (SUDA), West Bengal

Sub : Fund requisition for construction of U-PHCs under NUHM for 5 MCs

Madam,

As per letter vide this office Memo No. HFW-27038/17/2019-NHM SEC-Dept. of H&FW/1611, dated: 10/05/2019, a reconciliation workshop was held at Swastha Bhawan on 14th May, 2019 to work out the fund requirement for construction of U-PHCs for 6 Municipal Corporations (Howrah, Bidhannagar, Durgapur, Asansol and Siliguri). In this meeting SPMU officials, representatives of SUDA and Municipal Corporation were present. Individual scheme (construction) was analysed as regards to physical progress and financial expenditure. The information gathered was put into a format and was shared with SUDA through e-mail with a request to send the final fund requisition to State for construction. The requisition, however, in the prescribed format has not been received by the State. May I therefore request your good office to send the fund requisition in the prescribed format, attached herewith for construction under NUHM for Municipal Corporations. Your early action will be highly solicited.

Encl: as stated above


Additional Mission Director, NHM

Memo No. FW-27038/58/2018-NHM SEC-Dept. of H&FW/2451/1(2)

Date: 17.07.2019

Copy forwarded for information and necessary action to:

1. **Municipal Commissioner** (Howrah MC, Asansol MC, Durgapur MC, Siliguri MC and Bidhannagar MC).
2. **IT Cell**, Swasthya Bhawan for Web-posting.


Additional Mission Director, NHM

**FORMAT FOR REQUISITION OF FUND FOR CONSTRUCTION OF NEW U-PHC BUILDING
UNDER NUHM**

MC	No. of New Construction of U-PHC	Total Project Cost (Rs.)	Actual Fund Released from State considering refund (Rs.)	Fund to be remain Post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against Released Fund (31.03.19) (Rs.)	Physical Progress as on Mar - 19 (%)	Requisition of Fund Received from MCs FY 2019-20 (Rs.)	Expected date of completion & operation (DD-MM-YYYY)
Bidhannagar MC	5	37500000.00	9250000.00	28250000.00	9823730.00	-573730.00	UPHC 4 - 100% UPHC 1 - 85% UPHC 2 - 25% UPHC 1 - 0% UPHC 12 - 0%		
Durgapur MC	3	19500000.00	0.00	19500000.00	6252539.00	6252539.00	1 no. - 100% 1 no. - 70% 1 no. - 25%		

**FORMAT FOR REQUISITION OF FUND FOR CONSTRUCTION OF NEW U-PHC BUILDING
UNDER NUHM**

MC	No. of New Construct ion of U-PHC	Total Project Cost (Rs.)	Actual Fund Released from State considering refund (Rs.)	Fund to be remain Post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against Fund Released (31.03.19) (Rs.)	Physical Progress as on Mar - 19 (%)	Requisition of Fund Received from MCs FY 2019-20 (Rs.)	Expected date of completion & operational (DD-MM-YYYY)
Howrah MC	15	99500000.00	10500000.00	89000000.00	6174291.00	4325709.00	2 nos. - 100% 1 no. - 35% 2 nos. - 25% 1 no. - 5%" 1 No. 100% 8 No-0%		
Siliguri MC	1	6500000.00	0.00	6500000.00	0.00	0.00	70%		

**● FORMAT FOR REQUISITION OF FUND FOR CONSTRUCTION OF NEW U-PHC BUILDING
UNDER NUHM**

MC	No. of New Construction of U-PHC	Total Project Cost (Rs.)	Actual Fund Released from State considering refund (Rs.)	Fund to be remain Post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against Released Fund (31.03.19) (Rs.)	Physical Progress as on Mar - 19 (%)	Requisition of Fund Received from MCs FY 2019-20 (Rs.)	Expected date of completion & operation at (DD-MM-YYYY)
Asnasol MC	12	900000000.00	450000000.00	450000000.00	35412596.00	9587404.00	5 nos. - 100% 1 no. - 25% 1 no. - 100% 1 no. - 85% 1 no. - 0% 1 no. - 100% 1 no. - 85% 1 no. - 0%		
TOTAL	36	2530000000.00	647500000.00	1882500000.00	57663156.00	7086844.00			



Debjit Chakraborty <cphosuda@gmail.com>

Requisition - Construction of UPHCs

1 message

Dr. Debjit Chakraborty <cphosuda@gmail.com>

Thu, Jun 20, 2019 at 1:35 PM

To: "State Program Management Unit (NUHM)" <spm.u.nuhm@gmail.com>

Please see the attached file.



Requisition - Construction of UPHCs.jpeg
187K

9830143206.

Mail sent to spmu on Jun 20th 2019. ~~app~~ as directed by Director SPMU.
DL
20/6/19

রাজ্য নগর উন্নয়ন সংস্থা

STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-Health/NUHM/421/15

18.06.2019

ক্রমিক নং

তারিখ

From: Director
To: Additional Mission Director, (NHM)
Government of West Bengal
Department of Health & Family Welfare
Swasthya Bhavan, Kolkata

Sub: Submission of requisition of fund under the heading “Construction of UPHCs”
under NUHM during the FY 2019-20

Sir,

In response to the letter received through email on 04.06.2019 in respect of requisition of fund, received from 5 MCs under construction of UPHCs under NUHM for the FY 2019-20, and after observing the physical progress of construction status of UPHCs in these 5 MCs, a statement showing total fund required is placed below. We have confirmed the status of the physical progress from all these 5 MCs copy of which is placed herewith for ready reference.

Sl. No.	Name of MC	Amount (Rs.)
1	Asansol MC	Rs. 2,97,00,000
2	Bidhannagar MC	Rs. 1,32,50,000
3	Durgapur MC	Rs. 1,32,47,461
4	Howrah MC	Rs. 3,05,00,000
5	Siliguri MC	Rs. 65,00,000
Grand Total		Rs. 9,31,97,461

I, therefore request you to allot Rs. 9,31,97,461 under NUHM so that it may be sub allotted to all 5 MCs as mentioned above.

Yours faithfully,

Encl: As stated

Director, SUDA

SUDA-Health/NUHM/421/15/ /1(2)

Date: 18.06.2019

Copy forwarded for kind information to:

1. Dr. Tapan Saha, State Nodal Officer, NHM
2. The Sr. PA to the Pr. Secretary, UD&MA Department, Govt. of West Bengal

Director, SUDA

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadr@gmail.com

Account Section : 2358 6408



রাজ্য নগর উন্নয়ন সংস্থা

SUDA

STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-Health/NUHM/421/15

18.06.2019

ক্রমিক নং

তারিখ

From: Director
To : Additional Mission Director, (NHM)
Government of West Bengal
Department of Health & Family Welfare
Swasthya Bhavan, Kolkata

Sub: **Submission of requisition of fund under the heading “Construction of UPHCs”
under NUHM during the FY 2019-20**

Sir,

In response to the letter received through email on 04.06.2019 in respect of requisition of fund, received from 5 MCs under construction of UPHCs under NUHM for the FY 2019-20, and after observing the physical progress of construction status of UPHCs in these 5 MCs, a statement showing total fund required is placed below. We have confirmed the status of the physical progress from all these 5 MCs copy of which is placed herewith for ready reference.

Sl. No.	Name of MC	Amount (Rs.)
1	Asansol MC	Rs. 2,97,00,000
2	Bidhannagar MC	Rs. 1,32,50,000
3	Durgapur MC	Rs. 1,32,47,461
4	Howrah MC	Rs. 3,05,00,000
5	Siliguri MC	Rs. 65,00,000
Grand Total		Rs. 9,31,97,461

I, therefore request you to allot Rs. 9,31,97,461 under NUHM so that it may be sub allotted to all 5 MCs as mentioned above.

Yours faithfully,

Encl: As stated

Director, SUDA

SUDA-Health/NUHM/421/15/ /1(2)

Date: 18.06.2019

Copy forwarded for kind information to:

1. Dr. Tapan Saha, State Nodal Officer, NHM
2. The Sr. PA to the Pr. Secretary, UD&MA Department, Govt. of West Bengal

Director, SUDA

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408



Debjit Chakraborty <cphosuda@gmail.com>

Requisition - Construction of UPHCs

1 message

Dr. Debjit Chakraborty <cphosuda@gmail.com>

Thu, Jun 20, 2019 at 1:35 PM

To: "State Program Management Unit(NUHM)" <spm.u.nuhm@gmail.com>

Please see the attached file.



Requisition - Construction of UPHCs.jpeg
187K

*Mail sent to spmu on Jun 20/19
2019. ~~app~~ as directed by
Director SPMU.
DR.
20/6/19.*

SUDA, West Bengal		SUDA
Asansol MC		ULB
12		No. of New Construction of U-PHC
90000000.00		Total Project Cost (Rs.)
45000000.00		Actual Fund Released from State considering refund (Rs.)
45000000.00		Fund to be remain Post released against Total Project Cost (Rs.)
35412596.00		Cumulative Expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)
9587404.00		Scheme Balance against Fund Released (31.03.19) (Rs.)
5 nos. - 100% 1 no. - 25% 1 no. - 100% 1 no. - 85% 1 no. - 0% 1 no. - 100% 1 no. - 85% 1 no. - 0%		Physical Progress as on Mar - 19 (%)
45000000.00		Fund to be required in 2019-20 (Rs.)
<p>17/12/16 Jamuria Bye Pass- 17/12/16 Jamuria Balanpur - 17/12/16 Jamuria Partharpur - 17/12/16 RaniGANI Tawarpara - 27/02/19 RaniGANI Jhantidanga - 01/05/19 RaniGANI Sishubagan - Vetting Complt Kulti Kumardha- 26/05/16 Kulti Dhemomaln- 05/05/16 Kulti Sodepur- 26/05/16 Bidyanandapur- 26/05/16 Kulti Dishergarh- 04/07/16 Kulti Barakar- 13/10/18</p>		Date of completion as per work order (DD-MM-YYYY)
<p>22/06/19 Jamuria Bye Pass- 14/01/19 Jamuria Balanpur- 14/01/19 Jamuria Partharpur- 01/09/19 RaniGANI Tawarpara- 30/06/19 RaniGANI Jhantidanga- 02/05/19 RaniGANI Sishubagan- Vetting Complt Kulti Kumardha- 02/04/17 Kulti Dhemomaln- 15/01/19 Kulti Sodepur- 14/01/19 Bidyanandapur- 29/02/16 Kulti Dishergarh- 17/01/19 Kulti Barakar- 31/01/20</p>		Expected date of completion & operational (DD-MM-YYYY)

Asansol Municipal Corporation

Health Officer

30.5.19.

SUDA	ULB	No. of New Construction of U-PHC	Total Project Cost (Rs.)	Actual Fund Released from State considering refund (Rs.)	Fund to be remain Post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against Fund Released (31.03.19) (Rs.)	Physical Progress as on Mar-19 (%)	Fund to be required in 2019-20 (Rs.)	Date of completion as per work order (DD-MM-YYYY)	Expected date of completion & operational (DD-MM-YYYY)	Remarks
SUDA West Bengal	Howrah MC	15	99500000.00	10500000.00	89000000.00	6174291.00	4325709.00	2 nos - 100% 1 no - 35% 2 nos - 25% 1 no - 5% 1 no - 100%	90000000.00	01.02.2019 05.02.2019 05.02.2019 05.07.2019	30.08.2019 30.08.2019 30.08.2019 30.08.2019	
	Asansol MC	12	90000000.00	45000000.00	450000000.00	35412596.00	9587404.00	5 nos - 100% 1 no - 25% 1 no - 100% 1 no - 85% 1 no - 0% 1 no - 100% 1 no - 85% 1 no - 0%	58500000.00		23.01.2019 15.11.2019 24.03.2020	UPHC 4 - 1500000 UPHC 1 - 4250000 UPHC 2 - 4500000 UPHC 3 - 7500000 UPHC 5 - 5500000 UPHC 12 - 7500000
	Durgpur MC	3	19500000.00	0.00	19500000.00	6257519.00	-6252539.00	1 no - 100% 1 no - 70% 1 no - 25%	19500000.00	13.07.2019 15.07.2019 14.11.2020		
	Bidhannagar MC	5	37500000.00	9250000.00	28250000.00	9823730.00	-573730.00	UPHC 4 - 100% UPHC 1 - 85% UPHC 2 - 25% UPHC 11 - 0% UPHC 12 - 0%	20250000.00			
	Chanderpragore MC	1	6500000.00	0.00	6500000.00	-2867169.00	2867169.00	100%		31.07.2017	NA (Already Operational)	
Siliguri MC	1	6500000.00	0.00	6500000.00	0.00	0.00	70%		18th October, 2018	30th June, 2019	The completion of work delayed due to non availability of reserved material in that period	
TOTAL			250500000.00	64750000.00	185750000.00	31795897.00	-954413.00					

K. V. Kumar Ashwin
 Chief Health Officer 17/5/2019
 Bidhannagar Municipal Corporation
 Bidhannagar, Kolkata

SUDA	ULB	No. of New Construction of U-PHC	Total Project Cost (Rs.)	Actual Fund Released from State considering refund (Rs.)	Fund to be remain Post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against Fund Released (31.03.19) (Rs.)	Physical Progress as on Mar - 19 (%)	Fund to be required in 2019-20 (Rs.)	Date of completion as per work order (DD-MM-YYYY)	Expected date of completion & operational (DD-MM-YYYY)	Remarks
SUDA, West Bengal	Durgapur MC	3	195000000.00	0.00	195000000.00	6252539.00	-6252539.00	1 no. - 100% 1 no. - 70% 1 no. - 25%	195000000.00	30.06.2017 24.02.2019 12.08.2019	08.11.2018 30.07.2019 24.11.2019	1. fully operational at present 2. as on report till date physical progress is 85% (S & P work finished, electrical work going on) 3. As on till date physical progress is 40%. Roof work will be done by this week
TOTAL			195000000.00	0.00	195000000.00	6252539.00	-6252539.00					

File
15/5/2019
Asst. Manager
(Nurse, DMC)

Durgapur Urban Health Societ

Secretary 15.05.19

SUDA	MLR	No. of New Construction of U-PHC	Total Project Cost (Rs.)	Actual Fund Released from State considering refund (Rs.)	Fund to be retained Post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto March, 19 since inception (to date with FMD Mar 19) (Rs.)	Scheme Release against Fund Released (11.03.19) (Rs.)	Physical Progress as on Mar-19 (%)	Fund to be required in 2019 (Rs.)	Date of completion as per work order (DD-MM-YYYY)	Expected date of completion & operational (DD-MM-YYYY)	Remarks
SUDA, West Bengal	✓ Howrah MC	15	9000000.00	1000000.00	7900000.00	8174291.00	4126200.00	100% - 100% 100% - 25% 100% - 25% 100% - 50% 100% - 50% 100% - 0%	1900000.00	05.02.2019 05.02.2019 05.02.2019 05.02.2019 05.02.2019 05.02.2019	05.02.2019	Howrah UPHC 21 Ward No. 35 (Scheme No. 1) Fund Year- 2009-2019 Howrah UPHC 11 Ward No. 4 (Scheme No. 2) Fund Year- 2010-2019 Howrah UPHC 17 Ward No. 38 (Scheme No. 3) Fund Year- 2010-2019 Howrah UPHC 18 Ward No. 39 (Scheme No. 4) Fund Year- 2010-2019 Howrah UPHC 19 Ward No. 40 (Scheme No. 5) Fund Year- 2010-2019 Howrah UPHC 20 Ward No. 41 (Scheme No. 6) Fund Year- 2010-2019
	Asansol MC	12	9000000.00	4500000.00	4500000.00	3541356.00	9007400.00	100% - 100% 100% - 25% 100% - 30% 100% - 30% 100% - 50% 100% - 50% 100% - 0%	4500000.00			
	Durgam MC	1	1500000.00	0.00	1500000.00	6022570.00	4232530.00	100% - 100% 100% - 70% 100% - 20%	1500000.00	11.07.2015 15.07.2019 14.11.2020	21.09.2019 13.11.2019 24.01.2020	
	Balsamagar MC	5	3750000.00	4250000.00	3325000.00		873700.00	100% - 100% 100% - 0% 100% - 20% 100% - 0%	3000000.00	20.12.2019	15.03.2020	
	Chandernagar MC	1	500000.00	0.00	500000.00	2967569.00	2867569.00	100%		31.03.2017	NA (Already Operational)	
	Sikpat MC	1	600000.00	0.00	600000.00	0.00	0.00	70%	1117000.00	10th October, 2020	30th June, 2019	The completion of work delayed due to non availability of required material in that period.
	TOTAL			23750000.00	2975000.00	19775000.00	44771017.00	7354412.00				

Sangata Mukhopadhyay
20/05/19

NODAL OFFICER (NUHM)
HOWRAH MUNICIPAL CORPORATION

890,00,000/-

SUDA	ULB	No. of New Construction of U-PHC	Total Project Cost (Rs.)	Actual Fund Released from State considering refund (Rs.)	Fund to be remain post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto March, 19 since inception (in tune with FMR Mar 19) (Rs.)	Scheme Balance against Fund Released (31.03.19) (Rs.)	Physical Progress as on Mar - 19 (%)	Fund to be required in 2019-20 (Rs.)	Date of completion as per work order (DD-MM-YYYY)	Expected date of completion & operational (DD-MM-YYYY)	Remarks
SUDA, West Bengal	Siliguri MC	1	6500000.00	0.00	6500000.00	0.00	0.00	79%	6500000.00	18th October, 2018	30th, June, 2019	The completion of work delayed due to non availability of riverbed material in that period (more than 75% work has been done)
TOTAL:			6500000.00	0.00	6500000.00	0.00	0.00		6500000.00			

Health Officer
Siliguri Municipal Corporation



Finance Officer
Siliguri Municipal Corporation



Commissioner
Siliguri Municipal Corporation



6/7/2019

Requisition of Fund for Construction of U-PHCs from different Municipal Corporation - sunandabasu101@gmail.com - Gmail

Health MC

to ashutoshkundu.1986, Swagata spmu.nuhm, SUDA, me

2:02 PM

Madam,

In respect to your email, the fund requisition forwarded from our end has been verified & found to be correct. For your kind information & perusal.

6/7/2019

Requisition of Fund for Construction of U-PHCs from different Municipal Corporation - sunandabasu101@gmail.com - Gmail

Debarati Datta Gupta, WBCS (EXE)

Director SUDA W.B

----- Forwarded message -----

From: **Bidhannagar nuhm** <bidhannaganuhtm@gmail.com>

Date: Fri, Jun 7, 2019 at 12:13 PM

Subject: Re: Requisition of Fund for Construction of U-PHCs from different Municipal Corporation

To: Director, SUDA <wbsudadir@gmail.com>

Madam,

Thank you for forwarding the mail we are confirming the construction status report of the UPHCs and the fund asked for the purpose.

Thanking You,
Yours faithfully,

Dr. Kusum Kumar Adhikary,
Chief Health Officer,
Bidhannagar Municipal Corporation

Fr

Debarati Datta Gupta, WBCS (EXE.)

Director SUDA W.B

----- Forwarded message -----

From: **NUHM AMC** <nuhm.amc@gmail.com>

Date: Thu, Jun 6, 2019 at 3:48 PM

Subject: Re: Requisition of Fund for Construction of U-PHCs from different Municipal Corporation

To: Director, SUDA <wbsudadir@gmail.com>

Checked and Verified, the fund may please be disbursed for onward process of Construction.

Health Officer
Asansol Municipal Corporation



Sunanda Basu <sunandabasu101@gmail.com>

Fwd:

1 message

Director, SUDA <wbsudadir@gmail.com>
To: sunandabasu101@gmail.com

Thu, Jun 6, 2019 at 2:00 PM

For**Debarati Datta Gupta, WBCS (EXE.)****Director SUDA W.B**

----- Forwarded message -----

From: Siliguri Municipal Corporation <smc.health.slg@gmail.com>

Date: Thu, Jun 6, 2019 at 1:42 PM

Subject:

To: Director, SUDA <wbsudadir@gmail.com>

Sir, Madam

The Contraction work of UPHC-10 in SMC area work has been verified and the contraction work is around 70% completed as reported.

With regards
Dr. S Majumder
Nodal Officer
NUHM, SMC

SIDA	TUE	No. of New Construction of DPHC	Total Project Cost (Rs.)	Actual Fund Released from State consolidation fund (Rs.)	Fund to be remain Post released against Total Project Cost (Rs.)	Cumulative Expenditure of scheme upto March, 19 since inception (in tune with PSR Star 19) (Rs.)	Scheme Balance against Fund Released (31.03.19) (Rs.)	Physical Progress as on Mar - 19 (%)	Fund to be required in 2019-20 (Rs.)	Date of completion as per work order (DD-MM-YYYY)	Expected date of completion & operational (DD-MM-YYYY)	Remarks
SIDA, West Bengal	Durgapur MC	1	19500000.00	0.00	19500000.00	6252539.00	-6252539.00	1 no. - 100% 1 no. - 70% 1 no. - 20%	19500000.00	30.06.2017 24.02.2019 12.08.2019	08.11.2018 30.07.2019 24.11.2019	1 fully operational at present 2. as on report till date physical progress is 85% (S & P work finished, electrical work going on) As on till date % Road work will be done by this week
TOTAL			19500000.00	0.00	19500000.00	6252539.00	-6252539.00					

Shri
2/6/19

Secretary
07.06.19
Durgapur Urban Health Societ



Director, SUDA <wbsudadir@gmail.com>

Requisition of Fund for Construction of U-PHCs from different Municipal Corporation

2 messages

State Program Management Unit(NUHM) <spmnuhm@gmail.com>

Tue, Jun 4, 2019 at 11:48 AM

To: Sunanda Basu <sunandabasu101@gmail.com>

Cc: "Director, SUDA" <wbsudadir@gmail.com>, chowdhurydipankar_in@rediffmail.com, SNO NUHM <drtapankumar@gmail.com>, Chayan Kr Saha <me.chayansaha@gmail.com>

Madam,

Please go through the attached file and find herewith the signed copy of requisitions in respect of funds for construction of U-PHCs under NUHM shared by the different Municipal Corporations. A complied excel-sheet is also enclosed with this email for your ready reference.

In this regard, you are requested to please verify the said requisition and send final requisition from SUDA, WB under signature of Competent Authority. Otherwise it will be difficult for us to initiate the proposal for releasing the fund for construction of U-PHCs for MCs from this end.

Your cooperation is solicited

Regards

Pratap Majumder
State Urban Health Planning Manager, NUHM
State Programme Management Unit (SPMU)
National Urban Health Mission
Department of Health & Family Welfare
Govt. of West Bengal
Swasthya Bhawan, Kolkata-91
Ph. No. 033 - 2333-0432
Email ID : spmu.nuhm@gmail.com
Website : www.wbhealth.gov.in/NUHM

--
Thanks & Regards,

State Programme Management Unit (SPMU)
National Urban Health Mission
Department of Health & Family Welfare
Govt. of West Bengal
Swasthya Bhawan, Kolkata-91

Ph. No. 033 - 2333-0432

Email ID : spmu.nuhm@gmail.com

Website : www.wbhealth.gov.in/NUHM

6 attachments

HMC.jpg
1441K **AMC revised.pdf**
213K **Bidhannagar MC.pdf**
885K **Requisition of Fund for MCs.xlsx**
19K **DMC.pdf**
226K **Siliguri MC.pdf**
249K**Director, SUDA** <wbsudadir@gmail.com>

Thu, Jun 6, 2019 at 12:56 PM

To: bidhannagarnuhm@gmail.com, Health Hmc <health.hmc@gmail.com>, smc.health.slg@gmail.com,
nuhm.amc@gmail.com, nuhm.dmc@gmail.com

Cc: Debarati Datta Gupta <debaratidattagupta@gmail.com>, spmu.nuhm@gmail.com, sunandabasu101@gmail.com


Sir,
Enclosed herewith the signed copies of requisitions in respect of funds for construction of UPHCs under NUHM shared by your Municipal Corporation with SPMU NUHM Dept of Health & Family Welfare, W.B. based on monthly report. You are requested kindly to verify the said requisition and give your confirmation via e-mail to the undersigned on or before **7th June 2019 noon**, for initiating the process of fund disbursement from our end.

Thanks & Regards,

Debarati Datta Gupta, WBCS (EXE.)**Director SUDA W.B**

5 attachments

HMC.jpg
1441K



[Handwritten signature]
MUNICIPAL CORPORATION

 **AMC revised.pdf**
213K

 **Bidhannagar MC.pdf**
885K

 **DMC.pdf**
226K

 **Siliguri MC.pdf**
249K

There is a recruitment committee for all the districts for recruitment of various categories of staffs under NHM at district and facility level, formed vide this Department's order No. HFW/NRHM-34/2014/660, dated 18.02.2014. There is also a committee for recruitment of ASHA in each district, formed vide this Department's Memo no. HFW/NRHM/20//2006/(Pt.II)/1631, dated June 27, 2012, Memo no. HFW/NRHM/20/06/Pt.II/1844 dated 24 July, 2012, Memo no. HFW/NRHM-20/06/(Pt.III)/250, dated, 27.01.2014 and Memo no. HFW/NRHM-20/06/(Pt.III)/735, dated, 20.02.2014. These district level committees will recruit HR for the Municipal Corporations as well as Municipalities. **(All these memos are enclosed).**

While recruiting HR under NUHM for the City Programme Management Unit, Urban Primary Health Centre and ASHA at Community level, these district level recruitment committee will include the Mayor/Chairman or their representative from the concerned Municipal Corporation/Municipality as member of the said committee.

All category of recruitment for the Kolkata Municipal Corporation will be done by the KMC.

Yours faithfully,

Sanghamitra Ghosh

(Sanghamitra Ghosh)

Enclosed: As stated.

Memo No. H/SFWB/28R-02-2012/4806/1(14)

Date: 21/08/2014

Copy forwarded for kind information and necessary action to:

1. The Director of Health Services & e.o. Secretary, Govt. of West Bengal
2. The Director of Medical Education & e.o. Secretary, Govt. of West Bengal
3. The Addl. Mission Director NHM and Jt. Secretary to Govt. of west Bengal
4. The Addl Director of Health Services (Admn), West Bengal
5. The Addl Director of Health Services (TB), West Bengal
6. The Jt. Director of Health Services and SFWO, West Bengal
7. The Jt. Director of Health Services (PH & CD), West Bengal
8. The Jt. Director Of Health Service and CHO, KMUHO, Kolkata
9. The Jt. Director Of Health Service (P & D), west Bengal
10. The P. O. NHM, West Bengal
11. The Director Financial Management Group (FMG), NHM
12. The Senior Accounts Officer (Sr. A. O.), NHM
13. PS to Principal Secretary, Department of Health & Family Welfare, WB
14. Office copy

Sanghamitra Ghosh
(Sanghamitra Ghosh)

Contd.....P/4

Summary Statement of Fund release for construction of New U-PHC building (EMR Code P. 04.03.02)

Sl. No.	SUDA	ULB	Year of approval of the scheme	No. of U-PHC sanctioned	Unit Cost per U-PHC	Total Project Cost (Rs.)	Fund released from State (Rs.)	Fund refund to State (Rs.)	Actual Fund released considering the refund	Fund to be remained post release	Proposed fund to be released
A	B	C	D	E	F	G = E x F	H	I	J = H-I	K=G-(J+L)	L
1	SUDA	Asansol MC	2013-14	12	7500000.00	90000000.00	31500000.00	0.00	31500000.00	28500000.00	30000000.00
2	SUDA	Bidhannagar MC	2014-15	5	7500000.00	37500000.00	7500000.00	7000000.00	5000000.00	26500000.00	10500000.00
3	SUDA	Chandernagore MC	2013-14	1	7500000.00	7500000.00	1000000.00	0.00	1000000.00	0.00	6500000.00
4	SUDA	Durgapur MC	2013-14	3	7500000.00	22500000.00	3000000.00	7000000.00	-4000000.00	22500000.00	4000000.00
5	SUDA	Howrah MC	2013-14	14	7500000.00	105000000.00	16500000.00	7250000.00	9250000.00	70500000.00	25250000.00
6	SUDA	Siliguri MC	2013-14	1	7500000.00	7500000.00	1000000.00	0.00	1000000.00	6500000.00	0.00
Total						270000000.00	60500000.00	21250000.00	39250000.00	154500000.00	76250000.00

Dipankar Choudhury
DIPANKAR CHOWDHURY
 Finance Officer
 SUDA - Health

Devi Kishor
Finance Officer
 State Urban Development Agency
 Govt of West Bengal

Summary Statement of Fund release for construction of New U-PHC building (EMR Code P. 04.03.02)

Sl. No.	SUDA	ULB	Year of approval of the scheme	No. of U-PHC sanctioned	Unit Cost per U-PHC	Total Project Cost (Rs.)	Fund released from State (Rs.)	Fund refund to State (Rs.)	Actual Fund released considering the refund	Fund to be remained post release	Proposed fund to be released
A	B	C	D	E	F	G = E x F	H	I	J = H-I	K=G-(J+L)	L
1	SUDA	Asansol MC	2013-14	12	7,500,000	90,000,000	31,500,000	-	31,500,000	28,500,000	30,000,000
2	SUDA	Bidhannagar MC	2014-15	5	7,500,000	37,500,000	11,250,000	7,000,000	4,250,000	22,750,000	10,500,000
3	SUDA	Chandernagore MC	2013-14	1	7,500,000	7,500,000	1,000,000	-	1,000,000	-	6,500,000
4	SUDA	Durgapur MC	2013-14	3	7,500,000	22,500,000	3,000,000	7,000,000	(4,000,000)	22,500,000	4,000,000
5	SUDA	Howrah MC	2013-14	14	7,500,000	105,000,000	16,500,000	7,250,000	9,250,000	70,500,000	25,250,000
6	SUDA	Siliguri MC	2013-14	1	7,500,000	7,500,000	1,000,000	-	1,000,000	6,500,000	-
Total						270,000,000	64,250,000	21,250,000	43,000,000	150,750,000	76,250,000

sent by somv on-24.8.18

N.C.-5
75.00

R-21
0.60

H
R-25
N.C.-2

R N.C.
12-19

14-15

Bidharyung. R 10.00

N.C. 67.50

Rajonka R 60.00
N.C. 45.00

15-16

0 = 10.00

90.00 = 157.50

0 = 60.00
60.00 = 105.00

Fund released by Samiti to BMC dt. 16.7.2015

BMC

Rcvd - 10.00

N.C - 37.50

To SUDA

60.00 = 70.00

75.00 = 112.50

New Construction

(Amount in Rs.)

ULBs	Fund Received from DHFW	Fund released to ULBs	Refund to DHFW	SOE submitted					Total
				2018-19 (Upto June, 18)	2017-18	2016-17	2015-16	2014-15	
Asansol MC	31,500,000	18,000,000	-	3,051,997	14,269,436	-	-	-	17,321,433
Bidhannagar MC	7,500,000	13,000,000	7,000,000	-	6,616,039	-	-	-	6,616,039
Chandernagore MC	-	7,500,000	-	210,267	2,334,924	1,779,263	-	-	4,324,454
Durgapur MC	-	14,700,000	7,000,000	1,327,324	908,255	646,508	-	-	2,882,087
Howrah MC	4,500,000	17,500,000	7,250,000	-	9,113,913	-	-	-	9,113,913
Siliguri MC	-	-	-	-	-	-	-	-	-
Total =>	43,500,000	70,700,000	2,250,000 #####	4,589,588	33,242,567	2,425,771	-	-	40,257,926

Renovation

(Amount in Rs.)

ULBs	Fund Received from DHFW	Fund released to ULBs	Refund to DHFW	SOE submitted					Total
				2018-19 (Upto June, 18)	2017-18	2016-17	2015-16	2014-15	
Asansol MC	11,000,000	11,000,000	-	-	6,421,285	3,762,665	5,500,000	-	15,683,950
Bidhannagar MC	6,000,000	6,000,000	-	-	6,047,046	-	-	-	6,047,046
Chandernagore MC	3,000,000	2,000,000	-	2,955	681,247	383,884	904,626	-	1,972,712
Durgapur MC	11,000,000	8,000,000	1,600,000	53,570	2,566,310	3,358,848	12,150	-	5,990,878
Howrah MC	25,000,000	11,000,000	500,000	-	2,946,832	4,086,656	3,457,206	-	10,490,694
Siliguri MC	10,000,000	10,000,000	146,016	587,622	126,477	977,507	8,000,000	-	9,691,606
Total =>	66,000,000	48,000,000	2,246,016	644,147	18,789,197	12,569,560	17,873,982	-	49,876,886



ole
রাজ্য নগর উন্নয়ন সংস্থা



STATE URBAN DEVELOPMENT AGENCY

"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ
"ILGUS BHAVAN", H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নং SUDA-272/2007(Pt-IV)/

তারিখ 23.06.2017

From: Director, SUDA

To: The Chief Engineer
Municipal Engineering Directorate
Government of West Bengal

Sub: Forwarding the Minutes of the 75th Meeting of Technical Committee under SUDA held on 15.06.2017 in the Conference Hall of Nagarayan, Block-DF-8 Sector- I, Salt Lake Kolkata-700 064

Sir,

Enclosed please find a copy of the Minutes of the 75th Meeting of Technical Committee under SUDA held on 15.06.2017 in the Conference Hall of Nagarayan, Block-DF-8 Sector- I, Salt Lake Kolkata-700 064 for information and further necessary action.

Encl: Copy of the Minutes of the 75th Meeting
of the Technical Committee

Yours faithfully,

sd/
Director

23.06.2017

SUDA-272/2007(Pt-IV)/ 375/1(2)

Copy forwarded for information to:

1. Sri B.N. Kar, Additional Mission Director, Mission Nirmal Bangla
2. Sri Ashoke Kumar Das II, Addl. Mission Director, WBSULM



Director

Name of the ULB	Capacity of Shelter	Approved Component cost (civil cost)	Estimated amount put to Tender	No. of Bidders	Lowest quoted rate	Remarks
Uttarpara Kotrang Municipality	50 bedded	Rs. 12752045.60 + Rest amount for CLC (Borne by ULB)	Rs. 1,83,82,423.00	Four	Rs. 1,53,80,573.32	1st call & Lowest quoted rate 16.33 % below amount put to tender

In above case 4 bidders participated and as such the Committee recommended for acceptance of the offered rate by ULB for Construction of 50 bedded building for Shelter for Urban Homeless.

Item No 9: Acceptance of lowest rates for the works of 'Construction of new PHC Building in ward no. 06 within Kalyani Municipality under NUHM'.

Ref: i) e-NIeT No. WBMAD/ULB/KM/NIT-1(e)/Dev/2017-18 Sl.-2 dated 15.02.17

ii) CE MEDs No. ME/505/1P-46/2015 pt.-I dated 01.06.2017.

The Committee was informed that proposed work is Construction of new Primary Health Centre Building in ward no. 06 within Kalyani Municipality under NUHM.

The Committee noted that this is the 1st call of Tender and three participants offered their rates.

Rate for the said Tender has been obtained as 'Percentage rate basis'. Other details are shown in table below:

Short Name of work	NIT No. & Date	No. of Bidder	Lowest Bidder	Lowest offered rate	Amount put to tender	%age above/ below	Remarks
Construction of new Primary Health Centre Building in ward no. 06 within Kalyani Municipality under NUHM	WBMAD/ULB/KM/NIT-1(e)/Dev/2017-18 Sl.-2 Dated 15.02.17	3	Baidya Construction	Rs. 55,77,249.43	Rs. 55,78,365.10 (based on PWD, SoR Vol-I & Vol-II w.e.f 01.12.15)	0.02% below the amount put to tender	CE, MED, recommended for acceptance

The Committee was informed that approved project cost for building a new UPHC is 75.00 Lakh. Present scope of work includes building work with sanitary and plumbing. Other items like electrification, furniture, equipment etc. are the balance work and to be taken up at later stage.

Decision: After discussions on the issue based on the points mentioned above, the Committee recommended for acceptance of the offer of Baidya Construction by the ULB.

Table Agenda 1: Acceptance of lowest rates for the works of 'Geo-technical Investigation, Planning, Designing, Construction & Commissioning of 25 MT/Day solid waste processing set up by installing a Biogas Plant constructed by 5 units @ 5 MT/unit capacity steel fabricated Biogas Plant including O & M for one year within Jalpaiguri Municipality under SBM program'.

Ref:i) e-NIeB No. WBMAD/JAL/SWM/e-NIQ-1(3rd call)/2016-17,dated 27.03.2017

The committee was informed that solid Waste Management Scheme for Jalpaiguri Municipal Town was sanctioned by 1st Meeting of High Powered Committee for Nirmal Bangla Mission/ Swachh Bharat Mission dated 05.01.2017. Notice inviting e-Tender was issued by the Chairman, Jalpaiguri Municipality on 27.03.2017 for publication in the Newspapers as well as in the Website.

In this regard, some of the key points were highlighted as mentioned below:

1. 'ECLEAN SPECTRON ENVIRONMENT PRIVATE LIMITED', the lone bidder offered rate for an amount of Rs. 7,19,50,000.00 (after bid call) for the above work as 'Turn-key Basis'. Offered rate is 0.17% less than Rs. 7,20,70,502.45, the cost of the component (i/c O & M cost for one year) as per approved DPR.

The committee was further informed that this is 3rd call of tender in which only a single bidder has participated and the first call of Tender was cancelled due to no participant and the 2nd call of tender was cancelled by the Chairman, Jalpaiguri Municipality as only one participant was found.

Details are tabulated below

Sl. No.	Name of Work	No of Call	No of Bidders	Name of bidder	Cost offered by single bidder (Rs.)	Pro-rata Cost as per Approved DPR (Rs.)	Remarks
1	Planning, Designing, Construction and Commissioning of 25 MT per Day Solid waste processing setup by installing a Biogas Plant' under Jalpaiguri Municipality	3rd	1 no.	Eclean Spectron Environment Private Limited	71950000.00	72070502.45	The offered cost is 0.17 % less than the pro-rata cost as per approved DPR, hence may be accepted subject to the approval from the F.D

After detailed discussions on the above items, the committee's observations are noted as

follows:


1. EcleanSpectron Environment Private Limited being the single bidder in all four towns i.e. Jalpaiguri, Ranaghat, Krishnanagar & Shantipur, performance of the farm need to be evaluated by a sub-committee formed from the members of Technical Committee and are as follows:
 - (i) Director, SUDA.
 - (ii) Additional Mission Director, SBM/NIRMAL BANGLA.
 - (iii) Director General, Water Supply, KMC.
 - (iv) Chief Engineer, MED.

2. After obtaining recommendation of the sub-committee, mentioned above, final recommendation towards acceptance of the offer by the single bidder to be forwarded to the Chairman, Technical Committee and Secretary, UD&MA Department for consideration and onward submission to the Finance Department (F.D) in terms of F.D. memorandum no. 925-F(Y) dated 14-02-2017.

The Meeting ended with a vote of thanks to and from the chair.



(Onkar Singh Meena)
Secretary
UDMA Department
Government of West Bengal
& Chairman, Technical Committee



Chief Engineer
M.E Directorate
Deptt. of Municipal Affairs
Govt of West Bengal



Director
State Urban Development Agency

Meeting

w.r.t.

**Status of New-Construction of U-PHC
under NUHM**

at

SUDA Conference Hall

On

06.02.2018

Backdrop of renovation & new construction of U-PHC under NUHM :

- **89 ULBs including 07 Municipal Corporations have been covered under NUHM.**
- **To strengthen primary Health care service 168 no. of New Construction of U-PHC and 291 no. of Renovation of existing premises to function as U-PHC has been approved.**
- **Allotment for such work issued in 2013-14, 2014-15 & 2015-16.**
- **The activity status are being reviewed by NUHM, DHFW at bi-monthly interval.**
- **It is observed that construction of New U-PHC in a no. of ULBs are not progressing as per desired level.**

**● Resolution of Review Meeting dt. 13 to
15.09.2017 held with NUHM, DHFW spells :**

- All renovation work to be completed by
October, 2017**
- The ULBs to initiate construction of New
UPHC building within November, 2017.**

**ULB-wise status w.r.t. New Construction of U-
PHC**

Sl No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected date of completion
A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O	
1	Alipurdar	Alipurdar	Alipurdar UPHC 1 Ward No.16 New Alipurdar	NC	2015-16	75.00	30.00	30.00	21.86	8.14	0.00	8.14	40%	No physical progress since May 2017	Apr-18
2	Bankura	Bankura	Bankura UPHC 1 Ward No. 12 Idamahalia Bansalia	NC	2013-14	75.00	45.00	22.50	4.30	18.20	22.50	40.70	25%	Work not started but tender process completed 451. Contingency money to be set. Tender not started but tender process completed	Apr-18
	Bankura	Bankura	Bankura UPHC 2 Ward No. 19 Patala Pump House Kethadanga	NC	2013-14	75.00	45.00	0.00	0.00	0.00	45.00	45.00	0%	Work not started but tender process completed	Apr-18
	Bankura	Bankura	Bankura UPHC 3 Ward No. 1 Dasherbandh Lane near District Library	NC	2013-14	75.00	45.00	0.00	0.00	0.00	45.00	45.00	0%	Work not started but tender process completed	Apr-18
3	Bankura	Bishnupur	Bishnupur UPHC 1 Ward No. 15 near Bishnupur Municipality Premises	NC	2013-14	75.00	45.00	0.00	0.00	0.00	45.00	45.00	40%		Mar-18
4	Rampurhat HD	Rampurhat	Rampurhat UPHC 1 Ward No. 6 Gandhi Park	NC	2013-14	75.00	45.00	30.00	0.00	30.00	15.00	45.00	40%		Mar-18
5	Birbhum	Suri	Suri UPHC 1 Ward No 8 Suri Municipal Office	NC	2013-14	75.00	45.00	45.00	42.25	2.75	0.00	2.75	70%		Feb-18
6	Birbhum	Bolpur	Bolpur UPHC 1 Ward No. 17 Dharmatala	NC	2015-16	75.00	30.00	22.50	0.00	22.50	7.50	30.00	25%		May-18
	Birbhum	Bolpur	Bolpur UPHC 2 Ward No. 19 Bypass More	NC	2015-16	75.00	30.00	0.00	0.00	0.00	30.00	30.00	10%		May-18
7	Cooch Behar	Cooch Behar	Cooch Behar UPHC 1 Ward No. 12 Rahindranagar	NC	2013-14	75.00	45.00	23.50	27.03	-3.53	21.50	17.97	57%		Mar-18
	Cooch Behar	Cooch Behar	Cooch Behar UPHC 2 Ward No. 3 Kalabagan near kalabagan primary school	NC	2013-14	75.00	45.00	23.50	1.05	22.45	21.50	43.95	0%	Preparation of Plan estimate is yet to be done	Site Problem
8	Dakshin Dinajpur	Saturghat	Saturghat UPHC 3 Ward No. 17 Sare Tin No Club	NC	2013-14	75.00	45.00	22.50	0.00	22.50	22.50	45.00	0%	Work not started but tender process completed and work order issued	May-18
9	Hooghly	Dankuni	Dankuni UPHC 1 Ward No. 2 Kharai Barowatala Kanarpura	NC	2013-14	75.00	45.00	45.00	0.25	44.75	0.00	44.75	10%		Jul-18
	Hooghly	Dankuni	Dankuni UPHC 2 Ward No. 20 Maatur dingi near hanapur	NC	2013-14	75.00	45.00	45.00	8.75	36.25	0.00	36.25	10%		Jul-18
10	Hooghly	Arambagh	Arambagh UPHC 1 Chandur Bhatamore Ward No. 15	NC	2015-16	75.00	30.00	24.00	22.22	1.78	6.00	7.78	55%		Mar-18
11	Jaipalguri	Jaipalguri	Jaipalguri UPHC 1 Ward No. 18 Keranipara	NC	2013-14	75.00	45.00	30.57	15.93	14.64	14.43	29.07	40%		Feb-18
	Jaipalguri	Jaipalguri	Jaipalguri UPHC 2 Ward No. 15 Pandepara	NC	2013-14	75.00	45.00	30.45	0.00	30.45	14.55	45.00	1%	Work not started but tender process completed and work order issued since from April 2017	May-18
12	Maidah	Old Maida	Old Maida UPHC 1 Ward No. 5 Adjacent to Old Maida Municipal Administrative Building	NC	2015-16	75.00	30.00	0.00	0.00	0.00	30.00	30.00	0%	Work not started but only plan estimate vetted by MED	Aug-18
	Maidah	Old Maida	Old Maida UPHC 2 Ward No. 15 Shibram Rally Mangalbari	NC	2015-16	75.00	30.00	0.00	0.00	0.00	30.00	30.00	0%	Work not started but only plan estimate vetted by MED	Aug-18

File No 11-00 AM to 1 PM

-MED

A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O	
Sl. No.	District Name	ULB Name	U-PHC Name	Constructio n Type	Year of Approval	Amount Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditur e (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completi on	Remarks	Expected date of completion
13	Murshidabad	Berhampur	Berhampur UPHC 1 Ward No. 1 Cossimbazar	NC	2013-14	75.00	45.00	45.00	17.58	27.42	0.00	27.42	0%	1) 2nd call already floated and will be opened on 16.08.17 ii) 2nd call cancelled. iii) 3rd call already floated 08.09.2017 iv) 3rd call opened an Technical Papers sent to MED on 10.10.17	Aug-18
	Murshidabad	Berhampur	Berhampur UPHC 2 Ward No. 3 Saldabad Khara	NC	2013-14	75.00	45.00	45.00	37.53	7.47	0.00	7.47	95%		Jan-18
	Murshidabad	Berhampur	Berhampur UPHC 3 Ward No. 8 Kantanasar Khara	NC	2013-14	75.00	45.00	45.00	29.00	16.00	0.00	16.00	50%		Feb-18
	Murshidabad	Berhampur	Berhampur UPHC 4 Ward No. 21 R.N Taore Near Laldighi	NC	2013-14	75.00	45.00	45.00	21.58	23.42	0.00	23.42	35%		Mar-18
14	Murshidabad	Dhulan	Dhulan UPHC 1 Dr. APJ Abdul Kalam Azar Ward No. 04	NC	2014-15	75.00	22.50	22.50	10.00	12.50	0.00	12.50	40%		Mar-18
	Murshidabad	Dhulan	Dhulan UPHC 2 Sachindra Nath Hattchara Road	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	0%	Tender process yet to be done	Site Problem
15	Murshidabad	Jangipur	Jangipur UPHC 1 Ward No. 7 Roy Ward No. 16 Dighri Chotokalla	NC	2015-16	75.00	30.00	30.00	31.39	-1.39	0.00	-1.39	95%		Jan-18
	Murshidabad	Jangipur	Jangipur UPHC 2 Ward No. 3 Gokulpur Mathpara	NC	2015-16	75.00	30.00	30.00	0.00	30.00	0.00	30.00	0%	Plan Estimate yet to be done	Fresh modified proposal awaiting
16	Murshidabad	Jiaganj Azinganj	Jiaganj Azinganj UPHC 1 Ward No. 11 Jiaganj Town Centre	NC	2015-16	75.00	75.00	75.00	59.97	15.03	0.00	15.03	100%		Mar-18
	Murshidabad	Jiaganj Azinganj	Jiaganj Azinganj UPHC 2 Ward No. 17 Basulatali More Azinganj Junction	NC	2016-17	75.00	30.00	30.00	42.94	-12.94	0.00	-12.94	60%		Mar-18
17	Murshidabad	Kandi	Kandi UPHC 1 Ward No. 8 Jemo Bandanga Rajbari	NC	2015-16	75.00	30.00	30.00	0.00	30.00	0.00	30.00	0%	Tender process yet to be done	Will inform to State after 10 days
18	Nadia	Kalyani	Kalyani UPHC 1 Ward No. 1 Anukul More Chandamari Bazar	NC	2014-15	75.00	22.50	22.50	0.81	21.69	0.00	21.69	20%		Jan-18
19	Nadia	Nabadvip	Nabadvip UPHC 1 Dr. Bidhan Candra Roy Sasthya Kendra Ward No. 7 Misri Para	NC	2014-15	75.00	56.25	56.25	37.67	18.58	0.00	18.58	77%		Jan-18
	Nadia	Nabadvip	Nabadvip UPHC 2 Sister Nilbedita Sasthya Kendra Ward No. 17 Alania Shib Tala Road	NC	2014-15	75.00	56.25	56.25	33.20	23.05	0.00	23.05	77%		Jan-18
	Nadia	Nabadvip	Nabadvip UPHC 3 Mother Teresa Sasthya Kendra Ward No. 19 Kolar Demra Road	NC	2014-15	75.00	56.25	56.25	31.73	24.52	0.00	24.52	77%		Jan-18
20	Nadia	Santipur	Santipur UPHC 1 Ward No 17 Dr. B. C. Ray Road	NC	2014-15	75.00	28.75	28.75	2.16	26.59	0.00	26.59	31%		Mar-18
	Nadia	Santipur	Santipur UPHC 3 Ward No 13 Panchanan tata lane	NC	2014-15	75.00	28.75	28.75	0.00	28.75	0.00	28.75	70%		Jan-18
21	Nadia	Chakdaha	Chakdaha UPHC 1 Sakuntala Taltala Ward No. 20	NC	2015-16	75.00	30.00	30.00	30.00	0.00	0.00	0.00	80%		Jan-18
	Nadia	Chakdaha	Chakdaha UPHC 2 Malobika Ward No. 12 Ghughia Sarfarpara	NC	2015-16	75.00	30.00	30.00	32.16	-2.16	0.00	-2.16	75%		Jan-18
22	Nadia	Gayerpur	Gayerpur UPHC 1 Ward No. 15 Katabani	NC	2015-16	75.00	26.25	26.25	29.74	-3.49	0.00	-3.49	70%		Jan-18

Electrical plan
submitted
MED

A	B	C	D	E	F	G	H	I	J	K=I+J	L=H+I	M=K+L	N	Remarks	Expected date of completion
Sl. No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion		
23	Nadia	Haringhata	Haringhata UPHC 1 Ward No. 2 Subarnapur near Haringhata Bazar	NC	2015-16	75.00	18.75	18.75	11.71	7.04	0.00	7.04	70%	File drawing system has to be made by the contractor. Work order issued on 12.12.17	Jan-18
24	Nadia	Ranaghat	Ranaghat UPHC 1 Dargatala UPHC Ward No. 09 Dispensary Lane	NC	2015-16	75.00	30.00	30.00	17.76	12.24	0.00	12.24	55%	Work order issued on 12.12.17	Mar-18
25	Purulia	Purulia	Ranaghat UPHC 2 Nagra UPHC Ward No. 18 Bamsanaha Purulia UPHC 1 Ward No. 12 Namocara Durgamandir Purulia UPHC 2 Ward No. 5 Joydewan Club Nadia	NC	2013-14	75.00	45.00	45.00	0	45.00	0.00	45.00	0%	Completed	Jan-18
26	Howrah	Howrah MC	Howrah UPHC 3 Ward No 4 Satya Narayan Temple Road Salika	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Plan estimate yet to be done for UPHC building	2018
	Howrah	Howrah MC	Howrah UPHC 4 Ward No. 2 A. Nasser Para Road	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Plan estimate yet to be done	2018
	Howrah	Howrah MC	Howrah UPHC 15 Ward No 191, R. Bellious Lane	NC	2013-14	75.00	45.00	24.00	0.00	24.00	21.00	45.00	35%	Tender process completed & Work order issued	Jan-18
	Howrah	Howrah MC	Howrah UPHC 16 Ward No. 42 Priya Nath Ghosh Lane	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Tender process completed & Work order issued	Jan-18
	Howrah	Howrah MC	Howrah UPHC 17 Ward No. 10 Sita Nath Bose Lane	NC	2013-14	75.00	45.00	44.00	0.00	44.00	1.00	45.00	65%	Tender process completed & Work order issued	Jan-18
	Howrah	Howrah MC	Howrah UPHC 18 Ward No. 40 Deberdola Ganguly Road	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Tender process completed & Work order issued	Jan-18
	Howrah	Howrah MC	Howrah UPHC 19 HAU Ward No. 32 Kalidpur Lane	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Tender process completed & Work order issued	Jan-18
	Howrah	Howrah MC	Howrah UPHC 20 Ward No. 18 Benken Park Panchanatala Road	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Plan estimate yet to be done	Jan-18
	Howrah	Howrah MC	Howrah UPHC 21 Ward No. 141 C. Bose Road Howrah	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Plan estimate yet to be done	Jan-18
	Howrah	Howrah MC	Howrah UPHC 22 Ward No. 56 Benken Behari Ghosh Lane	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	For working order to be done	Jan-18
	Howrah	Howrah MC	Howrah UPHC 23 Ward No. 62 Bally GT Rd. Muza barrackpore	NC	2014-15	75.00	10.00	7.00	0.00	7.00	3.00	10.00	25%	Tender process completed & Work order issued. Requisition from SDO, Howrah under sanctioning.	Jan-18
27	Darjeeling	Siliguri MC	Siliguri UPHC 10 Ward No. 5 Ganganagar near Park	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Requisition submitted to HSD for working order. Tender will be floated on 16.1.18.	Aug-18

Requisition submitted to HSD for working order. Tender will be floated on 16.1.18.

Plan estimate yet to be done for UPHC building

For working order to be done

From 2 PM to 4 PM

STATUS OF CONSTRUCTION OF NEW U.P.H.C. BUILDING (upto November-2017)

A	B	C	D	E	F	G	H	I	J	K+L+J	L+K+J	M+K+L	N	O
District Name	ULB Name	U.P.H.C Name	Constructio n Type	Year of Approval	Amount Entire/ Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditur e (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District/ SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of Physical Completo n	Remarks	Expected date of completion
Paschim Bardhaman	Asansol MC	Asansol UPHC 12 Januria Ward No. 07 Kalamuri beside Bhanpur Road & Sarkis Centre	MC	2014-15	75.00	30.00	0.00	0.00	0.00	30.00	30.00	25%		Mar-18
Paschim Bardhaman	Asansol MC	Asansol UPHC 11 Januria Ward No. 04 Eye pass road spo. Januria Truck B Terminal	MC	2014-15	75.00	30.00	0.00	0.00	0.00	30.00	30.00	25%	This line-item will be changed due to non availability of Land, Procurement of Land for new site is under process. Final line-item will receive within Dec- 17	Site Problem
Paschim Bardhaman	Asansol MC	Asansol UPHC 14 Januria Ward No. 11 Spiral Ramp Colony	MC	2014-15	75.00	25.00	0.00	0.00	0.00	25.00	25.00	0%	Work not started but tender process will inform to State after 10 days	Jan-18
Paschim Bardhaman	Asansol MC	Tenant Petri within 85 Plot No. 227 Mouza - Egara at ward no.93, Rangpur	MC	2014-15	75.00	25.00	0.00	0.00	0.00	25.00	25.00	0%	Work not started but tender process will inform to State after 10 days	Jan-18
Paschim Bardhaman	Asansol MC	Jhandi Danga, plot No. 47 & 49, Mouza Bakur nagar, Ward No. - 35, Rangpur	MC	2014-15	75.00	25.00	0.00	0.00	0.00	25.00	25.00	0%	Work not started but tender process will inform to State after 10 days	Jan-18
Paschim Bardhaman	Asansol MC	Leprosy Society SBO project of	MC										Line-list was not received. Site was not yet finalized	
Paschim Bardhaman	Asansol MC	Dhemonakh, ward no. 58 (new), Kulti	MC	2015-16	75.00	30.00	30.00	0.00	0.00	30.00	30.00	100%	Work not started but tender process and work order issued	Will inform to State after 10 days
Paschim Bardhaman	Asansol MC	Baraker, ward no. 67 (new), Kulti	MC	2015-16	75.00	30.00	30.00	0.00	0.00	30.00	30.00	100%	Work not started but tender process and work order issued	Will inform to State after 10 days
Paschim Bardhaman	Asansol MC	Dhargarti, ward no. 105 (new), Kulti	MC	2015-16	75.00	30.00	30.00	0.00	0.00	30.00	30.00	100%	Work not started but tender process and work order issued	Will inform to State after 10 days
Paschim Bardhaman	Asansol MC	Bityandapur P.H.C., ward no. 99 (new), Kulti	MC	2015-16	75.00	30.00	30.00	0.00	0.00	30.00	30.00	100%	Work not started but tender process and work order issued	Will inform to State after 10 days
Paschim Bardhaman	Asansol MC	Sodepur P.H.C., ward no. 102 (new), Kulti	MC	2015-16	75.00	30.00	30.00	0.00	0.00	30.00	30.00	100%	Work not started but tender process and work order issued	Will inform to State after 10 days
Paschim Bardhaman	Asansol MC	Kumardaha P.H.C., ward no. 59 (new), Kulti	MC	2015-16	75.00	30.00	30.00	0.00	0.00	30.00	30.00	100%	Work not started but tender process and work order issued	Will inform to State after 10 days
2	North 24 Parganas Bidhanagar MC	Bidhanagar UPHC 1 Ward No. 28 poderite Krishnabai, UPHC	MC	2014-15	75.00	22.50	0.00	0.00	0.00	22.50	22.50	0%	Work not started due to litigation. functioning from Khamruihal, w no 36	Work not started due to litigation. functioning from Khamruihal, w no 36
	North 24 Parganas Bidhanagar MC	Bidhanagar UPHC 2 Ward No. 36	MC	2014-15	75.00	22.50	0.00	0.00	0.00	22.50	22.50	25%	Cancelled due to objection in bid. New site identified at no. 36- to be re-let in one month. end of Feb.	Work not started due to litigation. functioning from Khamruihal, w no 36
	North 24 Parganas Bidhanagar MC	Bidhanagar UPHC 4 Ward No. 39 near DA block	MC	2014-15	75.00	22.50	30.00	0.00	30.00	22.50	22.50	0%	Invoyment by P&C.	Work not started due to litigation. functioning from Khamruihal, w no 36
	North 24 Parganas Bidhanagar MC	Bidhanagar UPHC 11 Ward No. 7 Kalyanpur, Bidhanagar UPHC	MC	2014-15	75.00	22.50	0.00	0.00	0.00	22.50	22.50	0%	Site not yet finalized. (NOC from Airport Authority).	Work not started due to litigation. functioning from Khamruihal, w no 36
	North 24 Parganas Bidhanagar MC	Bidhanagar UPHC 12 Ward No. 27 Kalyanpur, Bidhanagar UPHC	MC	2014-15	75.00	22.50	0.00	0.00	0.00	22.50	22.50	0%	Site not yet finalized. (NOC from Airport Authority).	Work not started due to litigation. functioning from Khamruihal, w no 36

Plan estimate yet to be done
site not yet finalized.
poll from Bidhanagar is called.

estimate by 25th Dec
estimate by 25th Dec

SOB for Bidhanagar
Pondrond for 100%
follow to mp
DIPA - 3
E-tender - 1
Procurement - 1
Re-survey

A	B	C	D	E	F	G	H	I	J	K	L	M	N
Sl No.	District Name	U.I.B Name	U-PRC Name	Construction Type	Year of Approval	Amount Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to U.I.B (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at U.I.B (Rs. in Lakh)	Balance at SIDA (Rs. in Lakh)	Total Unpaid Balance (Rs. in Lakh)	% of physical completion
13	North 24 Parganas	Nobhati	Nishad UPRC 1 Ward No. 29 Nishad UPRC 2 Ward No. 02 R.B.C. Road Garia	NC	2014-15	75.00	22.50	13.50	0.00	13.50	9.00	22.50	30%
13	North 24 Parganas	Parhat	Parhat UPRC 1 Ward No. 3 Ramdharma Pally Paschager Road Kulherjee Road	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	30%
13	North 24 Parganas	Parhat	Parhat UPRC 2 Ward No. 6 D. Saraj Ushampur Football Ground	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	30%
14	North 24 Parganas	Parhat	Parhat UPRC 8 Ward No. 29 Pur Near Parbhari Bazar	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	30%
14	North 24 Parganas	Baduria	Baduria UPRC 1 Ward No. 5 PS Baduria	NC	2015-16	75.00	30.00	50.00	31.1	18.90	-20.00	1.10	85%
14	North 24 Parganas	Bauria	Baduria UPRC 2 Ward No. 2 Near purna bazar	NC	2016-17	75.00	0.00	30.00	0	10.00	-10.00	0.00	0%
15	North 24 Parganas	Garuha	Garuha UPRC 2 HAU Water Tank companion Ward No. 10 Garuda main road	NC	2015-16	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%
14	Paschim Medinipur	Gahal	Parhat UPRC 1 Ward No. 5 Gangpur	NC	2015-16	75.00	10.00	0.00	0.00	0.00	30.00	30.00	25%
17	Purba Bardhaman	Kalra	Kalra UPRC 1 Ward No. 17 Gatalapara	NC	2015-16	75.00	30.00	30.00	0.00	30.00	0.00	30.00	100%
18	Purba Bardhaman	Kalra	Kalra UPRC 1 Ward No. 18 Chak W. No. 16 Nishi UPRC 7 Ward No. 7 Bager	NC	2015-16	75.00	30.00	20.00	0.00	20.00	10.00	30.00	100%
19	Purba Medinipur	Haldia	Haldia UPRC 1 Ward No. 2 Haldia	NC	2014-15	75.00	30.00	25.32	16.37	8.95	4.68	13.63	70%
	Purba Medinipur	Haldia	Haldia UPRC 2 Ward No. 5 Raghubarichak Ramnagar	NC	2014-15	75.00	30.00	30.00	0.00	0.00	30.00	30.00	100%
	Purba Medinipur	Haldia	Haldia UPRC 3 Ward No. 11 Tentulibera P.O. Debhog	NC	2014-15	75.00	30.00	28.32	24.70	0.62	4.68	5.30	95%
	Purba Medinipur	Haldia	Haldia UPRC 4 Ward No. 6 Geonowave	NC	2014-15	75.00	30.00	25.32	13.62	11.70	4.68	16.38	70%
20	Purba Medinipur	Pandura	Pandura UPRC 1 Ward No. 2 Paratapour	NC	2015-16	75.00	30.00	32.12	32.12	0.00	-2.12	2.12	100%
21	Diamond Harbour	Diamond Harbour	Diamond Harbour UPRC 1 Ward No. 04 Jagerman Serei Phippur	NC	2013-14	75.00	45.00	22.50	21.50	0.00	22.50	22.50	60%
22	South 24 Parganas	Rajpur Sonarpur	Rajpur Sonarpur UPRC 5 Ward No. 05 Karnabon Sonarpur, Sankarman Chak	NC	2014-15	75.00	22.50	22.50	38.37	-13.07	0.00	-13.07	50%
	South 24 Parganas	Rajpur Sonarpur	Rajpur Sonarpur UPRC 6 Ward No. 12	NC	2014-15	75.00	22.50	22.50	2.21	20.29	0.00	20.29	100%
	South 24 Parganas	Rajpur Sonarpur	Rajpur Sonarpur UPRC 7 Ward No. 2 Chak Kharak, Vidyasobha	NC	2014-15	75.00	22.50	22.50	36.43	-13.93	0.00	-13.93	60%
	South 24 Parganas	Rajpur Sonarpur	Rajpur Sonarpur UPRC 8 Ward No. 35 Bela, Renu, Anuradha Nagar	NC	2014-15	75.00	22.50	22.50	9.58	13.14	0.00	13.14	35%

SITC

1+1'

Grand Award
road & starting
TWC / 18

Grand Award
road & starting
TWC / 18

Electrical equipment to be supplied by contractor. Single trench draw. opening at both side terminals.

Forming work by contractor. Forming work by contractor.

Site problem. Site problem. Site problem. Site problem. Site problem. Site problem. Site problem. Site problem. Site problem. Site problem.

Am

Status of Construction of New U.PHC Buildings, Ujala, Government - 17

A	B	C	D	E	F	G	H	I	J	K=I-J	L=H-I	M=K-L	N	O	
Sr No.	District Name	U.G. Name	U.PHC Name	Construction Type	Year of Approval	Amount Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to U/G (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at U/G (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected date of completion
23	Utter Dinajpur	Raiganj	Raiganj UPHC 2 Ward No. 02 Sri Ma Amranda Maiti Pura Swasthya Seva Kendra Deobhampura	NC	2013-14	75.00	75.00	22.50	0.00	22.50	52.50	75.00	0%	Work not started. Due to site problems through tender process completed.	Due to site problem fresh estimation will be sent to M&E for vetting Aug-18.
24	Utter Dinajpur	Raiganj	Raiganj UPHC 4 Ward No. 21 Maiti Pura Swasthya Seva Kendra Deobhampura	NC	2013-14	75.00	75.00	22.50	9.30	13.20	52.50	65.70	8%	Work was stopped for approx 1 yr. Now just started G+1 completed by 18	18-18
25	Utter Dinajpur	Gangarampur	Gangarampur UPHC 1 Ward No. 11 Durgapara	NC	2015-16	75.00	30.00	30.00	24.95	5.05	0.00	5.05	7%	WORK STOPPED from past 1 year	18-18
26	Utter Dinajpur	Katlaganj	Katlaganj UPHC 1 Ward No. 13 R.K. Srani	NC	2015-16	75.00	30.00	42.00	18.00	2.00	-10.00	8.00	10%	Work stopped from past 1 year. Work started on 5-2-18.	18-18
27	Paschim Medinipur	Kharagpur	Kharagpur UPHC 5 Ward No. 35 Talabegicha	NC	2014-15	75.00	45.00	45.00	101.06	-56.06	0.00	-56.06	100%	Work completed	Feb-18
	Paschim Medinipur	Kharagpur	Kharagpur UPHC 6 Ward No. 18 GIRD	NC	2014-15	75.00	45.00	45.00	101.06	-56.06	0.00	-56.06	100%	Work completed	Feb-18

Work stopped - Tender problem. Work will be opened soon by M&E.

Agency terminated on 29-1-18. Fresh tender will be sent to M&E for work on Feb-18.

Boo - letter -

VCT - N.S.

for filling up vacancy.

Dir. to issue letter

Schedule to be prepared.

Letter to issue

Ph: 240-008, 241-279

S.T.D - 03472

E-mail- chairmannabadwip@gmail.com

NUHM

দুরাভাষ : ২৪০-০০৮, ২৪১-২৭৯

এস.টি.ডি - ০৩৪৭২



পৌর সদস্য পর্ষদের কার্যালয়
নবদ্বীপ পৌরসভা, পো:-নবদ্বীপ, জেলা - নদীয়া

**OFFICE OF THE BOARD OF COUNCILLORS
NABADWIP MUNICIPALITY
NABADWIP, NADIA**

Memo No. / F- 73/ M & S Cell / NM / 13-14

Date-

From :

The Vice-Chairman,
Nabadwip Municipality,
Nabadwip, Nadia.

To

The Executive Engineer,
MED, Nadia
P.O. Krishnagar,
Dist. Nadia.

Sub: Request for prepare bill of UPHCs under NUHM in
Nabadwip Municipal Area.

Sir,

I like to draw your attention that civil work of UPHC of Nabadwip Municipalities under NUHM are likely to be completed (around 80%). But R.A. bill received from your office till date is amounting Rs.1, 04, 82,592/- (One Core four lakhs eighty two thousand five hundred ninety two) only which is 46.6% of total fund. The entire amount (Rs.1, 04, 82,592/-) already utilized. In this situation this office not getting further fund for this programme.

Now, I would request to you please take prompt action for prepare & submit of arrear R.A. bill of UPHCs under NUHM of Nabadwip Municipality to this office as early possible.

This is urgent.

With thanks,

Yours faithfully

S/d- Sachindra Basak

Vice-Chairman
Nabadwip Municipality

Memo No. ২১৭/১(২)/ F- 73/ M & S Cell / NM / 13-14

Date- 05/1/18

- 1). Dy.CMOH-1 and Nodal Officer, NUHM, Nadia.
- 2). State Nodal Officer, NUHM, West-Bengal.

SBK. 5/1/18

Vice-Chairman
Nabadwip Municipality

Vice-Chairman
Nabadwip Municipality

ole
: 240-008, 241-279
S.T.D - 03472

দুরাভাষ : ২৪০-০০৮, ২৪১-২৭৯
এস.টি.ডি - ০৩৪৭২



পৌর সদস্য পর্ষদের কার্যালয়
নবদ্বীপ পৌরসভা, পি:নবদ্বীপ, জলা - নদীয়া
**OFFICE OF THE BOARD OF COUNCILLORS
NABADWIP MUNICIPALITY
NABADWIP, NADIA**

Memo No. /F-73/M & S Cell/nm/13-14

Date-

From: - Sri Sachindra Basak
Vice-Chairman, Nabadwip Municipality
Nabadwip, Nadia.

To,
The Executive Engineer,
MED, Nadia
P.O. Krishnagar, Dist. Nadia

Sub: Request for prepare bill of UPHCs under NUHM in
Nabadwip Municipal area. (1st remainder)

Sir,

I like to draw your attention that civil work of UPHCs of Nabadwip Municipalities under NUHM are likely to be completed (around 80%). But R.A. bill received from your office and already paid till date is amounting Rs.1, 04, 82,592/- (One Core four lakhs eighty two thousand five hundred ninety two) only which is 46.6% of total Sanctioned fund. In this situation this office not getting further fund for this programme.

Now, I would request to you please take prompt action for prepare and submit of arrear R.A. bill of UPHCs under NUHM of Nabadwip Municipality to this office as early as possible.

This is urgent.

With thanks

Yours faithfully

S/d- S. Basak

Vice-Chairman
Nabadwip Municipality

Date- 25/01/18

GSK

Vice-Chairman
Nabadwip Municipality

Vice-Chairman
Nabadwip Municipality

Memo No. 225/1(2)/F-73/M & S Cell/nm/13-14

- 1). Dy.CMOH-1, Nadia and Nodal Officer, NUHM, Nadia
- 2). State Nodal Officer, NUHM, West Bengal



Ph : 240-008, 241-279
S.T.D - 03472



দুরাভাষ : ২৪০-০০৮, ২৪১-২৭৯
এস.টি.ডি - ০৩৪৭২



পৌর সদস্য পর্ষদের কার্যালয়
নবদ্বীপ পৌরসভা, পা:-নবদ্বীপ, জলা - নদীয়া
**OFFICE OF THE BOARD OF COUNCILLORS
NABADWIP MUNICIPALITY
NABADWIP, NADIA**

Memo No. /F-73/M & S Cell/nm/13-14

Date-

From: - Sri Sachindra Basak
Vice-Chairman, Nabadwip Municipality
Nabadwip, Nadia.

To,
The District Magistrate, Nadia
P.O. Krishnagar, Dist. Nadia

Sub: Bill of UPHCs under NUHM in Nabadwip Municipal area.

Sir,

I like to draw your attention that civil work of UPHCs of Nabadwip Municipalities under NUHM are likely to be completed (around 80%). But R.A. bill received from MED office and already paid till date is amounting Rs.1, 04, 82,592/- (One Core four lakhs eighty two thousand five hundred ninety two) only which is 46.6% of total Sanctioned fund. But MED not submitted rest R.A. bill of UPHCs. In this situation this office not getting further fund for this programme.

This office already requested to MED for preparation of R.A bill vide this office letter no. 214/F-73 /M&S Cell/NM /13-14 dated 05.01.18. A reminder also sends from this office to MED vides this office letter no. 225/F-73 /M&S Cell/NM /13-14 dated 25.01.18. But unfortunately no feedback received in this subject.

With thanks

Yours faithfully

SBK

Vice-Chairman
Nabadwip Municipality

Memo No. 230/1(4) /F-73/M & S Cell/nm/13-14

Date 30/1/18

1). The Executive Engineer,
MED, Nadia
P.O. Krishnagar, Dist. Nadia

Vice-Chairman
Nabadwip Municipality

- 2). The O.C.Health,Nadia
P.O.Krishnagar, Dist.Nadia
- 3). Dy.CMOH-1, Nadia and Nodal Officer,
NUHM,Nadia, P.O.Krishnagar, Dist.Nadia
- 4). State Nodal Officer,
NUHM,West Bengal



BSK.
Vice-Chairman
Nabadwip Municipality

**Vice-Chairman
Nabadwip Municipality**



HOWRAH MUNICIPAL CORPORATION
HOWRAH URBAN HEALTH SOCIETY
4, Mahatma Gandhi Road, Howrah – 711 101. Phone: 2638 3211-13,
Fax: 2641 2214/5846/5218. Email ID : health.hmc@gmail.com



**Resolution of Meeting held at Commissioners Room on 03.02.18
at Commissioners room**

Sl No.	Name of UPHC	Status	Person Responsible
1	19, Satyanarayan Temple Road (Badhaghat), Salkia	Estimation to be done within next week . MED Vetting by 12.02.18	Engineering Department.
2	55, A Naskar Para Road, Howrah -7	Estimation to be done within next week . MED Vetting by 12.02.18	
3	4, Gopal Lal Chowdhury Lane	Estimation to be done within next week . MED Vetting by 12.02.18	
4	14, Debendra Ganguly Road. Ward No-	Awaiting NOC form DHFW. But if a new UPHC is Constructed at Gopal Lal Choudhury lane, i.e place 3 Meationed above it will Couincide in the same ward.	To be raised in S.U.D.A Meeting.
5	Banku Bihari Ghosh Lane (Khamarpara)	Record to be Obtained form Bally Office by 05.02.18	Secretary HMC will provide the information to OSD(H)
6	Padmapukur Water Plant	HIT authority letter to be issued from Mayors and to the Concerned authority.	OSD (H) & N.O (NUHM)
7	Sayed Amir Ali School (Tikiapara)	Place to be Cofirmed.	
8	Priyanath Ghosh Lane, Howrah. Ward-42	Joined site visit with parks & Garden & Health dept.	MMIC (Health) will rais the issue in MIC Meeting
9	I.C Bane Lane	LR dept is to be Consulted	MMIC (Health) & Councillor Ward - 14
10	Ward - 7	Place to be identified.	MMIC (Health)
11	Ward- 51 (Bally)	Place to be identified.	MMIC (Health) & Secretary HMC will continu the place
12	Ward -45	Place to be identified.	MMIC (H) to consult with Councillor Ward-45
13	1 Place to be identified form Br. LII	Place to be identified.	Goutam Dutta Counciler-19 Brough Chairman -III
14	Dharsa Govt colony , Udbastu Samity Plot-16 Ward No-47	Colony Para under R.R Dept To be confirmed from L&R dept.	MMIC(H)

Members present from Health Dept.

1) MMIC (H&FW)

2) OSD (H)

3) Nodal Officer, NUHM

4) Consultant Epidemiologist, NUHM

Land belongs to HMC, MED Vetting by 12.02.18

maybe

maybe

maybe

maybe



HOWRAH MUNICIPAL CORPORATION
HOWRAH URBAN HEALTH SOCIETY
4, Mahatma Gandhi Road, Howrah – 711 101. Phone: 2638 3211-13,
Fax: 2641 2214/5846/5218. Email ID : health.hmc@gmail.com



**Resolution of Meeting held at Commissioners Room on 03.02.18
at Commissioners room**

SI No.	Name of UPHC	Status	Person Responsible
1	19, Satyanarayan Temple Road (Badhaghat), Salkia	Estimation to be done within next week . MED Vetting by 12.02.18	Engineering Department.
2	55, A Naskar Para Road, Howrah -7	Estimation to be done within next week . MED Vetting by 12.02.18	
3	4, Gopal Lal Chowdhury Lane	Estimation to be done within next week . MED Vetting by 12.02.18	
4	14, Debendra Ganguly Road. Ward No-	Awaiting NOC form DHFW. But if a new UPHC is Constructed at Gopal Lal Choudhury lane, i.e place 3 Meationed above it will Couincide in	To be raised in S.U.D.A Meeting.
5	Banku Bihari Ghosh Lane (Khamarpara)	Record to be Obtained form Bally Office by 05.02.18	Secretary HMC will provide the information to OSD(H)
6	Padmapukur Water Plant	HIT authority letter to be issued from Mayors and to the Concerned authority.	OSD (H) & N.O (NUHM)
7	Sayed Amir Ali School (Tikiapara)	Place to be Cofirmed.	
8	Priyanath Ghosh Lane, Howrah. Ward-42	Joined site visit with parks & Garden & Health dept.	MMIC (Health) will rais the issue in MIC Meeting
9	I.C Bane Lane	LR dept is to be Consulted	MMIC (Health) & Councillor Ward - 14
10	Ward - 7	Place to be identified.	MMIC (Health)
11	Ward- 51 (Bally)	Place to be identified.	MMIC (Health) & Secretary HMC will continu the place
12	Ward -45	Place to be identified.	MMIC (H) to consult with Councillor Ward-45
13	1 Place to be identified form Br. LII	Place to be identified.	Goutam Dutta Counciler-19 Brough Chairman -III
14	Dharsa Govt colony , Udbastu Samity Plot-16 Ward No-47	Colony Para under R.R Dept To be confirmed from L&R dept.	MMIC(H)

Members present from Health Dept.

1) MMIC (H&FW)

2)OSD (H)

3) Nodal Officer, NUHM

4) Consultant Epidemiologist, NUHM

COOCH BEHAR MUNICIPALITY

FAX : 03582-222656 COOCH BEHAR PHONE : 03582-222286

Memo No.- Estt/ 2059 /18

Date- 30-01-18

From : The Chairman,
Cooch Behar Municipality,
Cooch Behar.

To : Dr. Tapan Saha,
Nodal Officer. NUHM
Swastha Bhaban,
Salt Lake, Kolkata.

Sub.- Change of site for the work of "CONSTRUCTION OF TWO STORIED BUILDING FOR URBAN PUBLIC HEALTH CENTRE AT KALA BAGAN UNDER NATIONAL URBAN HEALTH MISSION (NUHM) OF COOCH BEHAR MUNICIPALITY IN WARD NO.- 03, COOCH BEHAR".

Sir,

As per letter of The Executive Engineer, Municipal Engineering Dte. Cooch Behar Division, Cooch Behar vide his memo no. ME/COB/704/NUHM-3/15, Pt.-1 dt. 11-07-17, we have selected a location free from all hindrance on the same Road at a distance 150 m of the parent site. The location in particular under discussion has been duly approved by the B.O.C. in its meeting held on 07-08-2017. (Copy enclosed for favour of ready reference).

In this connection the letter of the concerned Agency dt. 10-11-2017 is relevant. (Copy enclosed).

However I am once again forwarding herewith the land schedule of the proposed location.

In this context I would like to point out that in the event of any additional expenditure beyond the budgetary provisions, the Cooch Behar Municipality shall bear the same out of its own fund.

I would therefore request you to kindly convey your permission so that Cooch Behar Municipality could execute the project.

Yours faithfully,

[Signature]
30/01/18

Chairman
Cooch Behar Municipality
Cooch Behar

Date-

Encl : As stated.

No.: Estt / / 1(3) /18

Copy forwarded for information and necessary action to :

- 1) The Director, State Urban Development Agency (SUDA) "ILGUS BHAVAN",H-C Block, Sector-III, Bidhannagar,Kolkata-700106
- 2) The Chief Engineer, M.E. Directorate, Bikash Bhawan, Salt Lake, Kolkata- 700091.
- 3) The C.M.O.H., Cooch Behar.

Chairman
Cooch Behar Municipality
Cooch Behar

OFFICE OF THE COUNCILLORS
COOCH BEHAR MUNICIPALITY
COOCH BEHAR

FAX : 03582-222656

PHONE : 03582-222656

MAIL Id: chairmancbm@gmail.com

Extract form the Proceedings of the Meeting of the B.O.C. held on 07/08/2017:


এজেণ্ডা নং-২০

N.U.H.M. এর অন্তর্গত ৩ নং ওয়ার্ডের Health Centre এর স্থান নির্বাচন সংক্রান্ত আলোচনা ও সিদ্ধান্ত গ্রহণ

সিদ্ধান্ত:

N.U.H.M. এর অন্তর্গত ৩ নং ওয়ার্ডের Health Centre এর স্থান নির্বাচন সংক্রান্ত আলোচনা হয় যে, M.E.D. এর Executive Engineer, Govt. of West Bengal, Cooch Behar Division এর Memo No. ME/COB/704/NUHM-3/15(Pt.-I), date-11.07.2017 অনুযায়ী কিছু Technical অসুবিধার কথা জানিয়েছেন এবং Site Change করার কথা বলেছেন অন্যথায় আগামী এক বছরেও এই Health Centre নির্মাণের কাজ শুরু করা যাবে না। বর্তমানে এই Site এর পাশেই একটি নতুন Reserver তৈরী করা হয়েছে। তাঁর Pipe Line এর কাজটি শুরু করতে অসুবিধা হবে। পুরাতন Reserver টিও ভাঙতে প্রচুর সময় নিচ্ছে এবং ভাঙ্গাও কষ্টকর ব্যাপার হয়েছে।

অদ্যকার সভায় উপরোক্ত অসুবিধার বিষয়টি বিবেচনা করে কলাবাগান ৩ নং ওয়ার্ডের ঐ স্থান পরিবর্তন করে কাছাকাছি অন্য কোন স্থানে স্থানান্তরিকরণের জন্য আলোচনা হয় এবং বিগত ৭ জন বাসিন্দা পৌরসদস্য/সদস্য্য আপত্তি জানিয়েছেন। তারপর সংখ্যাধিক পৌরসদস্য/সদস্য্যগণের সমর্থনে Health Centre টি স্থান পরিবর্তনের সিদ্ধান্ত গৃহীত হয়।



সভাপতি ও পৌরপতি
কোচবিহার পৌরসভা
কোচবিহার

o/c

**GOVT. OF WEST BENGAL
OFFICE OF THE EXECUTIVE ENGINEER
COOCH BEHAR DIVISION
MUNICIPAL ENGINEERING DIRECTORATE
DEPARTMENT OF MUNICIPAL AFFAIRS**

P.O & Dist.- Cooch Behar. PIN - 736101.
Phone: (03582) 230743, E-Mail: coochbehardivnmed@gmail.com

Memo No: ME/COB/ 704 / NUHM-3/15 pt. I

Date: 11.07.2017

From: Executive Engineer,
M. E. Directorate,
Cooch Behar Division.

To :- The Chairman,
Cooch Behar Municipality

Sub: - Proposal for change of site for the work of "Construction of two storied building for Urban Public Health Centre at Kalabagan under National Urban Health Mission (NUHM) of Cooch Behar Municipality (UPHC-I), at ward no - 03, Cooch Behar".

Ref: - (i) Work Order No. PWD/1816/16, Dated 26.12.2016
(ii) Letter of Agency Rana Das dated 11.07.2017

Sir,


In reference to the above mentioned subject and memo, I would like to inform you that a site having a large unused old Over Head Reservoir (OHR) was allotted by your Municipality for construction of the aforesaid health Centre. In this regard, it is verbally communicated to your esteemed office for giving a hindrance free land for construction of the said building. But our appeal was not heard sincerely. Naturally, as a result, already six months has gone from the date of issue of the work order, yet no ray of hope is being seen to avail the site free from all hindrances like completion of demolition of existing huge RCC structure so that the foundation work can be started very soon. The existing structure has been demolished to some extent. But it can easily be predicted that it will be hardly impossible to demolish the existing heavy foundation of the old unused reservoir. Here another problem may appear during excavation of the foundation, since a new OHR and its allied rising main pipeline exists within very close vicinity. If we continue excavation & demolition of the existing foundation of OHR, there will be very much probability to hurt the newly laid pipeline connected with the new OHR at Kalabagan. Again it is to further mention here that if we cannot change the site location right now, it will take probably another more one year to clear the site to start the work.

Hence I would like to request your goodself to allot a comparatively hindrance free land for construction of the building in the greater interest of the public service so far health service to the poor people is concerned.

Thanking You,

Encio: - Letter of the Agency.


Yours faithfully,


Executive Engineer
Cooch Behar Division
M.E. Directorate
Govt. of West Bengal
Dated: 11.07.2017

Memo No: ME/COB/ 704 (1-2), NUHM-3/15 pt. I
Copy forwarded for information to-

1. The Additional Chief Engineer, North, M.E. Directorate, Siliguri.
2. The Superintending Engineer, North Circle, M.E. Directorate, Siliguri.

Yours faithfully,


Executive Engineer
Cooch Behar Division

To
The Chairman,
Cooch-Bihar Municipality,
Cooch-Bihar.

Date:- 10/11/2017.

3794
13.11.17

Ref:- Work of construction of Two storied Building For Urban Public Health Centre at Kalabagan under National Urban Health Mission (NUHM) of Cooch-Bihar Municipality(UPHC-1), in Ward No-3, Cooch-Bihar.

Sub:- Intimation of inability to perform and continue the above works in the schedule Site due to hindrance and objection of the inhabitants of the locality./

Sir,

With reference to above I beg to inform you that I was entrusted to raise construction of two storied building for Urban Public Health Centre at Kalabagan under (NUHM) in Ward No-3, Cooch-Bihar by demolishing an old structure of a concrete made unfinished Reservoir (Water Tank) . The above site is situated in a thickly populated area and there is a School adjacent to the said Site. When I started demolishing of structure of said reservoir with the help of four Vibrators the School Authority as well as the local public raised serious objection due to sound of breaking the same. Ultimately the School Authority fixed two hours time in the morning before starting School and two hours time in the afternoon after over of School hour for resuming works there. In this way it is not possible to carry on piecemeal works there in the said schedule hours. Accordingly I brought the above matter to the notice of the Councillor of Ward No-3 but he could not do any thing. In Cooch-Bihar it is the usual practice of the labours to start work at 10 A.M. and to stop work at 05 P.M . So it is quite impossible on my part to perform works there.

Under the above facts and circumstances I leave the entire matter for your kind consideration and I would pray to you to be kind enough to let me know what future recourses to be taken by me concerning the above works.

Thanking You,

Copy forwarded to:-
The Executive Engineer, M.E.Dte,
Cooch-Bihar Division for information.

Yours Faithfully,

Sri Rana Das


(Sri Rana Das)
Vivekananda Street,
P.O. & Dist: Cooch-Bihar.

COOCH BEHAR MUNICIPALITY

FAX : 03582-222656 COOCH BEHAR PHONE : 03582-222286

DECLARATIONS AND UNDERTAKINGS

1. Certified that the title of proposed land identified for the CONSTRUCTION OF TWO STORIED BUILDING FOR URBAN PUBLIC HEALTH CENTRE AT KALA BAGAN UNDER NATIONAL URBAN HEALTH MISSION (NUHM) OF COOCH BEHAR MUNICIPALITY IN WARD NO.- 03, COOCH BEHAR is in favour of Cooch Behar Municipality.
2. It is undertaken that in the event of any additional expenditure beyond the budgetary provisions, the Cooch Behar Municipality shall bear the same from its own resources.
3. Certified that the proposed location free from all hindrance and encroachment.

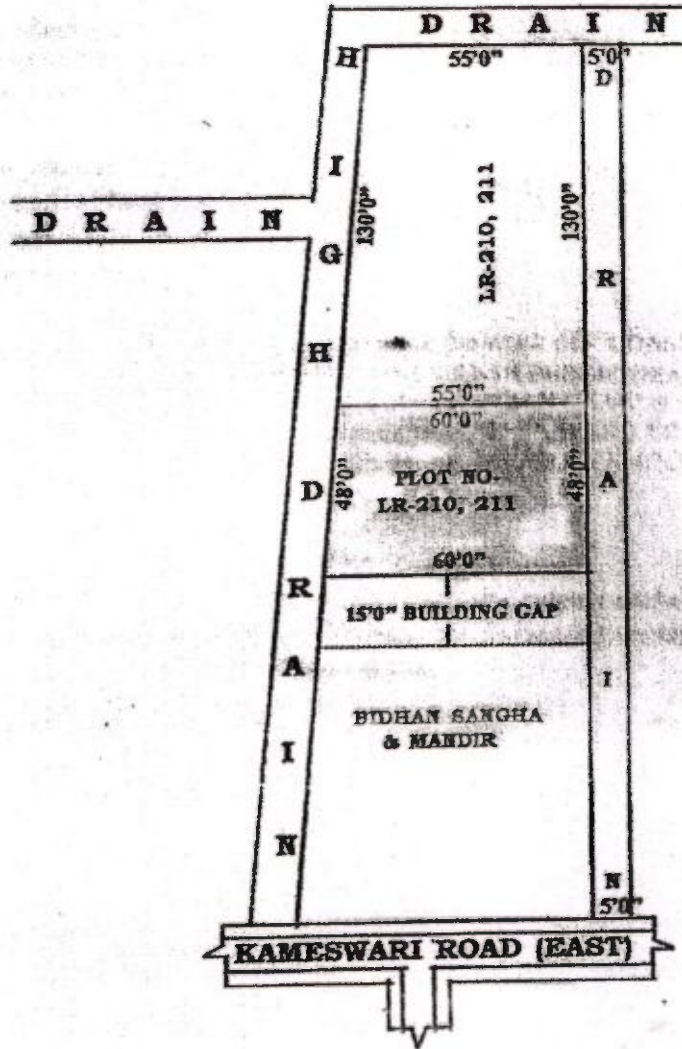


Chairman,
Cooch Behar Municipality,
Cooch Behar.



MOUZA KHARIMALA KHAGRABARI
SHEET NO- 01
J.L NO- 125
RS- NO- 954
P.S.- KOTWALI
DIST- COOCH BEHAR
WARD NO-04 HOLDING NO-

LAND BELONGS TO-
THE CHAIRMAN-
COOCHBEHAR MUNICIPALITY
COOCHBEHAR
P.S.- KOTWALI, DIST. COOCHBEHAR



SCHEDULE OF THE LAND AS PER PRESENT POSSESSION

TOUZI NO	KH NO	TOTAL LAND	TOTAL RENT	PLOT NO	NAME OF POSSESSOR	KH NO	PLOT NO	PARTICULARS OF LAND			
								ACRES	B-K-D	SQFT	COLOUR
IR NIL	IR NIL	IR NIL	IR NIL	IR 210 211	CHAIRMAN COOCHBEHAR MUNICIPALITY	IR NIL	IR 210 211	.066	0-4-0	2880	

DRAWN BY-
FRANAY DEB (AMIN)

Drawn by:-
Personel Dept.
Amin

7/9/2017

(Signature)
12/09/17

Chairman
Cooch Behar Municipality
Cooch Behar

Monthly reporting format for Monitoring of construction works under NUHM

Reporting for the month Feb-18

Name of District: Howrah		Financial Progress (Rs. in Lakh)										Physical Progress																
FMR Code	Name of ULB	Name of U-CHC / MH with address and Ward No.	Whether Sanctioned for Renovation / New Construction	Year of sanctioned	Amount sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Expenditure for the month (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at		Preparation of plan estimate (Yes/No)	Plan estimate submitted to MED for vetting (No.)	Plan estimate vetted by MED (No.)	Plan estimate approved by DH&FWS (No.)	Tender process completed (Yes/No)	Whether work order issued (Yes/No)	Construction completed up-to 10%	Construction completed up-to 25%	Construction completed up-to 40%	Construction completed up-to 55%	Construction completed up-to 70%	Construction completed up-to 85%	Construction completed up-to 100%	Whether functional or not (Yes/No)			
										ULB level (Rs. in Lakh)	DH&FWS (Rs. in Lakh)															Total unspent (Rs. in Lakh)		
1	2	3	4	5	6	7	8	9	10	11	12	13-11-12	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	
040301	Howrah Corporation	19, Saiya Narayan Temple Road, Sakia, Howrah - 6, Ward No. 4	NC	2015-16	75					11	12																	
		55, A. Naskar Para Road, Howrah - 7, Ward No. 2	NC	2015-16	75																							
		102, I.R. Bhalous Lane, Howrah - 1, Ward No. 19	NC	2015-16	75	25																						
		Priya Nath Ghosh Lane, Howrah, Ward No. 42	NC	2015-16	75																							
		17, Sita Nath Bose Lane, Howrah - 6, Ward No. 10	NC	2015-16	75	25		11.69																				
		14, Debendra Ganguly Road, Howrah, Ward No. 40	NC	2015-16	75																							
		9, Kapakur Lane, Howrah, Ward No. 32	NC	2015-16	75																							
		Banlom Park, Panchananale Road, Howrah, Ward No. 18	NC	2015-16	75																							
		1, I.C. Bose Road, Howrah, Ward No. 14	NC	2015-16	75																							
		Place not yet identified	NC	2015-16	75																							
		Place not yet identified	NC	2015-16	75																							
		Place not yet identified	NC	2015-16	75																							
		36, Banlom Bahar Ghosh Lane, Howrah, Ward No. 36	NC	2014-15	75																							
		273, G.T. Road, Muza Barampara, Howrah, Ward No. 02	NC	2014-15	75	25																						
						185			110.17		60.83																	
						185			110.17		60.83																	

** Mention "R" for Renovation, "NC" for New Construction and "U" for Upgradation in Column No. 4

Guidelines for reporting of physical progress noted below:

Sl. No.	Indicators for monitoring of Physical Progress	Description of Percentage (for New Construction only)
1	Construction completed upto 10 %	Earth work, excavation and materials procurement up to Plinth level
2	Construction completed upto 25 %	Foundation up to Plinth level
3	Construction completed upto 40 %	Structural work up to roof level
4	Construction completed upto 55 %	Structural work with brick work and plastering
5	Construction completed upto 70 %	Total finishing work
6	Construction completed upto 85 %	S&P and electrical work completed
7	Construction completed upto 100 %	Full finishing and ready to handed over

Swagata Mukherjee
06/02/18

S.A.E. HMC/18

FMR Code	Name of ULB	Name of U-CHC / MH with address and Ward No.	Whether sanctioned for Renovation / New Construction	Year of sanction	Amount sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Financial Progress (Rs. in Lakh)										Physical progress										Whether functional or not (Yes/No)
							Fund Released to ULB (Rs. in Lakh)	Expenditure for the month (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB level (Rs. in Lakh)	DH&F WS (Rs. in Lakh)	Total unspent (Rs. in Lakh)	Preparation of estimate plan (Yes/No)	Plan estimate submitted to MED for vetting (No.)	Plan estimate vetted by MED (No.)	Plan estimate approved by DH&FWS (No.)	Tender process completed (Yes/No)	Whether work order issued (Yes/No)	Construction completed up-to 10%	Construction completed up-to 25%	Construction completed up-to 40%	Construction completed up-to 55%	Construction completed up-to 70%	Construction completed up-to 85%	Construction completed up-to 100%		
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	
		UPHC 1, 55, Saeed Narayan Nath Ganguly Road, Howrah - 4, Ward	R	2013-14	10	10	10	0	9.93	0.07	0.07	0.07	Yes				Yes	Yes								100%	Yes
		UPHC 2, 18, Jaiscans Lane, Sakla, Howrah - 1, Ward No. 15	R	2013-14	10	10	10	0	9.78	0.24	0.24	0.24	Yes				Yes	Yes								100%	Yes
		UPHC 3, 729/128, Sankha Pukur Lane, Howrah - 2, Ward No. 15	R	2013-14	10	10	10	0	9.82	0.18	0.18	0.18	Yes				Yes	Yes								100%	Yes
		UPHC 4, 56, F. Road, Belgachia Howrah - 1, Ward No. 8	R	2013-14	10	10	10	0	9.91	0.09	0.09	0.09	Yes				Yes	Yes								100%	Yes
		UPHC 5, 183, G. T. Road, Howrah - 2, Ward No. 31	R	2013-14	10	10	10	0	9.81	0.19	0.19	0.19	Yes				Yes	Yes								100%	Yes
		UPHC 6, 21, Round Tank Lane, Howrah - 1, Ward No. 29	R	2013-14	10	10	10	0	9.91	0.09	0.09	0.09	Yes				Yes	Yes								100%	Yes
		UPHC 7, Malher Para, Uman, Howrah - 302, Ward No. 48	R	2013-14	10	10	10	0	9.82	0.18	0.18	0.18	Yes				Yes	Yes								100%	Yes
		UPHC 8, 827/2, Naranangis Dada Road, Howrah - 1, Ward No. 24	R	2013-14	10	10	10	0	9.81	0.19	0.19	0.19	Yes				Yes	Yes								100%	Yes
		UPHC 9, 37, Buzarh Road, Howrah - 10, Ward No. 41	R	2013-14	10	10	10	0	9.94	0.06	0.06	0.06	Yes				Yes	Yes								100%	Yes
		PP- VIII Building, Kadamah Ananya Bhawan, Bally ESPGD Building, Rajes Saha Lane, Bally	R	2014-15	10	10	10	0	9.77	0.23	0.23	0.23	Yes				Yes	Yes	95%							100%	Yes
		Prices not yet identified ---	R																								
		PP- VII Building, Kumarpore, Uda	R	2014-15	10	10	10	0									Yes	Yes								99%	Yes

HOWRAH



GOVERNMENT OF WEST BENGAL
OFFICE OF THE DISTRICT HEALTH & FAMILY WELFARE SAMITI
11, DR. P. K. BANERJEE ROAD, LICHUBAGAN, HOWRAH - 711101
TELE-FAX: 26412074 / 1805, URL: www.healthyhowrah.org
E-MAIL: cmoh_hwh@wbhealth.gov.in / cmoh.how@gmail.com

No: DHFWS/ HOW/ 160/18

Date: 12/1/18

To:
The Additional Mission Director (NHM)
Government of West Bengal
Department of Health & Family Welfare
Swasthya Bhawan, Kolkata


Sub:- Construction of Different Health Units at the Land of Department of Health & Family Welfare at 16, Debendra Ganguly Road, Howrah
Ref:- HFWS/NUHM488/2015/3279 dated 18/12/2017 of the Additional Mission Director (NHM)

Respected Sir,

Kindly refer the above; as directed, various information regarding the land at 16, Debendra Ganguly Road, Howrah are given below:

1. Land details: Area - 28 katha more or less, Mouza- Shibpur, Daag No: 107 (Report from the L&LR Deptt and sketch are enclosed herewith, Annex-I). Land is recorded in the name of Health & Family Welfare Department and has been made free from all encumbrances in the year of 2014.
2. Build up area of present structure: G+1 storied building structure having 5,699.49 sqft buildup area more or less (site plan of the buildup area prepared by the PWD is enclosed, Annex-II). The site has been visited by the CMOH, MMIC (Health) HMC, Engineers of PWD, HMC, DPMU. "Present building is very old one and dilapidated in such manner that is beyond economic repair & renovation may cause any casualty at any moment so it requires urgent demolition" (The inspection report of the Executive Engineer, PWD, Howrah Construction Division is enclosed, Annex-III)
3. The foundation of G+3 building is proposed. Yes there is a scope for further vertical extension. The proposed layout prepared by the Engineers of HMC & DPMU is enclosed herewith (Annex-IV). As decided, the land will be utilized for setting up of U-PHC (NUHM) & Store by HMC and ACMOH (Howrah Sadar) Office & Sub-Divisional Store by H&FW Deptt and Office of Howrah District Drugs Control by Directorate of Drugs Control.
4. At present, 28% has been earmarked as ground coverage / FAR. However, 20-25% (approx) ground coverage may be extended.

With regards,
Yours faithfully,


Chief Medical Officer of Health
Howrah


Annexures: I, II, III & IV

No: DHFWS/ HOW/ 160/18 (12) / 18

Date: 12/1/18

Copy forwarded for kind information and taking necessary action to:

1. The Mayor, Howrah Municipal Corporation
2. The Mission Director (NHM) & Secretary, Deptt of H&FW, Govt of WB
3. The Director of Health Services & e.o. Secretary, Deptt of H&FW, Govt of WB
4. The Director, Directorate of Drugs Control, Govt of WB
5. The District Magistrate, Howrah
6. The Commissioner, HMC
7. The Nodal Officer, NUHM, Deptt of H&FW, Govt of WB
8. The MMIC, Health, HMC
9. The Dy CMOH-I, Howrah
10. The Assistant Director of Drugs Control, Howrah


Howrah

পশ্চিমবঙ্গ সরকার
সমষ্টি ভূমি ও ভূমি সংস্কার আধিকারিকের করণ
হাওড়া টাউন সার্ভে ইউনিট, হাওড়া

- দাগের তথ্য -

০৫১৫২৪২

জিলা- হাওড়া

ব্লক - হাওড়া টাউন সার্ভে ইউনিট

থানা- শিবপুর

সীমা- শিবপুর শীট - ১৪২

জে.এল.নং- ১

দাগ নং- ১০৭

শ্রেণী- বাস্তু

জমির পরিমাণ(এ)- ০.৪২০৮

সাদেক দাগ নং- ৯৬

খতিয়ান নং শ্রেণী

অংশ অংশ পরিমাণ(এ) রায়তের বিবরণ মন্তব্য

৯৬

০.৫০০০

০.২১০৮

কনকপ্রভা দেবী
স্বামী-ব্রজহরি
সাং-১৬ নং দেবেন্দ্র গাজুলী রোড

১৬ নং দেবেন্দ্র গাজুলী রোড,

টালি-১, দোতাল্লা দালান-১

৪৮৯

০.৫০০০

০.২১০৮

লিলিম কুমার রায় চৌধুরী
পিতা-জয়হরি
সাং-১৬ নং দেবেন্দ্র গাজুলী রোড

১৬ নং দেবেন্দ্র গাজুলী রোড,

টালি-১, দোতাল্লা দালান-১,

প্রঃ স্বস্ত্য দক্ষতর (পলিক্লিনিক)

১.০০০০

০.৪২০৮

For office use only

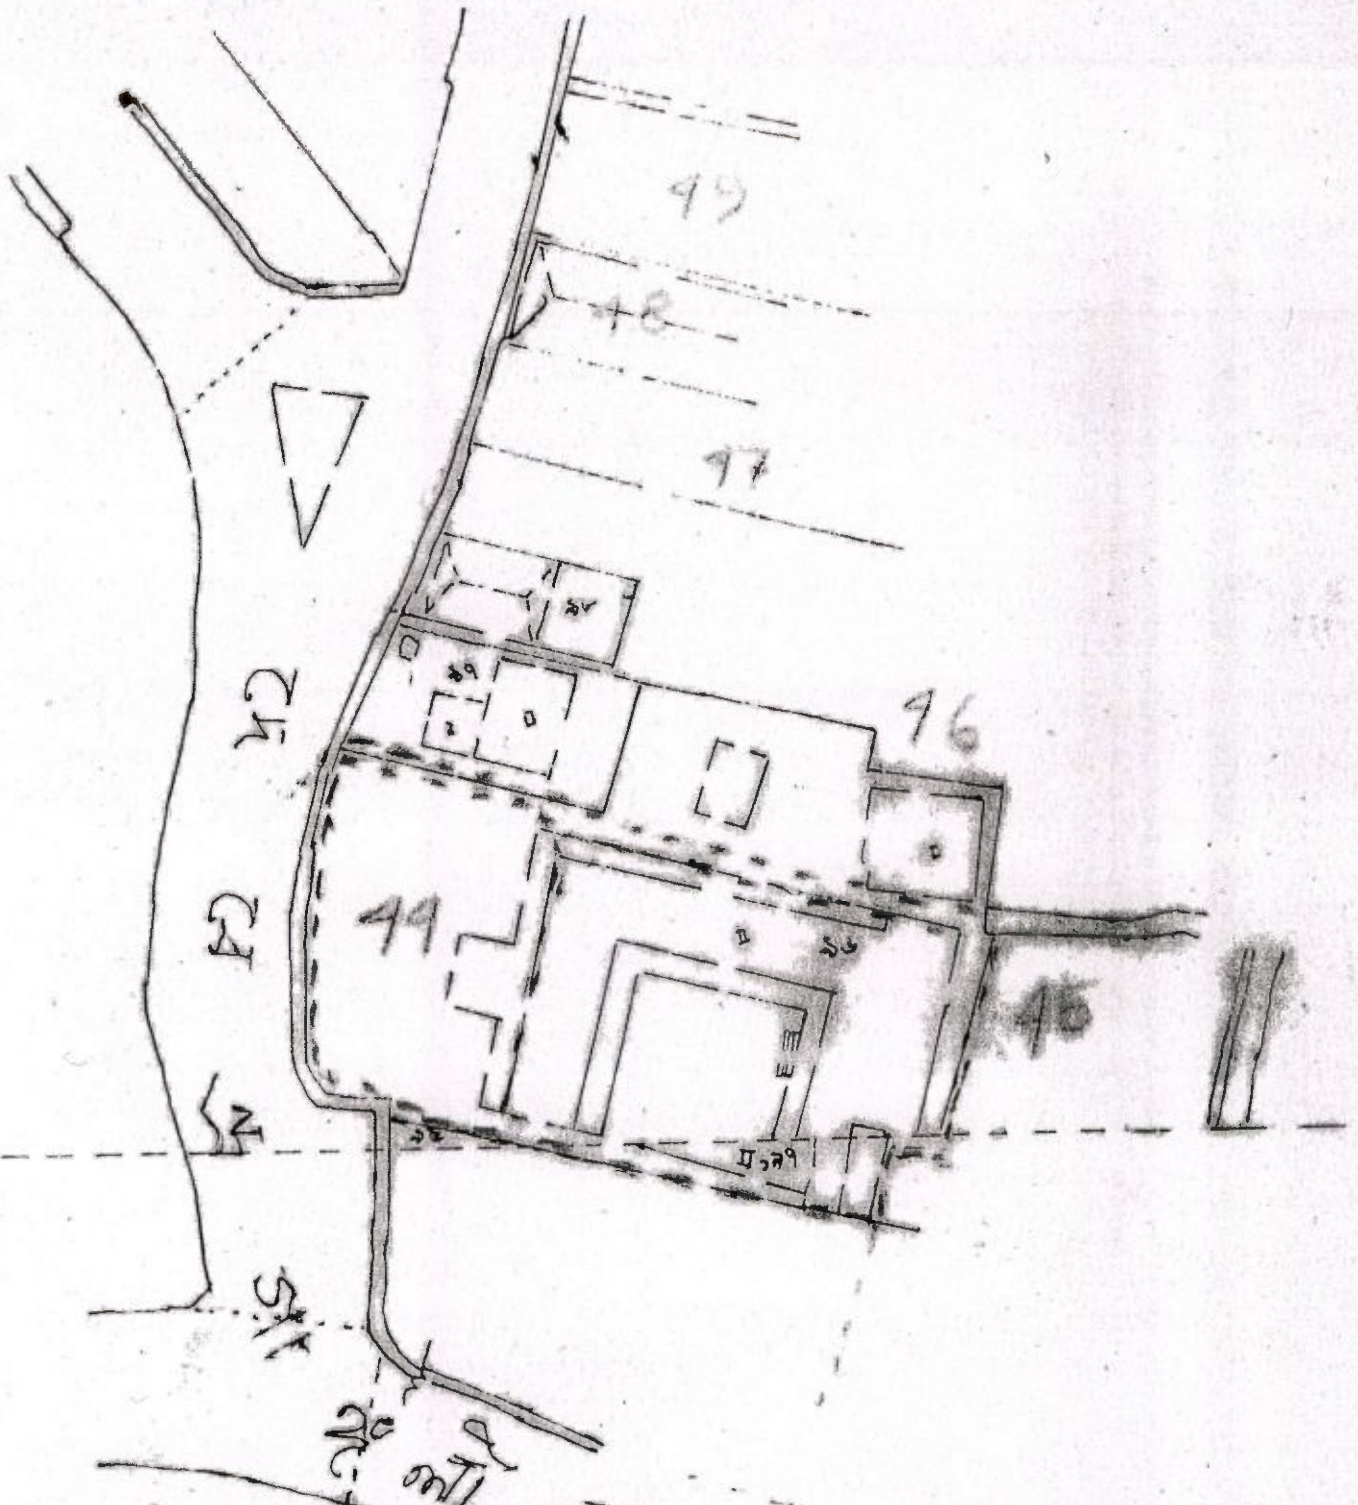
As per instruction of ADM & HLRD

Ref: ১ C.M.O.H, Howrah Office Memo addressed to (ADM & HLRD)

DHFG/NOH/470/14

dt 26/5/14

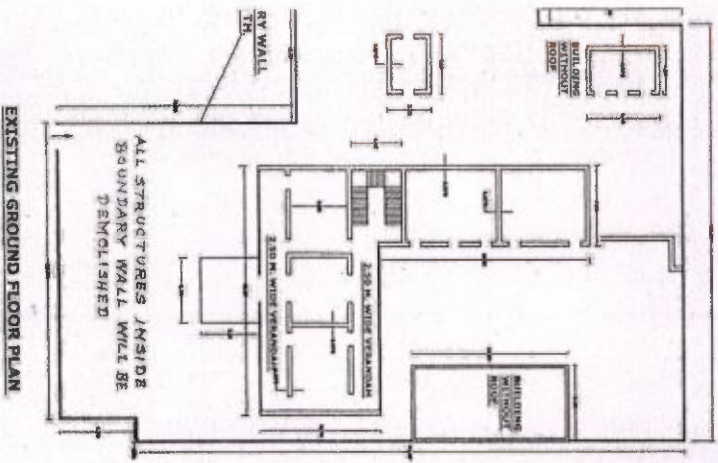
ভোজা জিবপুর ডিবিং = ১৪২



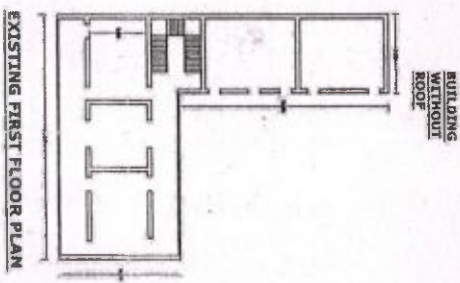
জিবপুর ডিবিং - ১৫০

জিবিং রোড

**THE PLAN FOR PROPOSED CONSTN. OF DISTRICT
ADMINISTRATIVE HEALTH OFFICE AT THE PREMISES
16, DEBEN GANGULY ROAD, HOWRAH**



EXISTING GROUND FLOOR PLAN



EXISTING FIRST FLOOR PLAN

[Signature]
 ASSISTANT ENGINEER
 CONSTN. SUB-DIVN.-I

[Signature]
 ASSISTANT ENGINEER(PWD)
 HOW. CONSTN. SUB-DIVN.-I

[Signature]
 EXECUTIVE ENGINEER(PWD)
 HOW. CONSTN. DIVN.



2762
06/06/14

AG 2014
06/06/14

GOVERNMENT OF WEST BENGAL
OFFICE OF THE EXECUTIVE ENGINEER (PWD)
HOWRAH CONSTRUCTION DIVISION
2, MAHATMA GANDHI ROAD (1st Floor)
HOWRAH-711101, Phone-033-26414776

NO - 997

Date - 06.06.2014

To
The Chief Medical Officer Of Health
Howrah

Sub :- Request for taking necessary steps for Construction of District Administrative Health Office at the Premises of 16, Deben Ganguly Road, Howrah.

Ref :- His memo no - DHFWS/How/474/14 dt - 26/05/2014.

In reply to your above memo regarding the subject in caption where in my opinion sought for whether the existing structure situated at the premises of land of around 28 Katha wherein the proposed office will be constructed is habitable or require to dismentle.

After inspection of the building on 23.05.14 it is clear that the building is very old one and dilapidated in such manner that is beyond economic repair & may cause any casualty at any moment. So it requires urgent dimolisation.

Executive Engineer (PWD)
Howrah Construction Division

Copy forwarded for information & necessary action to :
1. Assistant Engineer, Howrah Construction Division - I, PWD.

Executive Engineer (PWD)
Howrah Construction Division



GOVERNMENT OF WEST BENGAL
OFFICE OF THE DISTRICT HEALTH & FAMILY WELFARE SAMITI
11, DR. P. K. BANERJEE ROAD, LICHUBAGAN, HOWRAH - 711101
TELE-FAX: 26412074 / 1805, URL: www.healthyhowrah.org
E-MAIL: cmoh_hwh@wbhealth.gov.in / cmoh.how@gmail.com

No: DHFWS/ HOW/ 2133/17

Date: 25/08/17

To:
The Additional Mission Director (NHM)
Government of West Bengal
Department of Health & Family Welfare
Swasthya Bhawan, Kolkata

Sub:- Construction of Different Health Units at the Land of Department of Health & Family Welfare at 14, Debendra Ganguly Road, Howrah

Ref:- HFW/NUHM488/2015/1070 dated 27/06/2017 of the Additional Mission Director (NHM)

Respected Sir,

Kindly refer the above and apropos the discussions took place on 5th April 2017 at the Office Chamber of the DHS & consecutively on 27th June 2017 at the Office Chamber of the Additional Mission Director (NHM), Swasthya Bhawan in presence of the CMOH, Howrah, MMIC (Health), HMC, OSD (Health), HMC & DPC, Howrah, the land of around 28 katha holding by Deptt of H&FW at 14, Debendra Ganguly Road, Howrah will be utilized by setting of different health units of Deptt of H&FW, Howrah Municipal Corporation and Director of Drugs Control.

As decided, the land will be utilized for setting up of U-PHC (NUHM) & Store by HMC and ACMOH (Howrah Sadar) Office & Sub-Divisional Store by H&FW Deptt and Office of Howrah District Drugs Control by Directorate of Drugs Control. The undersigned was directed to submit a sketch map demarcating the land for setting up different facilities/offices which has been prepared by the Engineers of Howrah Municipal Corporation & National Health Mission (DPMU) jointly. The said sketch is enclosed herewith for your kind perusal.

With regards,

Yours faithfully,

Chief Medical Officer of Health
Howrah

Enclosure: The sketch

No: DHFWS/ HOW/

Date:

Copy forwarded for kind information and taking necessary action to:

1. The Mission Director (NHM) & Secretary, Deptt of H&FW, Govt of WB
2. The Mayor, Howrah Municipal Corporation
3. The Director of Health Services & e.o. Secretary, Deptt of H&FW, Govt of WB
4. The Director, Directorate of Drugs Control, Govt of WB
5. The Commissioner, HMC
6. The District Magistrate, Howrah
7. The MMIC, Health, HMC
8. The Dy CMOH-I, Howrah
9. The Assistant Director of Drugs Control, Howrah
10. The OSD, Health, HMC



Dr. Rathin Chakravarty

MAYOR

HOWRAH MUNICIPAL CORPORATION

4, Mahatma Gandhi Road, Howrah-711 101
Ph. (Office) : 2641 1332, 2638 3211-13 Ext. 201
Fax : (091-33) 2641 2114
E-mail : hmc.mayor@gmail.com

Residence :
5, Subal Koley Lane
Howrah-711 101
Phone (R) : 2638 2409

Ref. No. **MYR-08/17-18**

Date **02/05/2017**

To
The Mission Director(NHM) & Secretary,
Dept. Of H & FW
Govt. Of W.B.

**SUB : CONSTRUCTION OF DIFFERENT HEALTH UNITS AT THE LAND OF DEPARTMENT
OF HEALTH & FAMILY WELFARE AT 14, DEBENDRA GANGULY ROAD, HOWRAH.**

Dear Mission Director,

As per discussion in the meeting on 05/04/2017 at the chamber of D.H.S & E.O., Secretary, Department of Health and Family Welfare, Government of West Bengal, it was decided that at 14, Debendra Ganguly Road, Howrah (land of 28 katha) a new set-up will be constructed, where a set-up of proposed UPHC(NUHM) with a store of Health dept, Howrah Municipal Corporation will be located, The office of ACMOH (Howrah Sadar) and Sub-Divisional store of Health & Family Welfare will also be constructed thereon. Rest portion will be kept vacant for further use.

For that reason, we are seeking permission from your end to build the construction at that spot. Henceforth, it is also proposed that the plan of the construction-site may be prepared by the engineering department of Howrah Municipal Corporation.

In this context, I am also to inform that the total cost may be borne by both the departments (Howrah Municipal Corporation and Department of Health & Family Welfare, Government of West Bengal).

Please release your portion of fund as early as possible to make this joint project a grand success in near future.

Sincerely

Mayor
Howrah Municipal Corporation

Ref.No.MYR-08/(1-8)/17-18

Date : 02/05/2017

Copy forwarded for kind information and necessary action to:

1. The Additional Chief Secretary, Dept of H&FW, Govt of WB.
2. The Director of Health Services & E.O. Secretary, Dept of H&FW, Govt of WB.
3. M.M.I.C. (H &FW), H.M.C
4. The District Magistrate, Howrah
5. The Commissioner, HMC
6. The Joint DHS, Planning & Development, Swasthya Bhawan, Kolkata.
7. The CMOH, Howrah.
8. Office Copy.

Mayor
Howrah Municipal Corporation

0338/m at 24/04/17

Dr. S. N. Misra 02/M/14/H & FW at 28/04/17



OSD(H)
P.I. Bagchi 26-04-17

GOVERNMENT OF WEST BENGAL
OFFICE OF THE DISTRICT HEALTH & FAMILY WELFARE SAMITI
11, DR. P. K. BANERJEE ROAD, LICHUBAGAN, HOWRAH - 711101
TELE-FAX: 26412074 / 1805, URL: www.healthyhowrah.org
E-MAIL: cmoh_hwh@wbhealth.gov.in / cmoh.how@gmail.com

No: DHFWS/ HOW/ 923/17

Date: 20/4/17

হাওড়া মিউনিসিপাল কর্পোরেশন
কেন্দ্রীয় স্বাস্থ্য অফিস
23 APR 2017
10279
স্বাস্থ্য অফিস হাওড়া ১০২৩ জিলা

MMS (H)
25/04/17

To: The Mayor,
Howrah Municipal Corporation

Sub:- Construction of Different Health Units at the Land of Department of Health & Family Welfare at 14, Debendra Ganguly Road, Howrah

Respected Sir,

Apropos the discussion took place on 5th April 2017 at the Office Chamber of the DHS & e.o. Secretary, Deptt of H&FW, Govt of WB, Swasthya Bhawan in presence of the CMOH, Howrah, MMIC (Health), HMC, OSD (Health), HMC & DPC, Howrah, the land of around 28 katha holding by Deptt of H&FW at 14, Debendra Ganguly Road, Howrah will be utilized by setting of different health units of Deptt of H&FW and Howrah Municipal Corporation.

As directed by the DHS, one portion of land will be utilized for setting up of U-PHC (NUHM) & Store by HMC and ACMOH (Howrah Sadar) Office & Sub-Divisional Store by H&FW Deptt and rest portion of the land must be kept vacant for future use by the Deptt. On usable part, a building has to be constructed vertically with the provisions of all health units, stores, offices of both Deptt of H&FW & HMC. Necessary fund for construction of the building and different units will be arranged by HMC & Deptt of H&FW jointly. HMC will bear the cost for construction of U-PHC & Store and proposal for funding of the rest of the health units will be placed to the Deptt of H&FW by its own.

It has also been discussed in the said meeting that HMC will place a proposal to the Mission Director (NHM) & Secretary, Deptt of H&FW, Govt of WB with an intimation to the DHS & e.o. Secretary, Deptt of H&FW, Govt of WB. Afterwards detailed project report including plan, estimate with drawing will be prepared by the Engineering Section of the HMC and if approved, the construction work will be executed by them. This is for your kind information and taking necessary action please.

With regards,

Yours faithfully,

[Signature]
20/4/17

Chief Medical Officer of Health
Howrah

Date:

No: DHFWS/ HOW/

Copy forwarded for kind information and taking necessary action to:

1. The Mission Director (NHM) & Secretary, Deptt of H&FW, Govt of WB
2. The Director of Health Services & e.o. Secretary, Deptt of H&FW, Govt of WB
3. The Commissioner, HMC
4. The District Magistrate, Howrah
5. The MMIC, Health, HMC
6. The Dy CMOH-I, Howrah
7. The OSD, Health, HMC
8. The DPMU, Howrah

Chief Medical Officer of Health
Howrah



West Bengal Procurement System of Government of West Bengal

Tenders

AOC Summary

Date : 05-Feb-2018 05:29 PM

Print

Organisation Chain	MUNICIPAL AFFAIRS DEPARTMENT URBAN LOCAL BODIES KANDI
Tender ID	2017_MAD_114742_1
Tender Ref No	MAD/ULB/KANDI/ NleT-22 (3rd Call)
Tender Title	Construction of P.H.C. Building
Cover System	2

Contract Date	05-Feb-2018
Contract Value	INR 5227611.00
Work Completion Period (in days)	180
AOC document	AOC.pdf (943.00 KB)
AOC Description	Award of Contract

Awarded Bids List

S.No	Bid Number	Bidder Name	Awarded Currency	Awarded Value
1	620305	KANDURIA JANATA CO-OP LABOUR CONT AND CONST SOC LTD	INR	5227611.00

Congratulations! You have been awarded the contract for this tender.

Tender Inviting Authority

Office of the Board of Councillors of
Kandi Municipality
Kandi, Murshidabad

Date: 05/02/18

Memo No. 5013/III-K.M/2018

From
The Chairman
Kandi Municipality
Kandi, Murshidabad.

To
The Secretary
Kanduria Janata Co-op. Labour Contract & Construction Society Ltd.
Vill.- Kanduri, P.O.- Eroali, P.S.- Khargram, Dist.- Murshidabad
PIN- 742147

Ref:
1) N.I.eT No- MAD/ULB/KANDI/ NleT-22 (3rd Call)
2) Memo No. -2320/III-K.M./NleT/2017 Dated: 03/06/2017
3) Tender ID No.- 2017_MAD_114742_1

Sub: Acceptance cum work order for the work of "Construction of P.H.C. Building within Kandi Municipality, P.O.- P.S-Kandi, Dist.-Murshidabad, West Bengal, PIN-742137".

Work Order Amount: Rs. 52, 27,611.00 (Rupees Fifty two Lacs Twenty Seven Thousands Six Hundred and Eleven only)

This is to inform you that, the rate quoted by you against above stated NIT No. and Bid Call for the above mention work have been accepted by the undersigned on behalf of the board of councilors of the Kandi Municipality. You are requested to take up the work for construction of the same after execution of formal agreement and in consultation with the Engineer of Kandi Municipality and Engineer-in-Charge, MEDTe. Berhampore Division.

You are also requested to meet the undersigned to execute the formal agreement (3 Copies) within 5 days.

The construction work has to be completed within the stipulated time as mentioned in above stated NIT under supervision of the Municipal Engineering Director Authority thereof. The payment will be made with reasonable time as per standard norms.

Chairman,
Kandi Municipality.

Date: KANDI MUNICIPALITY

No.

Copy forwarded for information and necessary action to :

1. The Chief Engineer, M.E. Directorate, Bikash Bhawan, Salt Lake City, Kol- 700 091
2. The Superintending Engineer, Central Circle, M.E. Directorate. Malda.
3. The Executive Engineer, Berhampore Division, M.E.Dte. Berhampore
4. The Executive Officer, Kandi Municipality.
5. The Sub-Assistant Engineer, Kandi Municipality.
6. The Accountant Kandi Municipality.

Chairman,
Kandi Municipality.

Signature valid

Digitally signed by SANTANA ROY
Date: 2018.02.05 17:27:32 IST
Location: West Bengal

Resolution of Bi-monthly Review Meeting on NUHM with the representatives of ULBs and Districts Health Officials:

State level bi-monthly NUHM meetings to review the implementation status of National Urban Health Mission (NUHM) were held on 13.09.2017, 14.09.2017 and 15.09.2017 with the representatives of ULBs and Districts Health Officials. Addl. Secretary & Addl. Mission Director-NHM, Health & Family Welfare Department, Government of West Bengal chaired the meetings. The Districts and Urban Local Bodies (ULBs), who were present in the meeting are listed below:

Date of Meeting	District	Name of ULB participated	Place of Meeting	Participants List
13.09.2017	Bankura, Birbhum, Bishnupur HD, Diamond Harbour HD, Jhargram, Howrah, Nandigram HD, Paschim Bardhaman, Paschim Medinipur, Purba Bardhaman, Purba Medinipur, Purulia, Rampurhat HD, South 24 Parganas	Bankura Bolpur Suri Bishnupur Howrah MC Uluberia Contai Asansol MC Durgapur MC Ghatal Kharagpur Medinipur Burdwan Kalna Haldia Panskura Tamluk Purulia Rampurhat Baruipur Budge Budge Maheshtala Rajpur Sonarpur	2 nd floor Auditorium Hall, Swasthya Bhawan	Anne.-I
14.09.2017	Hooghly, Murshidabad, Nadia	Arambag Baidyabati Bansberia Bhadreswar Champdany Chandernagore MC Dankuni Hooghly Chinsurah Konnagar Rishra Serampore Uttarpara Kotrang Berhampur Dhulian Jangipur Jiaganj-Azimganj Chakdah Gayeshpur Haringhata	2 nd floor Conference Hall, Institute of Health & Family Welfare	Anne.-II

Date of Meeting	District	Name of ULB participated	Place of Meeting	Participants List
		Kalyani Krishnagar Nabadwip Ranaghat Santipur		
15.09.2017	Basirhat HD, North 24 Parganas	Baduria Basirhat Bangaon Baranagar Barasat Barrackpore Bhatpara Bidhannagar MC Dum Dum Garulia Habra Halisahar Kamarhati Kanchrapara Khardah Madhyamgram Naihati New Barrackpore North Dum Dum Panihati South Dum Dum Titagarh	2 nd floor Conference Hall, Institute of Health & Family Welfare	Anne.-III
22.09.2017	Alipurduar, Cooch Behar Dakshin Dinajpur Darjeeling Jalpaiguri Maida Uttar Dinajpur	Alipurduar Cooch Behar Balurghat, Gangarampur, Darjeeling, Siliguri MC Jalpaiguri English Bazar, Old Maida Islampur, Kaliaganj, Raiganj	WBSWAN of respective Districts	NA

Performances of ULBs were reviewed and following decisions were taken.

- 1) Out Patient Department (OPD) patient load has significantly increased in all districts except Diamond Harbour HD, South 24 Parganas, Purba Burdwan, Purulia, Murshidabad, Alipurduar, Cooch Behar etc. When reviewed ULB wise patient load, it was also observed that there is a significant increase of patient load in all the ULBs except Suri, Uluberia, Hooghly Chinsurah, Uttarpara Kotrung, Basirhat, Kanchrapara and North Barrackpore Municipality. These poor performing ULBs were requested to make necessary arrangement so that patient load increase at OPD. The activity which were suggested to increase the OPD load were proper IEC, regular OPD, strictly maintenance of OPD hours and regular supply of medicine.
- 2) All concerned were requested to start the U-PHCs those are non functional either in a rented house or in one of the Sub-centres of the selected U-PHC by October 2017.

- 3) Keep sufficient stock of medicine in all ULBs and U-PHCs to meet up any extra demand for post flood situation or ensuing puja festivals.
- 4) CMOHs were requested to ensure that all ULBs have submitted their UHND Micro-plan. ULBs will submit Micro-plan for Special Outreach by 20th of every month. District Health Officials will supervise the Special Outreach session according to Micro-plan.
- 5) ULBs will make provision for advance for conducting UHND and Special Outreach Camps and book the expenses in monthly FMR after making necessary adjustment.
- 6) It is reported by most of the Municipalities and Municipal Corporations, specially the ULBs in North 24 Parganas & Hooghly that the involvements of ICDS worker were poor during conducting UHNDS from ICDS Centre. CMOHs of the Districts were requested to sensitize the District Project Officers (ICDS), so that AWW get involved in conducting UHND at AWC.
- 7) For construction of new U-PHC it is reported that in 28 places tender process for new constructions have been completed but construction work are not yet started. The concerned ULBs were requested to initiate the construction of these new U-PHC buildings within November, 2017. **ULBs were also requested to complete all renovation work of U-PHCs by October, 2017.**
- 8) Arrangement are to be done for making payment of R/A Bills (Running Bill) according to physical progress of construction work.
- 9) CMOHs will publish advertisement for recruitment of Lab-Technicians, Staff Nurse with immediate effect so that the recruitment process might be completed by November, 2017.
- 10) It was observed that in number of places, Lab. Technicians are in position but laboratories are not functional for lack of infrastructure. All concerned were requested to take immediate measure so that the laboratories can start functioning by November 2017. Districts were requested to complete all formalities so that the ULBs can procure lab-equipment and other consumables to make their laboratories functional.
- 11) Districts are to send information regarding formation of MAS to the state in prescribed format by September 2017 and complete the district level training by October 2017.
- 12) ULBs were requested to put at least one IEC material of National Urban Health Mission (NUHM) at each of the Duga Puja pandal of their jurisdiction.

Meetings were concluded with thanks from and to the chair and all concerned were requested to take necessary steps as per resolution the meeting.

Anand Chakraborty
Addl. Secretary &
Addl. Mission Director, NHM
West Bengal

STATE URBAN DEVELOPMENT AGENCY**HEALTH WING
"ILGUS BHAVAN"****H-C BLOCK, SECTOR-III, BIDHANNAGAR, CALCUTTA-700 091
West Bengal**Ref No. **SUDA-Health/NUHM/421/15/310(27)**Date **31.01.2018****From : Director, SUDA****To : The Commissioner,
Howrah / Siliguri Municipal Corporation****To : The Chairman,****Alipurduar/Bankura/Bishnupur/Raipurhat/Suri/Bolpur/Cooch Behar/
Balurghat/Dankuni/Arambagh/Jalpaiguri/Old Malda/Berhampore/
Dhulian/Jangipur/JiaganjAzimganj/Kandi/Kalyani/Nabadwip/Santipur/
Chakdah/Gayeshpur/Haringhata/ Ranaghat/Purulia Municipality****Sub. : Meeting at SUDA on 06.02.2018 at 11 am w.r.t. status of
New Construction of U-PHCs under NUHM.****Sir / Madam,**

You are aware that 155 no. of U-PHCs have been approved for 88 ULBs under NUHM by the Govt. of India. The last review meeting with the ULBs on construction status of U-PHCs by NUHM, DHFW was held at Swasthya Bhawan from 20 to 22 November, 2017.

It is informed by the Addl. Mission Director, NHM that new construction of U-PHCs under NUHM in a no. of ULBs either not started or not progressing as per desired level.


Hence, a meeting will be held at SUDA Conference Hall on **06.02.2018 from 11 a.m. to 1 p.m.** to expedite the progress in this regard. ULB wise new construction status of U-PHCs is enclosed herewith.

You are requested to depute Executive Officer of the ULB and the person concerned who is responsible for the construction work to attend the meeting at SUDA.

Thanking you.

Encl. : As stated.

Yours faithfully,


Director, SUDA

SUDA-Health/NUHM/421/15/310(27)/1(1)

Dt. .. 31.01.2018

CC

The Addl. Mission Director, NHM,
Department of Health & Family Welfare FW



Director, SUDA

Sl. No.	ULB	Year of Approval	No. of new U-PHC to be constructed	Status
1	Howrah MC	13-14	14	1 – 30%, 1 – 20%, 1 – 15%, 2 – Plan & Estimate not yet completed, 8 – Place not yet identified, 1 – Awaiting NOC from DHFW.
2	Siliguri MC	13-14	1	1 – Plan estimate submitted to MED for vetting.
3	Alipurduar	15-16	1	1 – 40%, no physical progress since May, 17.
4	Bankura	13-14	3	1 – 25%, 2 – Tender process completed, work not stated.
5	Bishnupur	13-14	1	1 – 40%.
6	Rampurhat	13-14	1	1 – 40%.
7	Suri	13-14	1	1 – 70%.
8	Bolpur	15-16	2	1 – 25%, 1 – 10%.
9	Cooch Behar	13-14	2	1 – 57%, 1 – Place not yet identified.
10	Balurghat	13-14	1	1 – Tender process completed, work not stated.
11	Dankuni	13-14	2	2 – 10%.
12	Arambag	15-16	1	1 – 55%.
13	Jalpaiguri	13-14	2	1 – 40%, 1 – Tender process completed, work not stated.
14	Old Malda	15-16	2	2 – Plan estimate vetted by MED, work not started.
15	Berhampur	13-14	4	1 – 95%, 1 – 50%, 1 – 35%, 1 – 3 rd call opened. Technical papers sent to MED.
16	Dhulian	14-15	2	1 – 40%, 1 – Place not yet identified.
17	Jangipur	15-16	2	1 – 95%, 1 – Place not yet identified.
18	Jiaganj Azimganj	15-16	2	1 – 100%, 1 – 60%.
19	Kandi	15-16	1	1 – Tender process not yet done.
20	Kalyani	14-15	1	1 – 20%.
21	Nabadwip	14-15	3	3 – 77%.
22	Santipur	14-15	2	1 – 70%, 1 – 35%.
23	Chakdah	15-16	2	1 – 80%, 1 – 75%.
24	Gayeshpur	15-16	1	1 – 70%.
25	Haringhata	15-16	1	1 – 70%.
26	Ranaghat	15-16	2	1 – 85%, 1 – 55%.
27	Purulia	13-14	2	1 – Tender process completed, sent to Technical Committee – File no. 242/2017 sent by SUDA to Spl. Secretary on 16.10.17. 1 – e-Tender floated, last date of BID submission 20.12.17.

SUDA

STATE URBAN DEVELOPMENT AGENCY

**HEALTH WING
"ILGUS BHAVAN"**

**H-C BLOCK, SECTOR-III, BIDHANNAGAR, CALCUTTA-700 091
West Bengal**

SUDA-Health/NUHM/421/15/311(27)

31.01.2018

Ref No.

Date

From : Director, SUDA

**To : The Commissioner,
Asansol / Bidhannagar / Durgapur Municipal Corporation**

**To : The Chairman,
Barasat/Basirhat/Bhatpara/Baranagar/DumDum/Kamarhati/Kanchrapara/
Madhyamgram/Naihati/Panihati/Baduria/Garulia/Ghatal/Kalna/Katwa/
Hadia/Panskura/Diamond Harbor/Rajpur Sonarpur/Raiganj/Gangarampur/
Islampur/Kaliyaganj/Kharagpur Municipality**

**Sub. : Meeting at SUDA on 06.02.2018 at 2 p.m. w.r.t. status of
New Construction of U-PHCs under NUHM.**

Sir / Madam,

You are aware that 155 no. of U-PHCs have been approved for 88 ULBs under NUHM by the Govt. of India. The last review meeting with the ULBs on construction status of U-PHCs by NUHM, DHFW was held at Swasthya Bhawan from 20 to 22 November, 2017.

It is informed by the Addl. Mission Director, NHM that new construction of U-PHCs under NUHM in a no. of ULBs either not started or not progressing as per desired level.


Hence, a meeting will be held at SUDA Conference Hall on 06.02.2018 from 2 p.m. to 4 p.m. to expedite the progress in this regard. ULB wise new construction status of U-PHCs is enclosed herewith.

You are requested to depute Executive Officer of the ULB and the person concerned who is responsible for the construction work to attend the meeting at SUDA.

Thanking you.

Encl. : As stated.

Yours faithfully,


Director, SUDA

- 2 -

SUDA-Health/NUHM/421/15/311(27)/1(1)

Dt. .. 31.01.2018

CC

The Addl. Mission Director, NHM,
Department of Health & Family Welfare FW


Director, SUDA

ULB-wise status of construction of U-PHC :

Sl. No.	ULB	Year of Approval	No. of new U-PHC to be constructed	Status
1	Asansol MC	13-14	12	2 – 25%, 1 – 85%, 1 – 100%, 3 – Renovation done instead of New Construction, 3 – Tender process completed, work not stated, 2 – Place not yet identified.
2	Bidhannagar MC	14-15	5	1 – 85%, 1 – 25%, 1 – work not started due to litigation, 2 – Place not yet identified.
3	Durgapur MC	13-14	3	1 – 100%, 1 – 25%, 1 – Place not yet identified.
4	Barasat	13-14	3	1 – 100%, 1 – 85%, 1 – 55%.
5	Basirhat	13-14	3	1 – 45%, 1 – Tender process completed, work not stated, 1 – Plan estimated done.
6	Bhatpara	13-14	2	1 – 85%, 1 – 40%.
7	Baranagar	14-15	3	2 – 25%, 1 – Tender process completed, work not stated.
8	Dum Dum	14-15	1	1 – 10%.
9	Kamarhati	14-15	3	1 – 55%, 2 – 10%.
10	Kanchrapara	14-15	2	1 – 10%, 1 – Tender process completed, work not stated.
11	Madhyamgram	14-15	1	1 – 25%.
12	Naihati	14-15	2	2 – 25%.
13	Panihati	14-15	4	1 – 55%, 3 – 25%.
14	Baduria	15-16	2	1 – 85%, 1 – Tender process completed, work not stated.
15	Garulia	15-16	1	1 – Tender process completed, work not stated.
16	Ghatal	15-16	1	1 – 25%.
17	Kalna	15-16	1	1 – 40%.
18	Katwa	15-16	2	1 – 10%, 1 – Place not yet identified.
19	Haldia	14-15	4	1 – 85%, 2 – 70%, 1 – Renovation instead of new construction, work not stated.
20	Panskura	15-16	1	1 – 70%.
21	Diamond Harbor	13-14	1	1 – 60%.
22	Rajpur Sonarpur	14-15	4	2 – 55%, 1 – 25%, 1 – Tender process completed, work not stated.
23	Raiganj	13-14	2	1 – 30%, - worked stopped for one year-work started in Nov 17 1 – Place not yet identified
24	Gangarampur	15-16	1	1 – 70%.
25	Islampur	15-16	1	1 – 40%, work stopped for last one year.
26	Kaliaganj	15-16	1	1 – 60%.
27	Kharagpur	14-15	2	1 – 100%, 1 – 85%.

SUDA

STATE URBAN DEVELOPMENT AGENCY

HEALTH WING
"ILGUS BHAVAN"

H-C BLOCK, SECTOR-III, BIDHANNAGAR, CALCUTTA-700 091
West Bengal

Ref No. SUDA-Health/NUHM/421/15/294/1(54)

Date 31.01.2018

From : Director, SUDA

To : The Commissioner,
Asansol / Bidhannagar / Durgapur / Howrah / Siliguri Municipal Corporation

To : The Chairman,
..... Municipality

Sub. : Meeting at SUDA w.r.t. status of New Construction of U-PHCs
under NUHM.

Sir / Madam,

You are aware that 155 no. of U-PHCs have been approved for 88 ULBs under NUHM by the Govt. of India. The last review meeting with the ULBs on construction status of U-PHCs by NUHM, DHFW was held at Swasthya Bhawan from 20 to 22 November, 2017.

It is informed by the Addl. Mission Director, NHM that new construction of U-PHCs under NUHM in a no. of ULBs either not started or not progressing as per desired level.

You are requested to depute Executive Officer of the ULB and the person concerned who is responsible for the construction work to attend the meeting at SUDA on 06/2/18 at 11.00 am to expedite progress in this regard.

The list of ULBs and the new construction status of U-PHCs is enclosed herewith.

Thanking you.

Yours faithfully,

Enclo. : As stated.

Director, SUDA

SUDA-Health/NUHM/421/15/294/1(54)/1(1)

Dt. .. 31.01.2018

CC

The Addl. Mission Director, NHM,
Department of Health & Family Welfare FW

Director, SUDA

ULB-wise status of construction and meeting venue, date & time is given below :

Sl. No.	ULB	Year of Approval	No. of new U-PHC to be constructed	Status	Meeting Venue, Date & Time
1	Asansol MC	13-14	12	2 – 25%, 1 – 85%, 1 – 100%, 3 – Renovation done instead of New Construction, 3 – Tender process completed, work not stated, 2 – Place not yet identified,	<p>Venue – SUDA Conference Hall Date – 06/12/18 Time – 11 a.m. to 2 p.m.</p>
2	Balurghat	13-14	1	1 – Tender process completed, work not stated.	
3	Bankura	13-14	3	1 – 25%, 2 – Tender process completed, work not stated.	
4	Barasat	13-14	3	1 – 100%, 1 – 85%, 1 – 55%.	
5	Basirhat	13-14	3	1 – 45%, 1 – Tender process completed, work not stated, 1 – Plan estimated done.	
6	Berhampur	13-14	4	1 – 95%, 1 – 50%, 1 – 35%, 1 – 3 rd call opened. Technical papers sent to MED.	
7	Bhatpara	13-14	2	1 – 85%, 1 – 40%.	
8	Bishnupur	13-14	1	1 – 40%.	
9	Cooch Behar	13-14	2	1 – 57%, 1 – Place not yet identified.	
10	Dankuni	13-14	2	2 – 10%.	
11	Diamond Harbour	13-14	1	1 – 60%.	
12	Durgapur MC	13-14	3	1 – 100%, 1 – 25%, 1 – Place not yet identified.	
13	Howrah MC	13-14	14	1 – 30%, 1 – 20%, 1 – 15%, 2 – Plan & Estimate not yet completed, 8 – Place not yet identified, 1 – Awaiting NOC from DHFW.	
14	Jalpaiguri	13-14	2	1 – 40%, 1 – Tender process completed, work not stated.	
15	Purulia	13-14	2	1 – Tender process completed, sent to Technical Committee – File no. 242/2017 sent by SUDA to Spl. Secretary on 16.10.17. File could not be traced. 1 – e-Tender floated, last date of BID submission 20.12.17.	
16	Raiganj	13-14	2	1 – 30% - worked stopped for one year – work stated in Nov., 17. 1 – Place not yet identified.	
17	Rampurhat	13-14	1	1 – 40%.	
18	Siliguri MC	13-14	1	1 – Plan estimate submitted to MED for vetting.	
19	Suri	13-14	1	1 – 70%.	
20	Baranagar	14-15	3	2 – 25%, 1 – Tender process completed, work not stated.	
21	Bidhannagar MC	14-15	5	1 – 85%, 1 – 25%, 1 – work not started due to litigation, 2 – Place not yet identified.	
22	Dhulian	14-15	2	1 – 40%, 1 – Place not yet identified.	
23	Dum Dum	14-15	1	1 – 10%.	
24	Haldia	14-15	4	1 – 85%, 2 – 70%, 1 – Renovation instead of New Construction.	
25	Kalyani	14-15	1	1 – 20%.	
26	Kamarhati	14-15	3	1 – 55%, 2 – 10%.	
27	Kanchrapara	14-15	2	1 – 10%, 1 – Tender process completed, work not stated.	

S. No.	ULB	Year of Approval	No. of new U-PHC to be constructed	Status	Venue, Date & Time
28	Kharagpur	14-15	2	1 - 100%, 1 - 85%.	Venue - SUDA Conference Hall Date - 06/2/18 Time - 2.30 p.m. to 5.30 p.m.
29	Madhyamgram	14-15	1	1 - 25%.	
30	Nabadwip	14-15	3	3 - 77%.	
31	Naihati	14-15	2	2 - 25%.	
32	Panihati	14-15	4	1 - 55%, 3 - 25%.	
33	Rajpur Sonarpur	14-15	4	2 - 55%, 1 - 25%, 1 - Tender process completed, work not stated.	
34	Santipur	14-15	2	1 - 70%, 1 - 35%.	
35	Alipurduar	15-16	1	1 - 40%, no physical progress since May, 17.	
36	Arambag	15-16	1	1 - 55%.	
37	Baduria	15-16	2	1 - 85%, 1 - Tender process completed, work not stated.	
38	Bolpur	15-16	2	1 - 25%, 1 - 10%.	
39	Chakdah	15-16	2	1 - 80%, 1 - 75%.	
40	Gangarampur	15-16	1	1 - 70%.	
41	Garulia	15-16	1	1 - Tender process completed, work not stated.	
42	Gayeshpur	15-16	1	1 - 70%.	
43	Ghatal	15-16	1	1 - 25%.	
44	Haringhata	15-16	1	1 - 70%.	
45	Islampur	15-16	1	1 - 40%, work stopped for last one year.	
46	Jangipur	15-16	2	1 - 95%, 1 - Place not yet identified.	
47	Jiaganj Azimganj	15-16	2	1 - 100%, 1 - 60%.	
48	Kaliaganj	15-16	1	1 - 60%.	
49	Kalna	15-16	1	1 - 40%.	
50	Kandi	15-16	1	1 - Tender process not yet done.	
51	Katwa	15-16	2	1 - 10%, 1 - Place not yet identified.	
52	Old Malda	15-16	2	2 - Plan estimate vetted by MED, work not started.	
53	Panskura	15-16	1	1 - 70%.	
54	Ranaghat	15-16	2	1 - 85%, 1 - 55%.	

GOVERNMENT OF WEST BENGAL
HEALTH & FAMILY WELFARE DEPARTMENT
NATIONAL HEALTH MISSION (NHM)
GN -29, 2nd FLOOR, GRANTHAGAR BHAWAN,
SWASTHYA BHAWAN PREMISES, SECTOR -V
SALT LAKE, BIDHANNAGAR, KOLKATA - 700 091.

☎ 033 - 2333-0432, ☎ 033 - 2357 - 7930,

Email ID: spmu.nuhm@gmail.com; website: www.wbhealth.gov.in

Memo No. HFW/NUHM-638/2015/Pt.I/240

Date: 17.01.2018

From : **Addl. Mission Director, NHM**
Government of West Bengal

To : **Director, SUDA**
Government of West Bengal

Sub: Status of New Construction / Renovation work of U-PHCs under NUHM

Sir,

Under NUHM in West Bengal, 168 no. of new construction of U-PHCs were approved, at the same time 291 no. of UPHCs were approved renovation and up-gradation.

After lapses of considerable time it is observed that renovation work of U-PHCs in most of the ULBs have already been completed and new construction of U-PHCs are also complete in few ULBs.

Unfortunately, it is also observed that in some of the ULBs construction work has not yet been started, in spite of our regular reminder. It appears that these ULBs are unable to start the construction work of

U-PHC as the allotment was issued in 2013-14, 2014-15 and 2015-16.

In this situation, you are requested to look in to the matter urgently, discuss it with concerned ULB authority whether the ULB will be able to start construction work immediately. If it is not possible for the ULB to start the construction work with immediate effect they may be asked to refund back the fund allotted to them for construction work by 15 February, 2018.

List of ULBs where construction work has not yet been started is enclosed as Annexure III for new construction and Annexure-IV for renovation (status as on 30/11/17) for taking necessary action.

Yours faithfully,

Analeela Ghosh, 12/1/18
Addl. Mission Director, NHM
Government of West Bengal

Memo No. HFW/NUHM-638/2015/Pt.I/240/1(3)

Date: 17.01.2018

Copy forwarded for information and necessary action to:

1. **The Commissioner**, (Siliguri/Howrah/Bidhannagar/Asansol/ Durgapur) Municipal Corporation.
2. **PA to Mission Director, NHM**, Government of West Bengal
3. **IT cell** for web posting

Ankur Chakrabarti 17/1/18
Addl. Mission Director, NHM
Government of West Bengal

Status of New Construction under NUHM

Sl. No.	ULB	Year of Approval	No. of new ILCs to be constructed	Status	100%	95%	85%	75%	65%	55%	45%	35%	25%	<25%	Renov. Instead of NC	Tender Com. Work not start	Place not identified	Plan Estimate not done	Tech. Paper sent to MED after 3rd Call	Awaiting NOC from DHPW	Technical Committee	E-tender floated	Verted by MED, work not started	Sent to MED for vetting	Tender floated	
1	Aarnsol MC	13-14	12	2 - 25%, 1 - 85%, 1 - 100%, 3 - Renovation done instead of New Construction, 3 - Tender process completed, work not started, 2 - Place not yet identified.	1	1									3	3	2									
2	Balughat	13-14	1	1 - Tender process completed, work not started.												1										
3	Bankura	13-14	3	1 - 25%, 2 - Tender process completed, work not started.												2										
4	Barasat	13-14	3	1 - 100%, 1 - 85%, 1 - 55%	1	1																				
5	Basirhat	13-14	3	1 - 45%, 1 - Tender process completed, work not started, 1 - Plan estimated done												1		1								
6	Berhampur	13-14	4	1 - 95%, 1 - 50%, 1 - 35%, 1 - 3rd call opened. Technical papers sent to MED		1													1							
7	Bisnupara	13-14	2	1 - 85%, 1 - 40%												1										
8	Bishnupur	13-14	1	1 - 40%												1										
9	Burdwan	13-14	1	1 - 85%																						
10	Chandernagore MC	13-14	1	1 - 100%																						
11	Cooch Behar	13-14	2	1 - 57%, 1 - Place not yet identified.													1									
12	Darhanga	13-14	2	2 - 10%													2									
13	Diamond Harbour	13-14	1	1 - 60%																						
14	Durgapur MC	13-14	3	1 - 100%, 1 - 25%, 1 - Place not yet identified.													1									
15	English Bazar	13-14	2	2 - 100%																						
16	Habra	13-14	3	3 - 100%																						
17	Hooghly Chinsurah	13-14	1	1 - 90%																						
18	Howrah MC	13-14	14	1 - 30%, 1 - 20%, 1 - 15%, 2 - Plan & Estimate not yet completed, 8 - Place not yet identified, 1 - Awaiting NOC from DHPW													8	2		1						
19	Jalpaiguri	13-14	2	1 - 40%, 1 - Tender process completed, work not started.													1									
20	Jhargam	13-14	1	1 - 100%																						
21	Krishnagar	13-14	1	1 - 100%																						
22	Maheshtala	13-14	3	2 - 100%, 1 - 95%																						
23	Medinipur	13-14	3	2 - 100%, 1 - 85%																						
24	Purulia	13-14	2	1 - Tender process completed, sent to Technical Committee - File no 242/2017 sent by SUDA to Spl Secretary on 16.10.17. File could not be traced. 1 - e-Tender floated, last date of BID submission 20.12.17																						
25	Raiganj	13-14	2	1 - 30% - worked stopped for one year - work stated in Nov. 17 1 - Place not yet identified																						
26	Raipurhat	13-14	1	1 - 40%																						
27	Siliguri MC	13-14	1	1 - Plan estimate submitted to MED for vetting.																						
28	Suri	13-14	1	1 - 70%																						

Sl. No.	U.B	Year of Approval	No. of new U-PhC to be constructed	Status	100%	95%	85%	75%	65%	55%	45%	35%	25%	<25%	Renov. of NC	Tender Com. Work not start	Place not identified	Plan Estimate not done	Tech. Paper sent to M&ED after 3rd Call	Awaiting NOC from DHRW	Technical Committee	E-tender floated	Verted by M&ED, work not started	Sent to M&ED for vetting	Tender floated	
29	Tamiluk	13-14	1	1 - 100%	1																					
30	Ashoknagar Kalyangarh	14-15	2	2 - 85%			2																			
31	Baogson	14-15	2	2 - 100%																						
32	Barranagar	14-15	3	2 - 25%, 1 - Tender process completed, work not started			2																			
33	Bidhanagar MC	14-15	5	1 - 85%, 1 - 25%, 1 - work not started due to litigation, 2 - Place not yet identified			1																			
34	Dhulian	14-15	2	1 - 40%, 1 - Place not yet identified							1															
35	Dum Dum	14-15	1	1 - 10%																						
36	Haldia	14-15	4	1 - 85%, 2 - 70%, 1 - Renovation instead of New Construction.				1	2																	
37	Kalyani	14-15	1	1 - 20%																						
38	Kamrhati	14-15	3	1 - 55%, 2 - 10%							1															
39	Kanchrapara	14-15	2	1 - 10%, 1 - Tender process completed, work not stated																						
40	Katargaur	14-15	2	1 - 100%, 1 - 85%			1																			
41	Madhyangram	14-15	1	1 - 25%																						
42	Nabadwip	14-15	3	3 - 77%					3																	
43	Nahati	14-15	2	2 - 25%																						
44	Panhati	14-15	4	1 - 55%, 3 - 25%						1																
45	Rajpur Sonarpur	14-15	4	2 - 55%, 1 - 25%, 1 - Tender process completed, work not stated.							2															
46	Saantpur	14-15	2	1 - 70%, 1 - 35%							1															
47	South Dum Dum	14-15	2	2 - 100%					1																	
48	Alipurdur	14-16	1	1 - 40%, no physical progress since May-17																						
49	Arambag	15-16	1	1 - 55%																						
50	Baduria	15-16	2	1 - 85%, 1 - Tender process completed, work not stated																						
51	Bolpur	15-16	2	1 - 25%, 1 - 10%																						
52	Chakdaha	15-16	2	1 - 80%, 1 - 75%					1	1																
53	Contai	15-16	2	1 - 100%, 1 - 99%						1																
54	Gangarampur	15-16	1	1 - 70%																						
55	Ganjula	15-16	1	1 - Tender process completed, work not stated																						
56	Goyalspur	15-16	1	1 - 70%																						
57	Chatal	15-16	1	1 - 25%																						
58	Harnghata	15-16	1	1 - 70%																						
59	Isampur	15-16	1	1 - 40%, work stopped for last one year.																						
60	Jangipur	15-16	2	1 - 95%, 1 - Place not yet identified																						
61	Jiaganj Azimganj	18-16	2	1 - 100%, 1 - 60%																						
62	Kaltaganj	15-16	1	1 - 60%																						
63	Kalina	15-16	1	1 - 40%																						
64	Karadi	15-16	1	1 - Tender process not yet done																						
65	Karwa	15-16	2	1 - 10%, 1 - Place not yet identified																						
66	Old Malda	15-16	2	2 - Plan estimate vetted by M&ED, work not started																						
67	Panskura	15-16	1	1 - 70%																						
68	Ranighat	15-16	2	1 - 85%, 1 - 55%																						
69	Kalimpang	17-18	1	1 - Place not yet identified																						
Total =>						25	5	13	12	3	9	9	4	16	11	4	13	20	3	1	1	1	2	1	1	

Status of Construction of New U-PHC Building (upto November-17)

A	B	C	D	E	F	G	H	I	J	K=I-J	L=H-I	M=K+L	N	O	P
Sl No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected Date of Completion
1	Hooghly	Arambagh	Arambagh UPHC 1 Chandur Bhatamore Ward No. 15	NC	2015-16	75.00	30.00	24.00	22.22	1.78	6.00	7.78	55%		Mar-18
2	Hooghly	Chandernagar	Chandernagar UPHC 2 Ward No. 25 Tribazar Community Market Gondolpara	NC	2013-14	75.00	75.00	75.00	29.77	45.23	0.00	45.23	100%		
3	Hooghly	Dankuni	Dankuni UPHC 1 Ward No. 2 Kharial Barowartala Kanarpara	NC	2013-14	75.00	45.00	45.00	0.25	44.75	0.00	44.75	10%		Jul-18
4	Hooghly	Dankuni	Dankuni UPHC 2 Ward No. 20 Mathur dingi near hanspukur Mrigala	NC	2013-14	75.00	45.00	45.00	8.75	36.25	0.00	36.25	10%		Jul-18
5	Hooghly	Chinsurah	Hooghly Chinsurah UPHC 3 Ward No. 14 M K Hat HAU Satarmore	NC	2013-14	75.00	45.00	45.00	40.51	4.49	0.00	4.49	90%		Mar-18
6	Jhargram	Jhargram	Jhargram UPHC 1 Ward No. 6 Balaradhi	NC	2013-14	75.00	75.00	75.00	59.05	15.95	0.00	15.95	100%		
7	Nadia	Chakda	Chakdah UPHC 1 Sakuntala Talata Ward No. 20	NC	2015-16	75.00	30.00	30.00	30.00	0.00	0.00	0.00	80%		Jan-18
8	Nadia	Chakda	Chakdah UPHC 2 Malobika Ward No. 12 Ghughia Sarkarpara	NC	2015-16	75.00	30.00	30.00	32.16	-2.16	0.00	-2.16	75%		Jan-18
9	Nadia	Gayeshpur	Gayeshpur UPHC 1 Ward No. 15 Kataganj	NC	2015-16	75.00	26.25	26.25	29.74	-3.49	0.00	-3.49	70%		Jan-18
10	Nadia	Haringhata	Haringhata UPHC 1 Ward No. 2 Subarnapur near Haringhata Bazar	NC	2015-16	75.00	18.75	18.75	11.71	7.04	0.00	7.04	70%		Jan-18
11	Nadia	Kalyani	Kalyani UPHC 1 Ward No. 1 Anukul More Chandamari Bazar	NC	2014-15	75.00	22.50	22.50	0.81	21.69	0.00	21.69	20%	Will inform to State after 10 days	
12	Nadia	Krishna	Krishnagar UPHC 1 Ward No. 20 Chasa para Near Karimpur Bus stand	NC	2014-15	75.00	75.00	75.00	75.00	0.00	0.00	0.00	100%		
13	Nadia	Krishna	Krishnagar UPHC 2 Ward No. 12 Raja Road Chowdhury para	NC	2014-15	75.00	75.00	75.00	75.00	0.00	0.00	0.00	100%		
14	Nadia	Krishna	Krishnagar UPHC 3 Ward No. 10 Saktinagar Water Works Compound	NC	2014-15	75.00	75.00	75.00	75.00	0.00	0.00	0.00	100%		
15	Nadia	Nabadwip	Nabadwip UPHC 1 Dr. Bidhan Candra Roy Sachitra Kedra Ward No. 7 Mistr Para	NC	2014-15	75.00	56.25	56.25	37.67	18.58	0.00	18.58	77%		Jan-18

21.12.17

Status of Construction of New U-PHC Building (upto November-17)

SI No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected Date of Completion
A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O	P
16	Nadia	Nabadwip	Nabadwip UPHC 2 Sister Nilbedita Sasthya Kendra Ward No. 17 Alania Shib Tala Road	NC	2014-15	75.00	56.25	56.25	33.20	23.05	0.00	23.05	77%		Jan-18
17	Nadia	Nabadwip	Nabadwip UPHC 3 Mother Teresa Sasthya Kendra Ward No. 19 Kolar Denga Road	NC	2014-15	75.00	56.25	56.25	31.73	24.52	0.00	24.52	75%		Jan-18
18	Nadia	Ranaghat	Ranaghat UPHC 1 Dargata UPHC Ward No. 09 Dispensary Lane	NC	2015-16	75.00	30.00	30.00	17.76	12.24	0.00	12.24	55%		Mar-18
19	Nadia	Ranaghat	Ranaghat UPHC 2 Nasra UPHC Ward No. 18 Bantsangha	NC	2015-16	75.00	30.00	30.00	19.82	10.18	0.00	10.18	85%		Jan-18
20	Nadia	Santipur	Santipur UPHC 1 Ward No 17 Dr. B. C. Ray Road	NC	2014-15	75.00	28.75	28.75	2.16	26.59	0.00	26.59	35%		Mar-18
21	Nadia	Santipur	Santipur UPHC 3 Ward No 13 Panchanan tala lane	NC	2014-15	75.00	28.75	28.75	0.00	28.75	0.00	28.75	70%		Jan-18
22	Nandigram HD	Contai	Contai UPHC 1 Ward No 19 Kishorenagar	NC	2015-16	75.00	30.00	30.00	28.85	1.15	0.00	1.15	95%	Rest 90 Lakhs for 2 U-PHCs have been released from this office vide memo no. HFW/NUHM-582/14Pt-II/3209 dated	Dec-17
23	Nandigram HD	Contai	Contai UPHC 2 Ward No 11 Hatabari	NC	2015-16	75.00	30.00	30.00	39.21	-9.21	0.00	-9.21	100%		
24	Paschim Bardhaman	Asansol MC	Asansol UPHC 12 Jamuria Ward No. 07 Balampur beside Balampur Road & Satwik Cement	NC	2014-15	75.00	30.00	30.00	0.00	0.00	30.00	30.00	25%		Mar-18
25	Paschim Bardhaman	Asansol MC	Asansol UPHC 13 Jamuria Ward No. 04 Bye pass road opp. Jamuria Truck & Taxi Stand	NC	2014-15	75.00	30.00	30.00	0.00	0.00	30.00	30.00	25%		Mar-18
26	Paschim Bardhaman	Asansol MC	Asansol UPHC 14 Jamuria Ward No. 11 Sripur Rana Colliery	NC	2014-15	75.00	25.00	0.00	0.00	0.00	25.00	25.00	0%	This line-list will be changed due to non availability of Land. Procurement of Land for new site is under process. Final line-list will receive within Dec.-17	Site Problem
27	Paschim Bardhaman	Asansol MC	Tewari Para within RS Plot No, 227 Mouza -Egara at ward no-93, Raniganj	NC	2014-15	75.00	25.00	0.00	0.00	0.00	25.00	25.00	0%	Work not started but tender process and work order issued	Will inform to State after 10 days
28	Paschim Bardhaman	Asansol MC	Jhanti Danga, plot No. 47 & 49, Mouza-Baktar nagar, Ward No. 35, Raniganj	NC	2014-15	75.00	25.00	0.00	0.00	0.00	25.00	25.00	0%	Work not started but tender process and work order issued	Will inform to State after 10 days

Status of Construction of New U-PHC Building (upto November-17)

Sl No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected Date of Completion
A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O	P
29	Paschim Bardhaman	Asansol MC												Line-list was not received. Site was not yet finalised	
30	Paschim Bardhaman	Asansol MC	Dhenomoin, ward no. 58 (new), Kulti	NC	2015-16	75.00	30.00	30.00					85%		Jan-18
31	Paschim Bardhaman	Asansol MC	Barakar, ward no. 67 (new), Kulti	NC	2015-16	75.00	30.00	30.00					0%	Work not started but tender process and work order issued	Will inform to State after 10 days
32	Paschim Bardhaman	Asansol MC	Dishergharh, ward no. 105 (new), Kulti	NC	2015-16	75.00	30.00	30.00	72.94	107.06	0.00	107.06	100%		
33	Paschim Bardhaman	Asansol MC	Bidyandapur PHC, ward no. 99 (new), Kulti	NC	2015-16	75.00	30.00	30.00					100%		
34	Paschim Bardhaman	Asansol MC	Sodepur PHC, ward no. 102 (new), Kulti	NC	2015-16	75.00	30.00	30.00					100%		
35	Paschim Bardhaman	Asansol MC	Kumardihia PHC, ward no. 59 (new), Kulti	NC	2015-16	75.00	30.00	30.00					100%		
36	Paschim Bardhaman	Durgapur r MC	Durgapur UPHC 9 Ward No.37 Pursha	NC	2013-14	75.00	10.00	47.00	19.55	27.45	-37.00	-9.55	100%		
37	Paschim Bardhaman	Durgapur r MC	Durgapur UPHC 10 Ward No.13 Ramkrishna Pally	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Functional; Land Dispute for new const.	Will inform to State after 10 days
38	Paschim Bardhaman	Durgapur r MC	Durgapur UPHC 11 Ward No.18 Prantika	NC	2013-14	75.00	10.00	0.00	6.72	-6.72	10.00	3.28	25%		Apr-18
39	Paschim Medinipur	Ghatal	Ghatal UPHC 1 Ward No. 5 Gambhir Nagar	NC	2015-16	75.00	30.00	0.00	0.00	0.00	30.00	30.00	25%		Will inform to State after 10 days
40	Paschim Medinipur	Kharagpur ur	Kharagpur UPHC 5 Ward No. 35 Talbagicha	NC	2014-15	75.00	45.00	45.00	101.06	-56.06	0.00	-56.06	85%		Feb-18
41	Paschim Medinipur	Kharagpur ur	Kharagpur UPHC 6 Ward No. 18 GIRI MAIDAN Vidyasagar Abasan	NC	2014-15	75.00	45.00	45.00		45.00	0.00	45.00	100%		
42	Paschim Medinipur	Medinipur ur	Medinipur UPHC 1 Ward No. 2 Abasgarh Kulkota	NC	2013-14	75.00	59.06	59.06		-120.69	0.00	-120.69	85%		Feb-18
43	Paschim Medinipur	Medinipur ur	Medinipur UPHC 2 Ward No. 23 Narampur Sarpatally	NC	2013-14	75.00	59.06	59.06	179.75	59.06	0.00	59.06	100%	Scheme wise Expenditure & Balance was not received	

Status of Construction of New U-PHC Building (upto November-17)

Sl No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected Date of Completion
A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O	P
44	Paschim Medinipur	Medinipur	Medinipur UPHC 3 Ward No. 16 Berh Bailavpur Manikpur	NC	2013-14	75.00	61.63	61.63		61.63	0.00	61.63	100%		
45	Purba Medinipur	Haldia	Haldia UPHC 1 Ward No. 2 Nandarampur near Paranchak	NC	2014-15	75.00	30.00	25.32	16.37	8.95	4.68	13.63	70%		Mar-18
46	Purba Medinipur	Haldia	Haldia UPHC 2 Ward No. 5 Raghunathchak Ramnagar	NC	2014-15	75.00	30.00	30.00		0.00	30.00	30.00		Providing Scheme type as Renovation instead of New	
47	Purba Medinipur	Haldia	Haldia UPHC 3 Ward No. 11 Tentulberia P. O. Debhog	NC	2014-15	75.00	30.00	25.32	24.70	0.62	4.68	5.30	85%		Feb-18
48	Purba Medinipur	Haldia	Haldia UPHC 4 Ward No. 14 Geondave	NC	2014-15	75.00	30.00	25.32	13.62	11.70	4.68	16.38	70%		Mar-18
49	Purba Medinipur	Panskura	Panskura UPHC 1 Ward No. 12 Pratappur	NC	2015-16	75.00	30.00	32.12	32.12	0.00	-2.12	-2.12	70%		Feb-18
50	Purba Medinipur	Tamralipta	Tamralipta UPHC 1 Ward No. 14 UC Sankarara Tamluk	NC	2013-14	75.00	45.00	47.12	53.15	-6.03	-2.12	-8.15	100%		

Status of Construction of New U-PHC Building

Sl No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of Physical completion	Remarks
A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O
1	Bankura	Bankura	Bankura UPHC 1 Ward No 12 Idgamahalla Banstata	NC	2013-14	75.00	45.00	22.50	4.30	18.20	22.50	40.70	25%	
2	Bankura	Bankura	Bankura UPHC 2 Ward No 19 Pataola Pump House Kethardanga	NC	2013-14	75.00	45.00	0.00	0.00	0.00	45.00	45.00	0%	Work not started but tender process completed
3	Bankura	Bankura	Bankura UPHC 3 Ward No 1 Dasherbandh lane near District Library	NC	2013-14	75.00	45.00	0.00	0.00	0.00	45.00	45.00	0%	Work not started but tender process completed
4	Basirhat HD	Baduria	Baduria UPHC 1 Ward No. 5 PS Baduria	NC	2015-16	75.00	30.00	50.00	31.10	18.90	-20.00	-1.10	85%	Physical progress is not developing from Last Feb. - 17
5	Basirhat HD	Baduria	Baduria UPHC 2 Ward No. 12 Punra near punra bazar	NC	2016-17	75.00	0.00	10.00	0.00	10.00	-10.00	0.00	0%	Work not started but tender process completed and work order issued
6	Basirhat HD	Basirhat	Basirhat UPHC 1 Ward No. 19 Bhabla RN Mukharjee Charitable Dispensary	NC	2013-14	75.00	45.00	15.00	0.00	15.00	30.00	45.00	0%	Work not started but tender process completed
7	Basirhat HD	Basirhat	Basirhat UPHC 2 Ward No. 2 Haladhar Bhattacharya main Road Nalkora	NC	2013-14	75.00	45.00	15.00	0.00	15.00	30.00	45.00	45%	Work not started but tender process completed and work order issued
8	Basirhat HD	Basirhat	Basirhat UPHC 3 Ward No. 16 Harishpur Natun Bazar	NC	2013-14	75.00	45.00	10.00	0.00	10.00	35.00	45.00	0%	Work not started but only preparation of plan estimate done
9	Bishnupur HD	Bishnupur	Bishnupur UPHC 1 Ward No 15 near Bishnupur Municipality Premises	NC	2013-14	75.00	45.00	0.00	0.00	0.00	45.00	45.00	40%	
10	Diamond Harbour HD	Diamond Harbour	Diamond Harbour UPHC 1 Ward No. 06 Jagannath Sarani Pritypur	NC	2013-14	75.00	45.00	22.50	22.50	0.00	22.50	22.50	60%	
11	North 24 Parganas	Ashoknagar Kalyang	Ashoknagar UPHC 1 Ward No. 4 Asoke Kalyangath Municipal Health Centre	NC	2014-15	75.00	22.50	22.79	15.60	7.19	-0.29	6.90	85%	
12	North 24 Parganas	Ashoknagar Kalyang	Ashoknagar UPHC 2 Ward No. 18 Prajanananda Seba Sadan	NC	2014-15	75.00	22.50	22.80	15.60	7.20	-0.30	6.90	85%	
13	North 24 Parganas	Bangaon	Bangaon UPHC 1 Motiganj Palpara Ward No 1	NC	2014-15	75.00	22.50	44.14	38.80	5.34	-21.64	-16.30	100%	
14	North 24 Parganas	Bangaon	Bangaon UPHC 2 Burma Colony Ward No 19	NC	2014-15	75.00	22.50	44.14	38.78	5.36	-21.64	-16.28	100%	

20.12.17

Status of Construction of New U-PHC Building

Sl No.	District Name	ULB Name	U-PhC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks
A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O
15	North 24 Parganas	Baranagar	Baranagar UPHC 1 Ward No. 15 near RIC Gate	NC	2014-15	75.00	22.50	19.05	0.00	19.05	3.45	22.50	25%	
16	North 24 Parganas	Baranagar	Baranagar UPHC 2 Ward No. 3 Behind Ashokgarh Bazar	NC	2014-15	75.00	22.50	19.04	0.00	19.04	3.46	22.50	25%	
17	North 24 Parganas	Baranagar	Baranagar UPHC 3 Ward No. 27 Bagha, Jatini Road	NC	2014-15	75.00	22.50	19.45	0.00	19.45	3.05	22.50	0%	Work not started but tender process completed and work order issued
18	North 24 Parganas	Barasat	Barasat UPHC 1 Ward No. 8 Sister Bhagini Nivedita UPHC Boys School Rd. Nawapally	NC	2013-14	75.00	45.00	19.08	21.40	-2.32	25.92	23.60	55%	
19	North 24 Parganas	Barasat	Barasat UPHC 2 Ward No. 3 Dwijahari Das Colony	NC	2013-14	75.00	45.00	18.70	21.42	-2.72	26.30	23.58	85%	
20	North 24 Parganas	Barasat	Barasat UPHC 6 Ward No. 26 Hatkhola UPHC near I.M.A. Hatkhola	NC	2013-14	75.00	45.00	19.08	21.40	-2.32	25.92	23.60	100%	
21	North 24 Parganas	Bhatpara	Bhatpara UPHC 1 Ward No. 3 Community Centre Rahapara	NC	2013-14	75.00	45.00	46.66	33.19	13.47	-1.66	11.81	85%	
22	North 24 Parganas	Bhatpara	Bhatpara UPHC 3 Ward No. 18 Nandallal Sur park jagatdal	NC	2013-14	75.00	45.00	46.66	33.19	13.47	-1.66	11.81	40%	
23	North 24 Parganas	Bidhannagar MC	Bidhannagar UPHC 1 Ward No. 28 polenite Khasmahal UPHC	NC	2014-15	75.00	22.50	0.00	0.00	0.00	22.50	22.50	0%	Work not started due to litigation. functioning from khasmahal, w.no 36
24	North 24 Parganas	Bidhannagar MC	Bidhannagar UPHC 2 Ward No. 36 Nawbhanga UPHC	NC	2014-15	75.00	22.50	0.00	0.00	0.00	22.50	22.50	25%	
25	North 24 Parganas	Bidhannagar MC	Bidhannagar UPHC 4 Ward No. 39 near DA block	NC	2014-15	75.00	22.50	30.00	0.00	30.00	-7.50	22.50	85%	
26	North 24 Parganas	Bidhannagar MC	Bidhannagar UPHC 11 Ward No. 7 Rajarhat Gopalpur Mondalganthe Arjunpur	NC	2014-15	75.00	22.50	0.00	0.00	0.00	22.50	22.50	0%	Plan Estimate yet to be done
27	North 24 Parganas	Bidhannagar MC	Bidhannagar UPHC 12 Ward No. 27 Rajarhat Gopalpur Udayanpally	NC	2014-15	75.00	22.50	0.00	0.00	0.00	22.50	22.50	0%	Plan Estimate yet to be done
28	North 24 Parganas	Dum Dum	Dum Dum UPHC 1 Ward No. 22 patal nagar colony	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	10%	

Status of Construction of New U-PHC Building

A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O
Sl No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks
29	North 24 Parganas	Garulia	Garulia UPHC 2 HAUI Water Tank compound Ward No. 10 Garulia main road	NC	2015-16	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Work not started but tender process completed
30	North 24 Parganas	Habra	Habra UPHC 1 Ward No. 6 Super Market Kamarthuba	NC	2013-14	75.00	45.00	48.34	48.17	0.17	-3.34	-3.17	100%	
31	North 24 Parganas	Habra	Habra UPHC 2 Ward No. 22 Sarada Bhawan Banipur	NC	2013-14	75.00	45.00	48.30	48.17	0.13	-3.30	-3.17	100%	
32	North 24 Parganas	Habra	Habra UPHC 3 Ward No. 12 Akampur Biswakabi Road	NC	2013-14	75.00	45.00	48.33	48.17	0.16	-3.33	-3.17	100%	
33	North 24 Parganas	Kamarhati	Kamarhati UPHC 5 IPP VIII building Ward No. 16 M.M. Feeder Road	NC	2014-15	75.00	22.50	18.57	0.00	18.57	3.93	22.50	55%	
34	North 24 Parganas	Kamarhati	Kamarhati UPHC 6 Ward No. 24 DP Nagar Playground No. 2	NC	2014-15	75.00	22.50	18.79	0.00	18.79	3.71	22.50	10%	
35	North 24 Parganas	Kamarhati	Kamarhati UPHC 7 Ward No. 35 Jatindas Nagar Belghorra	NC	2014-15	75.00	22.50	18.62	0.00	18.62	3.88	22.50	10%	
36	North 24 Parganas	Kanchra para	Kanchrapara UPHC 1 Ward No. 6 Ghatak Road	NC	2015-16	75.00	26.25	13.47	0.00	13.47	12.78	26.25	0%	Tender process completed & Work order issued
37	North 24 Parganas	Kanchra para	Kanchrapara UPHC 2 Ward No. 12 Sashi Babu Road	NC	2015-16	75.00	26.25	13.48	0.00	13.48	12.77	26.25	10%	
38	North 24 Parganas	Madhya mgram	Madhyamgram UPHC 4 Ward No. 4	NC	2014-15	75.00	22.50	18.18	6.27	11.91	4.32	16.23	25%	
39	North 24 Parganas	Naihati	Naihati UPHC 3 Ward No. 22 Adhata Road Near Star Club	NC	2014-15	75.00	22.50	13.50	0.00	13.50	9.00	22.50	25%	
40	North 24 Parganas	Naihati	Naihati UPHC 4 Ward No. 02 R.B.C. Road Garifa	NC	2014-15	75.00	22.50	13.40	0.00	13.40	9.10	22.50	25%	
41	North 24 Parganas	Panihati	Panihati UPHC 1 Ward No. 3 Ramkrisna Pally Pathagar Road	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	55%	
42	North 24 Parganas	Panihati	Panihati UPHC 2 Ward No. 6 Dr. Saraj Mukherjee Road	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	25%	

Status of Construction of New U-PhC Building

SI No.	District Name	ULB Name	U-PhC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUBA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks
A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O
43	North 24 Parganas	Panihati	Panihati UPHC 7 Ward No. 25 Beside Ushampur Football Ground	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	25%	
44	North 24 Parganas	Panihati	Panihati UPHC 8 Ward No. 35 Partha Pur Near Parthapur Bazaar	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	25%	
45	North 24 Parganas	South Dum Dum	South Dum Dum UPHC 7 Ward No. 11 R.N. Tagore Road Bediapara	NC	2014-15	75.00	22.50	22.50	18.19	4.31	0.00	4.31	100%	
46	North 24 Parganas	South Dum Dum	South Dum Dum UPHC 8 Ward No. 3 Promudnagar	NC	2014-15	75.00	22.50	22.50	18.19	4.31	0.00	4.31	100%	
47	Purulia	Purulia	Purulia UPHC 1 Ward No. 12 Namopara Durgamondir	NC	2013-14	75.00	45.00	45.00	0.00	45.00	0.00	45.00	0%	Tender process completed
48	Purulia	Purulia	Purulia UPHC 2 Ward No. 5 Joy Jowan Club Nadiha	NC	2013-14	75.00	45.00	0.00	0.00	0.00	45.00	45.00	0%	e_Tender Floated, last date of Bid Submission - 20 Dec 2017
49	South Twenty Four Parganas	Mahesthala	Mahesthala UPHC 7 Ward No. 10 Shanti Nagar	NC	2013-14	75.00	45.00	45.00	52.18	-7.18	0.00	-7.18	100%	
50	South Twenty Four Parganas	Mahesthala	Mahesthala UPHC 8 Ward No. 16 Santoshpur Govt. Colony	NC	2013-14	75.00	45.00	45.00	42.29	2.71	0.00	2.71	95%	
51	South Twenty Four Parganas	Mahesthala	Mahesthala UPHC 9 Ward No. 21 Akra Boga Noapara	NC	2013-14	75.00	45.00	45.00	45.64	-0.64	0.00	-0.64	100%	
52	South Twenty Four Parganas	Rajpur Sonarpur	Rajpur Sonarpur UPHC 5 Ward No. 05 Kamrabad Sonarpur Srikhanda Garia	NC	2014-15	75.00	22.50	22.50	35.57	-13.07	0.00	-13.07	55%	
53	South Twenty Four Parganas	Rajpur Sonarpur	Rajpur Sonarpur UPHC 6 Ward No. 12 Sonarpur	NC	2014-15	75.00	22.50	22.50	2.21	20.29	0.00	20.29	0%	Work not started but tender process completed and work order issued
54	South Twenty Four Parganas	Rajpur Sonarpur	Rajpur Sonarpur UPHC 7 Ward No. 21 Chak Harinavi Manashatala Subhasgram	NC	2014-15	75.00	22.50	22.50	36.43	-13.93	0.00	-13.93	55%	
55	South Twenty Four Parganas	Rajpur Sonarpur	Rajpur Sonarpur UPHC 8 Ward No. 35 Boral Rania Auribinda Nagar	NC	2014-15	75.00	22.50	22.50	9.36	13.14	0.00	13.14	25%	

Status of Construction of New U-PHC Building (upto November - 17)

A	B	C	D	E	F	G	H	I	J	K=I-J	L=H-I	M=K-L	N	O	
Sl No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected date of completion
1	Alipurduar	Alipurduar	Alipurduar UPHC 1 Ward No 16 New Alipurduar	NC	2015-16	75.00	30.00	30.00	21.86	8.14	0.00	8.14	40%	No physical progress since May 2017	Apr-18
2	Birbhum	Bolpur	Bolpur UPHC 1 Ward No. 17 Dharmarajjala	NC	2015-16	75.00	30.00	22.50	0.00	22.50	7.50	30.00	25%		May-18
3	Birbhum	Bolpur	Bolpur UPHC 2 Ward No. 19 Bypass More	NC	2015-16	75.00	30.00	0.00	0.00	0.00	30.00	30.00	10%		May-18
4	Birbhum	Suri	Suri UPHC 1 Ward No 8 Suri Municipal Office	NC	2013-14	75.00	45.00	45.00	42.25	2.75	0.00	2.75	70%		Feb-18
5	Cooch Behar	Cooch Behar	Cooch Behar UPHC 1 Ward No. 12 Rabindranagar	NC	2013-14	75.00	45.00	23.50	27.03	-3.53	21.50	17.97	57%		Mar-18
6	Cooch Behar	Cooch Behar	Cooch Behar UPHC 2 Ward No. 3 Kalabagan near kalabagan primary school	NC	2013-14	75.00	45.00	23.50	1.05	22.45	21.50	43.95	0%	Preparation of Plan estimate is yet to be done	Site Problem
7	Dakshin Dinajpur	Balughat	Balughat UPHC 3 Ward No. 17 Sare Tin No Club	NC	2013-14	75.00	45.00	22.50	0.00	22.50	22.50	45.00	0%	Work not started but tender process completed and work order issued	May-18
8	Dakshin Dinajpur	Gangara	Gangarampur UPHC 1 Ward No. 11 Dangapara	NC	2015-16	75.00	30.00	30.00	24.95	5.05	0.00	5.05	70%		Mar-18
9	Darjeeling	Siliguri MC	Siliguri UPHC 10 Ward No. 5 Ganganagar near Park	NC	2013-14	75.00	10.00	0.00	0.00	0.00	10.00	10.00	0%	Plan estimate submitted to MED for vetting	Aug-18
21	Jalpaiguri	Jalpaiguri	Jalpaiguri UPHC 1 Ward No. 18 Keranipara	NC	2013-14	75.00	45.00	30.57	15.93	14.64	14.43	29.07	40%		Feb-18
22	Jalpaiguri	Jalpaiguri	Jalpaiguri UPHC 2 Ward No. 15 Pandapara	NC	2013-14	75.00	45.00	30.45	0.00	30.45	14.55	45.00	0%	Work not started but tender process completed and work order issued since from April.	May-18
23	Maldah	English Bazar	English Bazar UPHC 1 Ward No. 12 Baluchar	NC	2013-14	75.00	45.00	45.00	56.13	-11.13	0.00	-11.13	100%		
24	Maldah	English Bazar	English Bazar UPHC 2 Ward No. 8 R.K. Mission Road	NC	2013-14	75.00	45.00	45.00	81.67	-36.67	0.00	-36.67	100%		
25	Maldah	Old Malda	Old Malda UPHC 1 Ward No. 5 Adjacent to Old Malda Municipal Administrative Building	NC	2015-16	75.00	30.00	0.00	0.00	0.00	30.00	30.00	0%	Work not started but only plan estimate vetted by MED	Aug-18
26	Maldah	Old Malda	Old Malda UPHC 2 Ward No. 15 Shibram Pally Mangalbari	NC	2015-16	75.00	30.00	0.00	0.00	0.00	30.00	30.00	0%	Work not started but only plan estimate vetted by MED	Aug-18

22.12.17.

Status of Construction of New U-PHC Building (upto November - 17)

Sl No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected date of completion
A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O	
27	Murshidabad	Berham pur	Behampur UPHC 1 Ward No. 1 Cossimbazar	NC	2013-14	75.00	45.00	45.00	17.58	27.42	0.00	27.42	0%	i) 2nd call already floated and will be opened on 16.08.17 ii) 2nd call cancelled. iii) 3rd call already floated 08.09.2017 iv) 3rd call opened on Technical Papers sent to MED	Aug-18
28	Murshidabad	Berham pur	Behampur UPHC 2 Ward No. 3, Saidabad Khagra	NC	2013-14	75.00	45.00	45.00	37.53	7.47	0.00	7.47	95%		Jan-18
29	Murshidabad	Berham pur	Behampur UPHC 3 Ward No. 8 Kantanagar Khagra	NC	2013-14	75.00	45.00	45.00	29.00	16.00	0.00	16.00	50%		Feb-18
30	Murshidabad	Berham pur	Behampur UPHC 4 Ward No. 21 R.N Tagore Near Laldighi	NC	2013-14	75.00	45.00	45.00	21.58	23.42	0.00	23.42	35%		Mar-18
31	Murshidabad	Dhulian	Dhulian UPHC 1 Dr. APJ Abdul Kalam Azar Ward No. 04 Hatichara Road	NC	2014-15	75.00	22.50	22.50	10.00	12.50	0.00	12.50	40%		Mar-18
32	Murshidabad	Dhulian	Dhulian UPHC 2 Sachindra Nath Roy Ward No. 16 Dighri	NC	2014-15	75.00	22.50	22.50	0.00	22.50	0.00	22.50	0%	Tender process yet to be done	Site Problem
33	Murshidabad	Jangipu r	Jangipur UPHC 1 Ward No. 7 Chhotokalia	NC	2015-16	75.00	30.00	30.00	31.39	-1.39	0.00	-1.39	95%		Jan-18
34	Murshidabad	Jangipu r	Jangipur UPHC 2 Ward No. 3 Gakulpur MathPara	NC	2015-16	75.00	30.00	30.00	0.00	30.00	0.00	30.00	0%	Plan Estimate yet to be done	Fresh modified proposal awaiting
35	Murshidabad	Jiaganj Azimganj	Jiaganj Azimganj UPHC 1 Ward No. 11 Jiaganj Town Centre	NC	2015-16	75.00	75.00	75.00	59.97	15.03	0.00	15.03	100%		
36	Murshidabad	Jiaganj Azimganj	Jiaganj Azimganj UPHC 2 Ward No. 17 Basutitalai More Azimganj Junction	NC	2016-17	75.00	30.00	30.00	42.94	-12.94	0.00	-12.94	60%		Mar-18
37	Murshidabad	Kandi	Kandi UPHC 1 Ward No. 8 Jemo Bagdanga Rajbati	NC	2015-16	75.00	30.00	30.00	0.00	30.00	0.00	30.00	0%	Tender process yet to be done	Aug-18
38	Purba Bardhaman	Burdwan	Burdwan UPHC 6 Ward No. 24 Kanchan Nagar Rath Tala	NC	2013-14	75.00	45.00	29.98	0.00	29.98	15.02	45.00	85%		Mar-18
39	Purba Bardhaman	Kalna	Kalna UPHC 1 Ward No. 17 Ghatakpara	NC	2015-16	75.00	30.00	30.00	0.00	30.00	0.00	30.00	40%		Mar-18

Status of Construction of New U-PHC Building (upto November - 17)

A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O	
Sl. No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected date of completion
40	Purba Bardhaman	Katwa	Katwa UPHC 1 Ward No. 19 Atuhat Chak.	NC	2015-16	75.00	30.00	20.00	0.00	20.00	10.00	30.00	10%	Work not started but tender process completed	Site will change
41	Purba Bardhaman	Katwa	Katwa UPHC 2 Ward No. 7 Sahab Bagan	NC	2015-16	75.00	30.00	20.00	0.00	20.00	10.00	30.00	0%	Work not started but tender process completed	Site will change
42	Rampurhat HD	Rampurhat	Rampurhat UPHC 1 Ward No. 6 Gandhi Park	NC	2013-14	75.00	45.00	30.00	0.00	30.00	15.00	45.00	40%		Mar-18
43	Uttar Dinaipur	Islampur	Islampur UPHC 1 Ward No. 1 Teesta More	NC	2015-16	75.00	30.00	50.00	46.89	3.11	-20.00	-16.89	40%	WORK STOPPED from past 1 year	Mar-18
44	Uttar Dinaipur	Kaliaganj	Kaliaganj UPHC 1 Ward No. 15 R.K. Sarani	NC	2015-16	75.00	30.00	40.00	38.00	2.00	-10.00	-8.00	60%		Feb-18
45	Uttar Dinaipur	Raiganj	Raiganj UPHC 2 Ward No. 02 Sri Ma Sarada Moni Poura Swasthya Seva Kendra Debsahamapara	NC	2013-14	75.00	75.00	22.50	0.00	22.50	52.50	75.00	0%	Work not started. Due to site problems though tender process completed	Due to site problem fresh estimation will be sent to MED for vetting
46	Uttar Dinaipur	Raiganj	Raiganj UPHC 4 Ward No. 21 Mother Teresa Poura Swasthya Seva Kendra Birnagar	NC	2013-14	75.00	75.00	22.50	9.30	13.20	52.50	65.70	30%	Work was stopped for approx 1 yr.; Now just started	Mar-18

21.12.17

Status of Renovation of existing building (upto Nov. - 17)

A	B	C	D	E	F	G	H	I	J	K = I - J	L = H - I	M = K + L	N	O	P
Sl No.	District Name	ULB Name	U-PHC Name	Construction Type	Year of Approval	Amount Entitled / Sanctioned (Rs. in Lakh)	Fund Released from State (Rs. in Lakh)	Fund Released to ULB (Rs. in Lakh)	Cumulative Expenditure (Rs. in Lakh)	Balance at ULB (Rs. in Lakh)	Balance at District / SUDA (Rs. in Lakh)	Total Unspent Balance (Rs. in Lakh)	% of physical completion	Remarks	Expected Date of Completion
1	Hooghly	Baidyabati	Baidyabati UPHC 1 Ward No. 20 Baurlapara Road	R	2014-15	10.00	10.00	10.00	10.00	0.00	0.00	0.00	100%		
2	Hooghly	Baidyabati	Baidyabati UPHC 2 Ward No.6 SCM road Sheoraphuli	R	2014-15	10.00	10.00	10.00	6.02	3.98	0.00	3.98	100%		
3	Hooghly	Bansberia	Bansberia UPHC 1 Kamale Kamini Charitable Dispensary Ward No. 13 Tribeni Bhangaaghat	R	2014-15	10.00	10.00	10.00	10.00	0.00	0.00	0.00	100%		
4	Hooghly	Bansberia	Bansberia UPHC 2 Ward No. 7 Bansberia Municipality Free Primary School beside Ramballav Charitable	R	2014-15	10.00	10.00	10.00	10.00	0.00	0.00	0.00	100%		
5	Hooghly	Bhadreswar	Bhadreswar UPHC 1 Ward No. 9 Segunbagan Telinpara	R	2014-15	10.00	10.00	10.00	10.00	0.00	0.00	0.00	100%		
6	Hooghly	Bhadreswar	Bhadreswar UPHC 2 Ward No. 3 N.S. Road Near Subhashmaldan	R	2014-15	10.00	10.00	10.00	10.00	0.00	0.00	0.00	100%		
7	Hooghly	Champdani	Champdani UPHC 1 Ward No. 13 R.B.S. Road NEAR BANABITTHI PARK	R	2015-16	10.00	10.00	10.00	10.00	0.00	0.00	0.00	100%		
8	Hooghly	Champdani	Champdani UPHC 2 Ward No. 19 NEAR BISS FREE PRIMARY SCHOOL	R	2015-16	10.00	10.00	10.00	10.00	0.00	0.00	0.00	100%		
9	Hooghly	Chandannagar MC	Chandernagore UPHC 1 B.K.G Sishu Hospital Ward No. 7 Dharapara	R	2013-14	10.00	10.00	10.00	9.05	0.95	0.00	0.95	100%		
10	Hooghly	Chandannagar MC	Chandernagore UPHC 3 Ward No. 31 Bramhinpara Khalsani	R	2013-14	10.00	10.00	10.00	7.65	2.35	0.00	2.35	100%		
11	Hooghly	Hooghly Chinsurah	Hooghly Chinsurah UPHC 1 Ward No. 3 Keota Health Unit Sarat Sarani Sahaganl	R	2013-14	10.00	10.00	10.00	10.00	0.00	0.00	0.00	100%		
12	Hooghly	Hooghly Chinsurah	Hooghly Chinsurah UPHC 2 Ward No. 10 Karbala HAU cum ESOPD complex vivekananda Road	R	2013-14	10.00	10.00	10.00	0.00	10.00	0.00	10.00	0%	Work not started but tender process completed and work order issued	Jun-18
13	Hooghly	Hooghly Chinsurah	Hooghly Chinsurah UPHC 4 Ward No. 22 Taldanga HAU Taldanga Road	R	2013-14	10.00	10.00	10.00	8.99	1.01	0.00	1.01	100%		
14	Hooghly	Konnagar	Konnagar UPHC 1 Ward No. 6 1. C.S. Mukherjee Street	R	2015-16	10.00	10.00	10.00	6.10	3.90	0.00	3.90	100%		
15	Hooghly	Konnagar	Konnagar UPHC 2 Ward No. 18 Family Welfare Centre Rajiv Gandhi Road	R	2015-16	10.00	10.00	10.00	6.27	3.73	0.00	3.73	100%		
