

Director, SUDA <wbsudadir@gmail.com>

Meeting Notice

1 message

Joint Secretary MA & UD Department <jsudmadeptt@gmail.com>

Sat, Oct 6, 2018 at 2:44 PM

To: "Director, SUDA" <wbsudadir@gmail.com>, AMRUT westbengal <amrut.wb@gmail.com>, secretarymedte@gmail.com, ceokmda@gmail.com, Sanjay Mukhopadhyay <smdgp13@gmail.com>, Kishore Sengupta <kishoresengupta19@gmail.com>, fa.udma\_wb@gmail.com

-  
- Regards

Special Secretary  
Urban Development & Municipal Affairs Department

Meeting in connection with CSS.pdf  
31K

AD (BNK)  
AD (SC)  
DD (AS)  
CM PM  
Report by today pl.  
ADfa/10

SMAI's  
CPHO  
POH  
107. put up specific problems  
indicating report  
du 09/10/18

**Government of West Bengal**  
**Department of Urban Development & Municipal Affairs**  
**Nagarayan, Block-DF-8, Sector-I,**  
**Salt Lake, Kolkata-700 064**

No: 1193/MA/C-10/1R-6/2017

Dated Kolkata the 6<sup>th</sup> October, 2018.

From:  
Special Secretary to the  
Govt. of West Bengal

To:

1. The Director, SUDA.
2. State Mission Director, AMRUT.
3. Secretary, MED.
4. Chief Engineer, MED.
5. Chief Engineer, KMDA (AMRUT).

Madam/Sir,


Principal Secretary, UD & MA Department will hold a review meeting in respect of Centrally Sponsored Scheme on **10.10.2018 at 5.00 p.m.** at Conference Hall, Nagarayan, 5<sup>th</sup> Floor.

You are requested to make yourself convey to attend the said meeting ULBs wise/project wise updated progress report .

**Specific problem area should be clearly indicated in the said report .**

With thanks,

Yours faithfully,

  
(Special Secretary)

No: 1193/1(3)/MA/C-10/1R-6/2017

Dated Kolkata the 6<sup>th</sup> October, 2018

Copy to:

1. C.E.O., K.M.D.A with a request to spare the concerned engineer(AMRUT) to attend the said meeting along with other officials if any.
2. Financial Advisor, UD & MA Department with a request to attend the said meeting.
3. Personal Secretary to Pr. Secy, UD & Ma Department. With a request to place it before Pr. Secy.

  
Special Secretary.

Asansol MC

Municipal Corporation	No. of U-PHC sanctioned for new construction	No. of U-PHCs where land not identified	No. of U-PHCs where work done up to Plinth level	No. of U-PHCs where construction completed up to 80%	No. of U-PHC where construction either completed or almost completed	Minor renovation done in the existing PHC of H&FW Dept. instead of new construction	Existing land of H&FW Dept.
Asansol MC	12	1	1	1	5	3	1

Howrah MC

Municipal Corporation	No. of U-PHC sanctioned for new construction	No. of U-PHCs where land not identified	No. of U-PHC where land identified but not yet handed over to HMC	No. of U-PHC where land identified but work not initiated	No. of U-PHC where work order given	No. of U-PHC where construction completed or almost completed	
Howrah MC	15	2	5	4	1	3	

WITH  
 LONG  
 COLLARS  
 DHFK  
 RT

Report as on August 2018

SI No.	District	ULB	No. of U-PHC where new construction works was not started	Basirhat HD	Howrah MC	Kandi	Bidhannagar MC	Paschim Bardhaman	Purulia	Uttar Dinajpur	Raiganj	Total
1			2									
2			12									
3			1									
4			3									
5			2									
6			1									
7			1									
												22

OPD	2679621
UHND	54547
Special Outreach Camp	6017

13-14-2

15-16-1

15-14 W

**Govt. of West Bengal**

Health & Family Welfare Department

National Health Mission

GN-29, 4<sup>th</sup> Floor, Swasthya Sathi

Swasthya Bhawan Premises, Sector - V

Salt-Lake, Bidhannagar, Kolkata - 7000091

(033) 2333 0123 (Phone); (033) 2357 7930(Fax)

Email: amdnhmwbhealth@gmail.com \ amd.nrhм@wbhealth.gov.in;

web: www.wbhealth.gov.in

Memo No. HFW-27038/84/2018-NHM SEC-Dept. of H&FW/4843

Date: 14/09/2018

From: **Additional Mission Director, NHM &  
Joint Secretary, H&FW**  
Government of West Bengal

To: **Municipal Commissioner,**  
Howrah Municipal Corporation

**Sub: Request to expedite the progress of new construction of U-PHCs under NUHM**

Sir,

The progress of construction of new U-PHCs under NUHM is very poor in Howrah MC since a long time period. As of now, total fifteen (15) U-PHCs have been sanctioned for construction of new U-PHC building for Howrah MC. But, not a single U-PHC building has been fully completed and functional at newly constructed buildings till date. Although, several reminders have been given from this end to expedite the progress of construction of new U-PHCs.

In this context, State Urban Health Planning Manager from SPMU has visited Howrah MC to explore the hindrance of construction of new U-PHCs on 11<sup>th</sup> & 12<sup>th</sup> September, 2018. He has visited all the sites selected for construction of new U-PHC building jointly with the Nodal Officer, Howrah MC and other officials of CPMU. He also met MMIC (Health) in the evening on 12<sup>th</sup> September, 2018 for debriefing of his observation. A copy of his filed visit report is annexed herewith.

I'd therefore request you to look into the matter personally, so that, the progress of construction of U-PHCs could be expedited and completed within this financial year, otherwise approval of new U-PHC building may have be shifted to other potential places where progress of construction is good for the interest of the overall urban population especially the urban poor and vulnerable sections.

Encl: As stated above.

Yours faithfully,

*Handwritten signature*  
14/09/18

**Additional Mission Director, NHM &  
Joint Secretary, H & F, Govt. of WB**

**Copy forwarded for kind information and necessary action to-**

- 1) **Mayor**, Howrah Municipal Corporation
- 2) **MMIC, (Health)**, Howrah Municipal Corporation
- 3) **Director, SUDA**, West Bengal
- 4) **District Magistrate**, Howrah District
- 5) **Chief Medical Officer of Health**, Howrah District
- 6) **Nodal Officer, NUHM**, Howrah Municipal Corporation

*Donthun*  
14/09/18

**Additional Mission Director, NHM &  
Joint Secretary, H&FW, Govt. of WB**

**Field Observation Report**  
**on construction of new U-PHCs building in Howrah MC**

Date of visit: 11<sup>th</sup> September, 2018

Sl. No.	Site of construction with Ward No.	Observation	Suggested Actions Points
1.	102, I. R. Belilious Lane, Howrah - 1, Ward No. 19 <i>C</i>	<ul style="list-style-type: none"><li>• Civil &amp; Electrical part of construction is almost complete.</li><li>• Furniture and lab equipments are yet to be installed</li><li>• Signage and IEC yet to be arranged</li></ul>	<ul style="list-style-type: none"><li>• To be made functional by 1<sup>st</sup> October, 2018</li><li>• MO &amp; LT to be arranged by the CMOH</li><li>• Support staff to be arranged by the Howrah MC</li><li>• Furniture and lab equipments be installed within September, 2018 by Howrah MC</li><li>• Signage and IEC to be arranged within September, 2018 by Howrah MC</li></ul>
2.	East West Road, Tikiapara, Howrah, Ward No. 22 <i>✓ HIT</i>	<ul style="list-style-type: none"><li>• Site is situated beside Tikiapara Railway Station</li><li>• Land is not yet handover in the name of Howrah MC</li><li>• At present existing land is owned by the Howrah Improvement Trust (HIT) as per record of the Office of the Land and Land Reforms Department, O/o- District Magistrate, Howrah</li></ul>	<ul style="list-style-type: none"><li>• The issue to be discussed with the District Magistrate, Howrah.</li></ul>
3.	Dharsa Govt. Colony, Howrah, Ward No. 47 <i>✓ Land Dept</i>	<ul style="list-style-type: none"><li>• Land is not yet handed over in the name of Howrah MC</li><li>• At present existing land is owned by District Land Department</li></ul>	<ul style="list-style-type: none"><li>• The issue to be discussed with the District Magistrate, Howrah.</li></ul>
4.	Padmapukur, Ward No. 41 <i>Land owned by HMC. Plan &amp; estimation not yet prepared by HMC.</i>	<ul style="list-style-type: none"><li>• Land is owned by Howrah MC.</li><li>• Site is ready for construction.</li><li>• Plan &amp; estimation is not yet prepared.</li></ul>	<ul style="list-style-type: none"><li>• Plan &amp; estimation to be prepared immediately with the help of Engineering Section of Howrah MC</li></ul>
5.	Salimar, Ward No. 39 <i>✓ Railway land</i>	<ul style="list-style-type: none"><li>• Land is owned by the South Eastern Railway</li></ul>	<ul style="list-style-type: none"><li>• Alternative land may be identified immediately.</li></ul>
6.	14, Debendra Ganguly Road, Ward No. 40 <i>Land owned by DHFW. No objection is required by DHFW.</i>	<ul style="list-style-type: none"><li>• Land is owned by the District Health &amp; Family Welfare Department.</li><li>• Demolition of existing abandoned building is required.</li><li>• No objection is needed from the</li></ul>	<ul style="list-style-type: none"><li>• NOC is needed for Howrah MC to establish U-PHC under NUHM.</li><li>• Health &amp; Family Welfare Department to issue NOC.</li></ul>

**Field Observation Report  
on construction of new U-PHCs building in Howrah MC**

Sl. No.	Site of construction with Ward No.	Observation	Suggested Actions Points
		Health & Family Welfare Department to operate U-PHC under NUHM <ul style="list-style-type: none"><li>At present file lying with the Health &amp; Family Welfare Department</li></ul>	
7.	14, Gopal Lal Chowdhury Lane, Howrah, Ward No. 40 <i>land owned by HMC. construction not yet started</i>	<ul style="list-style-type: none"><li>Land is owned by the Howrah MC</li><li>Land is situated behind the old building of Borough No. 5. But at present this building unutilized by Howrah MC</li><li>Work order is issued on 05/07/2018</li><li>Construction is not yet started</li></ul>	<ul style="list-style-type: none"><li>To pursue the matter with the construction wing of Howrah MC for initiation of work.</li><li>Howrah MC may operate U-PHC from the infrastructure of Borough No. 5 till the completion of new U-PHC building.</li></ul>

Date of visit: 12<sup>th</sup> September, 2018

Sl. No.	Site of construction with Ward No.	Physical Progress	Observation and remarks
1.	17, Sita Nath Bose Lane, Howrah - 6, Ward No. 10 <i>c</i>	<ul style="list-style-type: none"><li>Civil &amp; Electrical part of construction is almost complete.</li><li>Furniture and lab equipments are yet to be installed</li><li>Signage and IEC yet to be arranged</li></ul>	<ul style="list-style-type: none"><li>To be made functional by 1<sup>st</sup> October, 2018</li><li>MO &amp; LT to be arranged by the CMOH</li><li>Support staff to be arranged by the Howrah MC</li><li>Furniture and lab equipments be installed within September, 2018 by Howrah MC</li><li>Signage and IEC to be arranged within September, 2018 by Howrah MC</li></ul>
2.	77/31, B. Road, Howrah, Ward No. 7 <i>land owned by private party</i>	<ul style="list-style-type: none"><li>Donation Deed is currently lying with the Law Officer of HMC.</li></ul>	<ul style="list-style-type: none"><li>Deed may be finalised by Howrah MC as early as possible</li></ul>
3.	Bally, Patuapara, Ward No. 63 <i>land not yet identified</i>	<ul style="list-style-type: none"><li>The owner of land of Bally, Patuapara is not yet identified. This is the private property.</li><li>They have explored another alternative site owned by the Howrah MC at Chashipara</li></ul>	<ul style="list-style-type: none"><li>Proceed immediately for construction U-PHC building in the alternative site where ownership of the land is lying with the Howrah MC</li></ul>



**Field Observation Report  
on construction of new U-PHCs building in Howrah MC**

Sl. No.	Site of construction with Ward No.	Physical Progress	Observation and remarks
		beside water tank in Ward No. 63	
4.	36, Bankim Behari Ghosh Lane, Khamarpara, Howrah, Ward No. 56 <i>land owned by private contractor. not started</i>	<ul style="list-style-type: none"><li>• Own land of Howrah MC</li><li>• Work order is issued on 05/07/2018</li><li>• Construction is not yet started</li></ul>	<ul style="list-style-type: none"><li>• To pursue the matter with construction wing of Howrah MC</li></ul>
5.	273, G. T. Road, Muza Barrackpore, Howrah, Ward No. 62 <i>C</i>	<ul style="list-style-type: none"><li>• Civil &amp; Electrical part of construction is almost complete.</li><li>• Furniture and lab equipments are yet to be installed</li><li>• Signage and IEC yet to be arranged</li></ul>	<ul style="list-style-type: none"><li>• To be made functional by 1<sup>st</sup> October, 2018</li><li>• MO &amp; LT to be arranged by the CMOH</li><li>• Support staff to be arranged by the Howrah MC</li><li>• Furniture and lab equipments be installed within September, 2018 by Howrah MC</li><li>• Signage and IEC to be arranged within September, 2018 by Howrah MC</li></ul>
6.	55, A. Naskar Para Road, Howrah - 7, Ward No. 2 <i>land owned by H&amp;FW</i>	<ul style="list-style-type: none"><li>• Land is owned by the Howrah MC</li><li>• Land is insufficient according to the requirement of U-PHC</li><li>• Vertical extension may be needed</li><li>• Demolition of the existing building is to be arranged immediately.</li></ul>	<ul style="list-style-type: none"><li>• To pursue the matter with construction wing of Howrah MC</li></ul>
7.	19, Satyanarayan Temple Road, Salkia, Howrah - 6, Ward No. 4 <i>work order issued. construction not yet started</i>	<ul style="list-style-type: none"><li>• Land ready for construction.</li><li>• Work order issued</li><li>• Demolition of the existing building is under process</li><li>• Construction not started</li></ul>	To pursue the matter with construction wing of Howrah MC

\*\*\*\*\*

*Chandhan*  
14/09/18  
Additional Mission Director, NHM  
& Joint Secretary  
to the Government of West Bengal  
Health & Family Welfare Department

Govt. of West Bengal  
Health & Family Welfare Department  
National Health Mission  
GN-29, 4<sup>th</sup> Floor, Swasthya Sathi  
Swasthya Bhawan Premises, Sector - V  
Salt-Lake, Bidhannagar, Kolkata - 700091  
(033) 2333 0123 (Phone); (033) 2357 7930(Fax)  
Email: amdnhmwbhealth@gmail.com \ amd.nrhm@wbhealth.gov.in;  
Web: www.wbhealth.gov.in

Memo No. HFW-27038/81/2018-NHM SEC-Dept. of H&FW/4788

Date: 11.09.2018

From : Mission Director, NHM  
& Secretary to the Government of West Bengal  
Health & Family Welfare Department

To : Commissioner, Howrah Municipal Corporation

Sub: Non starter for construction of new U-PHCs under NUHM

Madam / Sir,

It is observed from the monthly report of July, 2018 that constructions of new U-PHCs have not been started in 11 places under your jurisdiction as mentioned below.

Sl No.	District Name	ULB Name	Year of Approval	U-PHC Name
1	Howrah	Howrah MC	2015-16	Howrah UPHC13 Ward No 4 Satya Narayan Temple Road Salkia
				Howrah UPHC14 Ward No. 2 A. Naskar Para Road
				Howrah UPHC 16 Ward No. 42 Priya Nath Ghosh Lane
				Howrah UPHC 18 Ward No. 40 Gopal Lal Chowdhury Lane
				Howrah UPHC 19 HAU Ward No. 32 Kaipukur Lane
				Howrah UPHC 20 Ward No. 18 Bankim Park Panchanantala Road
				Howrah UPHC 21 Ward No. 14 I. C. Bose Road Howrah
				Howrah UPHC 22 Ward No. 56 Bankim Behari Ghosh Lane
				Howrah UPHC 24 Ward No. 47 Dharsa Govt. Colony
				Howrah UPHC 25 Ward No. 7 B. Road
				Howrah UPHC 26 Ward No. 55 Khamarpara

Constructions of new U-PHCs are time bound activity and cannot be left undone for indefinite period of time.

You are therefore requested to look in to the matter, fix up a time line for starting as well as finishing of construction for the U-PHCs mentioned above and communicate it to the undersigned at [spmu.nuhm@gmail.com](mailto:spmu.nuhm@gmail.com)

It is to be noted here that construction of the U-PHCs must be started within 30.09.2018.

Yours faithfully,

Mission Director, NHM  
Government of West Bengal

Memo No. HFW-27038/81/2018-NHM SEC-Dept. of H&FW/4788/1(2)

Date: 11.09.2018

Copy forwarded for information and taking necessary action to:

1. Director, State Urban Development Agency (SUDA).
2. Chief Medical Officer of Health, Howrah.

Mission Director, NHM  
Government of West Bengal

**Govt. of West Bengal**  
**Health & Family Welfare Department**  
**National Health Mission**  
**GN-29, 4<sup>th</sup> Floor, Swasthya Sathi**  
**Swasthya Bhawan Premises, Sector - V**  
**Salt-Lake, Bidhannagar, Kolkata - 7000091**  
**(033) 2333 0123 (Phone); (033) 2357 7930(Fax)**  
**Email: amdnhmwbhealth@gmail.com \ amd.nrhm@wbhealth.gov.in;**  
**Web: www.wbhealth.gov.in**

Memo No. HFW-27038/81/2018-NHM SEC-Dept. of H&FW/4787

Date: 11.09.2018

From : **Mission Director, NHM**  
**& Secretary to the Government of West Bengal**  
**Health & Family Welfare Department**

To : **Commissioner, Bidhannagar Municipal Corporation**

**Sub: Non starter for construction of new U-PHCs under NUHM**

Madam / Sir,

It is observed from the monthly report of July, 2018 that constructions of new U-PHCs have not been started in 3 places under your jurisdiction as mentioned below.


Sl No.	District Name	ULB Name	Year of Approval	U-PHC Name
1	North 24 Parganas	Bidhannagar MC	2014-15	Bidhannagar UPHC 1 Ward No. 28 polenite Khashmahal UPHC
				Bidhannagar UPHC 11 Ward No. 7 Rajarhat Gopalpur Mondalganthe Arjunpur
				Bidhannagar UPHC 12 Ward No. 18 Rajarhat Gopalpur Udayanpally

Constructions of new U-PHCs are time bound activity and cannot be left undone for indefinite period of time.

You are therefore requested to look in to the matter, fix up a time line for starting as well as finishing of construction for the U-PHCs mentioned above and communicate it to the undersigned at [spm.u.nuhm@gmail.com](mailto:spmu.nuhm@gmail.com)

It is to be noted here that construction of the U-PHCs must be started within 30.09.2018.


Yours faithfully,

  
**Mission Director, NHM**  
**Government of West Bengal**

Memo No. HFW-27038/81/2018-NHM SEC-Dept. of H&FW/4787/1(2)  
Copy forwarded for information and taking necessary action to:

Date: 11.09.2018

1. Director, State Urban Development Agency (SUDA).
2. Chief Medical Officer of Health, North 24 Parganas.

  
**Mission Director, NHM**  
**Government of West Bengal**

Govt. of West Bengal  
Health & Family Welfare Department  
National Health Mission  
GN-29, 4<sup>th</sup> Floor, Swasthya Sathi  
Swasthya Bhawan Premises, Sector - V  
Salt-Lake, Bidhannagar, Kolkata - 700091  
(033) 2333 0123 (Phone); (033) 2357 7930(Fax)  
Email: amdnhmwbhealth@gmail.com \ amd.nrhm@wbhealth.gov.in;  
Web: www.wbhealth.gov.in

Memo No. HFV-27038/81/2018-NHM SEC-Dept. of H&FW/4783

Date: 11.09.2018

From : Mission Director, NHM  
& Secretary to the Government of West Bengal  
Health & Family Welfare Department

To : Commissioner, Siliguri Municipal Corporation

Sub: Non starter for construction of new U-PHC under NUHM

Madam / Sir,

It is observed from the monthly report of July, 2018 that constructions of new U-PHCs have not been started in 1 place under your jurisdiction as mentioned below.

Sl No.	District Name	ULB Name	Year of Approval	U-PHC Name
1	Darjeeling	Siliguri MC	2015-16	Siliguri UPHC 10 Ward No. 5 Ganganagar near Park

Constructions of new U-PHCs are time bound activity and cannot be left undone for indefinite period of time.

You are therefore requested to look in to the matter, fix up a time line for starting as well as finishing of construction for the U-PHCs mentioned above and communicate it to the undersigned at [spm.nuhm@gmail.com](mailto:spmu.nuhm@gmail.com)

It is to be noted here that construction of the U-PHCs must be started within 30.09.2018.

Yours faithfully,

Mission Director, NHM  
Government of West Bengal

Memo No. HFV-27038/81/2018-NHM SEC-Dept. of H&FW/4783/1(2)

Date: 11.09.2018

Copy forwarded for information and taking necessary action to:

1. Director, State Urban Development Agency (SUDA).
2. Chief Medical Officer of Health, Darjeeling.

Mission Director, NHM  
Government of West Bengal

Govt. of West Bengal  
Health & Family Welfare Department  
National Health Mission  
GN-29, 4<sup>th</sup> Floor, Swasthya Sathi  
Swasthya Bhawan Premises, Sector - V  
Salt-Lake, Bidhannagar, Kolkata - 700091  
(033) 2333 0123 (Phone); (033) 2357 7930(Fax)  
Email: amdnhmwbhealth@gmail.com \ amd.nrhm@wbhealth.gov.in;  
Web: www.wbhealth.gov.in

Memo No. HFV-27038/81/2018-NHM SEC-Dept. of H&FW/4781

Date: 11.09.2018

From : Mission Director, NHM  
& Secretary to the Government of West Bengal  
Health & Family Welfare Department

To : Commissioner, Asansol Municipal Corporation

Sub: Non starter for construction of new U-PHCs under NUHM

Madam / Sir,

It is observed from the monthly report of July, 2018 that constructions of new U-PHCs have not been started in 2 places under your jurisdiction as mentioned below.


Sl No.	District Name	ULB Name	Year of Approval	U-PHC Name
1	Paschim Bardhaman	Asansol MC	2014-15	Asansol UPHC 17 Raniganj (Site not yet finalized)
			2015-16	Barakar, ward no. 67 (new), Kulti

Constructions of new U-PHCs are time bound activity and cannot be left undone for indefinite period of time.

You are therefore requested to look in to the matter, fix up a time line for starting as well as finishing of construction for the U-PHCs mentioned above and communicate it to the undersigned at [spm.u.nuhm@gmail.com](mailto:spmu.nuhm@gmail.com)

It is to be noted here that construction of the U-PHCs must be started within 30.09.2018.

Yours faithfully,


  
Mission Director, NHM  
Government of West Bengal

Memo No. HFV-27038/81/2018-NHM SEC-Dept. of H&FW/4781/1(2)

Date: 11.09.2018

Copy forwarded for information and taking necessary action to:

1. Director, State Urban Development Agency (SUDA).
2. Chief Medical Officer of Health, Paschim Bardhaman.

  
Mission Director, NHM  
Government of West Bengal

**SUDA**

**STATE URBAN DEVELOPMENT AGENCY**

**HEALTH WING**

**"ILGUS BHAVAN"**

**H-C BLOCK, SECTOR-III, BIDHANNAGAR, CALCUTTA-700 091  
West Bengal**

**Ref No. ...SUDA:Health/NUHM/429(Pt.II/18/110(06)**

**Date .....12.09.2018**

**From : Director, SUDA**

**To : The Commissioner  
Asansol / Bidhannagar / Chandernagore / Durgapur /  
Howrah / Siliguri Municipal Corporation**

**Sub. : Observation w.r.t. implementation Status of NUHM at your ULB.**

**Sir,**

This is to inform you that a meeting was held with SUDA at Swasthya Bhawan on 04.07.2018 to review the implementation status of NUHM of 06 Municipal Corporations i.e. Asansol, Bidhannagar, Chandernagore, Durgapur, Howrah and Siliguri. Activity-wise Status report of your ULB is enclosed at **Annexure – I**.

You are requested to furnish the reasons w.r.t. non-functional U-PHCs and poor status of the targeted activities **by 20.09.2018** for taking up the issues with the Authority.

Your active intervention is required to boost up the implementation status.

Thanking you.

Yours faithfully,

**Enclo. : As stated.**

*DDF 12/9/18*

**Director, SUDA**

**SUDA-Health/NUHM/429(Pt.II/18/110(06)/1(2)**

**Dt. .. 12.09.2018**

**CC**

1. The Addl. Mission Director, NHM, DHFW
2. The Sr. PA to the Principal Secretary, UD & MA Dept.

*DDF 12/9/18*

**Director, SUDA**

## Activity-wise Status Report

## a. Non-functioning status of U-PHC

ULB	Total U-PHC sanctioned	No. of non-functioning U-PHC
Siliguri	10	1
Bidhannagar	12	2
Asansol	23	6

## b. OPD attendance at functional U-PHC

ULB	Average no. of patient less than 700 per U-PHC
Siliguri	536
Howrah	556

## c. Special Outreach Camp held against approval

ULB	Less than 50% achievement
Durgapur	03%
Asansol	59%

## d. Clerk and GDA recruitment by the ULB

Asansol MC not yet recruited clerk and GDA @ 23 nos. each.

## e. New Construction of U-PHC vis-à-vis expenditure status

ULB	Approved number	% of physical progress	% of SOE	Remarks
Siliguri	1	0%	0%	No progress observed in comparison to status on Feb., 2018.
Howrah	14	90%- 1 no. 85%- 1 no. 75%- 1 no.	52%	Work order issued for 04 nos. Drawing design under process and will be sent to the MED – for 04 nos. Site not yet finalized for 03.
Asansol	12	100% - 5 no. 75% - 2 nos. 70% - 1 no. 40% - 1 no. 10% - 1 no.	74%	Site not yet finalized for 2
Chandernagore	1	100% - 1 no.	55%	SOE is less though construction work completed.
Durgapur	3	100% - 1 no. 55% - 1 no.	58%	No progress observed in comparison to status on Feb., 2018
Bidhannagar	5	100% - 1 no. 25% - 1 no.	>100%	Site not yet finalized for 3



**STATE URBAN DEVELOPMENT AGENCY****HEALTH WING****"ILGUS BHAVAN"****H-C BLOCK, SECTOR-III, BIDHANNAGAR, CALCUTTA-700 091  
West Bengal**Ref No. ....**SUDA-Health/NUHM/429(Pt.II/18/110(06)**Date .....**06.09.2018****From : Director, SUDA****To : The Commissioner  
Asansol / Bidhannagar / Chandernagore / Durgapur /  
Howrah / Siliguri Municipal Corporation****Sub. : Observation w.r.t. implementation Status of NUHM at your ULB.****Sir,**

This is to inform you that a meeting was held with SUDA at Swasthya Bhawan on 04.07.2018 to review the implementation status of NUHM of 06 Municipal Corporations i.e. Asansol, Bidhannagar, Chandernagore, Durgapur, Howrah and Siliguri. Activity-wise Status report of your ULB is enclosed **at Annexure – I.**

You are requested to furnish the reasons w.r.t. non-functional U-PHCs and poor status of the targeted activities by <sup>20</sup>**14.09.2018** for taking up the issues with the Authority.

Your active intervention is required to boost up the implementation status.

Thanking you.

Yours faithfully,

**Encl. : As stated.**

  
**Director, SUDA**


**SUDA-Health/NUHM/429(Pt.II/18/110(06)/1(2)**

**Dt. .. 06.09.2018**

CC

1. The Addl. Mission Director, NHM, DHFW
2. The Sr. PA to the Principal Secretary, UD & MA Dept.

  
**Director, SUDA**



**NATIONAL URBAN HEALTH MISSION**

**Meeting with SUDA**

**Implementation of NUHM**

**A Status Report**


**Date: 04/07/2018**

### OPD attendance at Functional U-PHC

District	U-PhC	Year of Approval of U-PhC	Total No. of U-PhC Functional	Total no. of patients treated at OPD May-'18	Avg No. of Patient treated at OPD per month per functional U-PhC May-'18
Darjeeling	Siliguri MC	2013-14	9	9648	536
	Chandannagar MC	2013-14	3	11462	1910
Hooghly	Howrah MC	2013-14	27	29997	556
North 24 Parganas	Bidhannagar MC	2014-15	10	34088	1704
	Asansol MC	2013-14	17	28120	827
Paschim Bardhaman	Durgapur MC	2013-14	11	35598	1618
<b>Total</b>			<b>77</b>	<b>148913</b>	<b>967</b>

### Functional Status of U-PHC

District	U-PhC	Year of Approval of U-PhC	Total No. of U-PhC functional	Total No. of U-PhC Functional	Total No. of U-PhC are yet to be Functional
Darjeeling	Siliguri MC	2013-14	10	9	1
Hooghly	Chandannagar MC	2013-14	3	3	0
Howrah	Howrah MC	2013-14	27	27	0
North 24 Parganas	Bidhannagar MC	2014-15	12	10	2
Paschim Bardhaman	Asansol MC	2013-14	23	17	6
	Durgapur MC	2013-14	11	11	0
<b>Total</b>			<b>86</b>	<b>77</b>	<b>9</b>

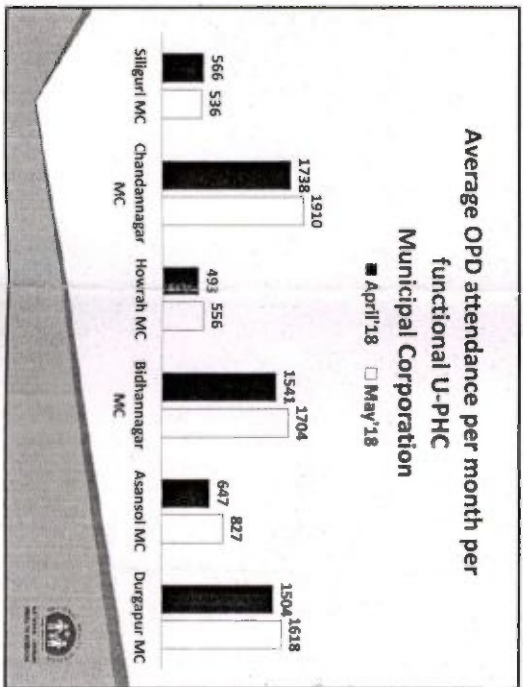


### UHND held against approval

District Name	ULB Name	Physical Progress		Financial Progress (Rs. in Lakh)			
		Upto May'18	% of achievement	Upto May'18	% of Exp. against expected		
Durgeeling	Siliguri MC	344	506	147%	39%		
Hooghly	Chandannagar MC	148	198	134%	100%		
Howrah	Howrah MC	772	1748	226%	16%		
North 24 Parganas	Bidhannagar MC	88	169	192%	100%		
Paschim Bardhaman	Asansol MC	604	432	72%	52%		
	Durgapur MC	232	266	115%	115%		
				2.24	0.77	0.67	


### Special Outreach Camp held against approval

District Name	ULB Name	Physical Progress		Financial Progress (Rs. in Lakh)			
		Upto May'18	% of achievement	Upto May'18	% of Exp. against expected		
Durgeeling	Siliguri MC	60	42	70%	0%		
Hooghly	Chandannagar MC	18	14	78%	99%		
Howrah	Howrah MC	162	135	83%	11%		
North 24 Parganas	Bidhannagar MC	72	70	97%	100%		
Paschim Bardhaman	Asansol MC	138	67	49%	36%		
	Durgapur MC	66	2	3%	>100%		
				7.85	1.32	0.10	

### UHND

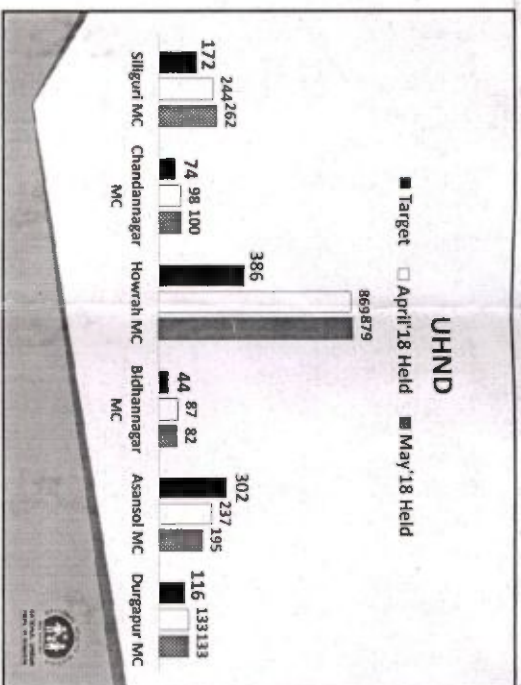

### Monthly Special Outreach Camp

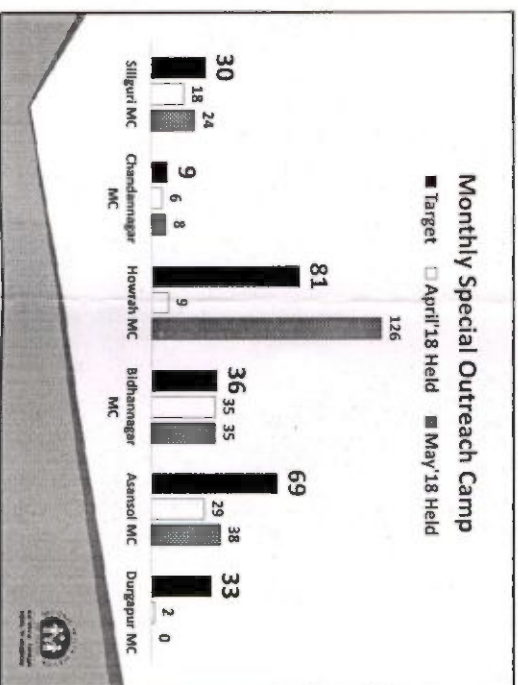

### Preparation of Micro plan of Special Outreach Camp

Name of ULB	May'18			June'18		
	Approved	Planned	Held	Approved	Planned	Held
Bidhanagar MC	36	NA	35	36	NA	Yet to be received
Siliguri MC	30	8	24	30	19	Yet to be received
Chandernaggar MC	9	8	8	9	8	Yet to be received
Howrah MC	81	NA	126	81	NA	Yet to be received
Asansol MC	69	NA	38	69	NA	Yet to be received
Durgapur MC	33	NA	0	33	NA	Yet to be received

\* NA - Not Available

### HR status (May - 18)

ULB Name	Total No. of positions (ULB MC)	FTNO (in position)	FTNO (in position)	Planned (in position)	Staff (in position)	LIC (in position)	Group (in position)	Total in HR	Total Sanction HR	% (Increasing #)	
Durgapur MC	9	3	4	8	2	1	10	10	38	80	48%
Chandernaggar MC	3	3	2	3	3	0	3	3	17	24	71%
Howrah MC	27	10	11	22	14	18	12	12	99	216	46%
Bidhanagar MC	10	4	12	10	3	0	12	12	53	96	55%
Asansol MC	12	15	9	16	2	0	0	0	42	184	23%
Durgapur MC	11	7	11	10	1	0	11	11	51	88	58%

### Progress of New – Construction work of U-PHC (up-to May. 18)

ULB Name	Year of Approval	No. of U-PHC approved by ULB	No. of New U-PHC (in position)	Planned (in position)	Completed (in position)	% of Physical progress	Available Fund (Rs. in Lakh)	Construction Exp. (Rs. in Lakh)	% of Exp. Paid in ULB
Durgapur MC	2013-14	1	0	0	0	0%	10.00	0.0	0%
Howrah MC	2013-14	1	1	1	1	100%	75.00	41.14	55%
Bidhanagar MC	2013-14	14	10	7	3	1 no. - 85% 1 no. - 75%	175.00	91.13	52%
Chandernaggar MC	2013-14	5	3	3	2	1 no. - 100% 1 no. - 25%	30.00	66.16	>100%
Asansol MC	2013-14	12	12	11	10	100% - 2 nos. - 75% - 1 no. - 70% 1 no. - 40% 1 no. - 10%	180.00	133.96	74%
Durgapur MC	2013-14	3	3	2	2	1 no. - 100% - 1 no. - 50%	47.00	27.07	58%

### Progress of Renovation work of U-PHC (up-to May . 18)

ULB Name	Year of Approval	No. of U-PHC approved by ULB	No. of New U-PHC (in position)	Planned (in position)	Completed (in position)	% of Physical progress	Available Fund (Rs. in Lakh)	Construction Exp. (Rs. in Lakh)	% of Exp. Paid in ULB
Durgapur MC	2013-14	9	9	8	8	100%	90.00	89.41	99%
Howrah MC	2013-14	2	2	2	2	100%	20.00	19.70	99%
Bidhanagar MC	2013-14	13	12	12	12	11 nos. - 100% - 1 no. - 50%	110.00	98.48	90%
Chandernaggar MC	2013-14	7	7	7	7	6 nos. - 100% - 1 no. - 85% 1 no. - 40%	60.00	59.87	99.8%
Asansol MC	2013-14	11	11	11	11	100%	110.00	77.68	71%
Durgapur MC	2013-14	8	8	8	8	100%	65.00	50.23	77%

## Meeting Agenda

Monthly Review Meeting with SUDA on 04/07/2018; Time - 03:30 PM

Sl. No.	Activities
1.	Programme review.
2.	Non Communicable Diseases.
3.	Submission of report on formation of MAS and training of MAS
4.	Analysis of HMIS data of Howrah MC (HMC)
5.	Construction issues of HMC
6.	Poor fund booking of different activities in HMC
7.	Miscellaneous.
