



# রাজ্য নগর উন্নয়ন সংস্থা



## STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

ক্রমিক নং SUDA - 376/2019/1829

তারিখ 10. 09. 2020

SUDA-376/2019/

.09.2020

### Memorandum

Release of fund to Bankura Municipality & Halisahar Municipality for construction of Shelter for Urban Homeless.

Funds shown herein are being released electronically in favour of Bankura Municipality & Halisahar Municipality for **construction of Shelter for Urban Homeless** under DAY-NULM. This is the 3 rd (final) installment.

Utilization Certificate of the funds received from SUDA may please be sent to this office in GFR12-C and uploaded at sudawb.org e-services positively within 90 days.

SL. NO	Name of ULB		Central Share (Rs. In Lakh)	State Share (Rs. In Lakh)	Total (Rs. in Lakh)
1	Bankura	3 rd (final) installment	13.60	9.07	22.67
2	Halisahar	3 rd (final) installment	14.49	9.66	24.15

  
Finance Officer, SUDA

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408

SUDA-376/2019/ 1829 1(2)


Dated: 10 .09.2020

Copy for information to:

**Chairperson, BOA/ Finance Officer,  
Banura Municipality, Halisahara Municipality**

He/she is requested to verify that the respective account of NULM of the ULB has duly credited with the sanctioned allotment. For any discrepancy, he/she is requested to report the same immediately to SUDA.

1. SMM-S & SI, NULM



**Finance Officer, SUDA**

o/c

SUDA

সুডা

রাজ্য নগর উন্নয়ন সংস্থা

STATE URBAN DEVELOPMENT AGENCY

‘ইলগাস ভবন’, এইচসি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

‘ILGUS BHAVAN’, HC Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-376/2019/1793

08.09.2020

০৭

From : Finance Officer, SUDA


To : The Branch Manager,  
State Bank of India,  
Salt Lake, Sector-I Branch  
Salt Lake City, Kolkata - 700 064.Sub : Electronic Transfer of Fund debiting this office  
Current Account No.37715094723.


Shelter for Urban Homeless (SUH) – NULM

Sir,


You are requested to kindly arrange for electronic transfer of funds as per details given below debiting the amount from this office Current Account No.37715094723 lying with your branch in respect of Shelter for Urban Homeless (SUH) - NULM.

Sl. No.	Name of the Payee	Amount (in Rs.)	Payees' Bank Details
01.	Bankura Municipality	22,67,000.00	Punjab National Bank, Bankura Branch, A/C No.1295000100112958, IFS Code.PUNB0129500
Total		22,67,000.00	
(Rupees Twenty Two Lakh Sixty Seven Thousand only)			

  
(Petrus Anuranjan Soreng)  
Finance Officer  
SUDA

  
(Goutam Hore)  
Finance Officer  
SUDA.

08.09.2020

  
08/09/2020

দূরভাষ: ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স: ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408

o/c

SUDA

সুডা

রাজ্য নগর উন্নয়ন সংস্থা

STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচসি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, HC Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-376/2019/1792

08.09.2020  
০৭

From : Finance Officer, SUDA

To : The Branch Manager,  
State Bank of India,  
Salt Lake, Sector-I Branch  
Salt Lake City, Kolkata - 700 064.Sub : Electronic Transfer of Fund debiting this office  
Current Account No.37715094723.

Shelter for Urban Homeless (SUH) – NULM


Sir,

You are requested to kindly arrange for electronic transfer of funds as per details given below debiting the amount from this office Current Account No.37715094723 lying with your branch in respect of Shelter for Urban Homeless (SUH) - NULM.

Sl. No.	Name of the Payee	Amount (in Rs.)	Payees' Bank Details
01.	Halisahar Municipality	24,15,000.00	Punjab National Bank, Halisahar Branch, A/C No.4836000100046352, IFS Code.PUNB0483600
T o t a l		24,15,000.00	
(Rupees Twenty Four Lakh Fifteen Thousand only)			



(Petrus Anuranjan Soreng)  
Finance Officer  
SUDA



(Goutam Hore)  
Finance Officer  
SUDA



08/09/2020

08-09-2020

দূরভাষ: ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স: ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408



**Note No. #1**

**Sub: Release of fund (final installment) for construction 50 bedded shelter unit under the scheme Shelter for Urbane Homeless (SUH) under DAY-NULM in favour of Halisahar Municipality.**

A 50 bedded shelter unit under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM at Halisahar Municipality with approved cost of **Rs. 120.75 Lakh** (excluding DPR preparation cost) was approved by Project Sanction Committee (PSC) in its 5 th meeting. Out of which Civil, S&P, Electrical work cost is Rs 107.62 Lakh, Cost for furniture & Utensils is Rs. 8.71 Lakh, WBSEDCL Service connection cost is Rs. 0.50 Lakh, Fire fighting cost is Rs. 0.40 Lakh & Contingency Rs. 3.52 Lakh.

Based on this approval, fund to tune of Rs. 48.30 Lakh+ Rs. 48.30 Lakh (2 nd installment)=**Rs. 96.60 Lakh** was released in favour of Halisahar Municipality in two installments. Now Concerned ULB has submitted the Utilization Certificate. As per report available at this office, construction work of this shelter unit is completed and ready to be functional. Fund has been released as per NULM guidelines Central: State share is 60: 40.

Utilization Certificate of 2 nd installment of construction cost to the tune of Rs. 13.67 Lakh + Rs. 27.11 Lakh = Rs. 40.78 Lakh have been received by this office in GFR 12C duly signed by chairperson, BOA, Halisahar Municipality, Finance Office, Halisahar Municipality & authenticated by Executive Engineer, MED North 24 Division as per prevailing norms. A requisition of fund of 3 rd or final installment has been submitted by the concerned ULB. (Copy placed in the C.P. side)

As per field implementation guidelines of SUH, further installment may be released after receiving of 70% utilization of previous installments. Here 85% UC of previous installment has been received and concerned ULB submitted a claim for 20% of sanctioned Project Cost.

Now an amount of **Rs. 24.15 Lakh** (Central Share Rs. 14.49 Lakh & State Share Rs. 9.66 Lakh) (including 3% contingency) may be released as final installment of sanctioned project cost in favour of the Halisahar Municipality for the settlement of the bills as per prevailing norms.

Submitted for your kind perusal.

03/09/2020 4:32 PM

**SOUMEN DE**  
(SMM-WBSULM(NULM)(SUDA))

**Note No. #2**

An amount of **Rs. 24.15 Lakh** (Central Share Rs. 14.49 Lakh & State Share Rs. 9.66 Lakh) (including 3% contingency) may be released as final installment of sanctioned project cost in favour of the Halisahar

Municipality for the settlement of the bills as per prevailing norms for construction of 50 bedded SUH under NULM.

All previous UCs have been submitted by the ULB

03/09/2020 5:07 PM

SHAON SEN  
(AD DIR(SUDA))

**Note No. #3**

As proposed.

04/09/2020 10:32 AM

SANTANU MUKHERJEE  
(DIR(SUDA))

**Note No. #4**

FO kindly release the fund

04/09/2020 2:19 PM

SHAON SEN  
(AD DIR(SUDA))

**Note No. #5**

Please process.

04/09/2020 5:44 PM

GOUTAM HORE  
(FO(ACCT)(SUDA))

installment has been received and concerned ULB submitted a claim for 3 rd installment of sanctioned Project Cost.

Now an amount of **Rs. 22.67 Lakh** (Central Share Rs. 13.60 Lakh & State Share Rs. 9.07 Lakh) (including 3% contingency) may be released as final installment of sanctioned project cost in favour of the Bankura Municipality for the settlement of the bills as per prevailing norms.

Submitted for your kind perusal.

02/09/2020 6:27 PM

SOUMEN DE  
(SMM-WBSULM(NULM)(SUDA))

**Note No. #18**

An amount of **Rs. 22.67 Lakh** (Central Share Rs. 13.60 Lakh & State Share Rs. 9.07 Lakh) (including 3% contingency) may be released as final installment of sanctioned project cost in favour of the Bankura Municipality for the settlement of the bills as per prevailing norms for construction of 50 bedded SUH under NULM .

All previous UCs have been submitted by the ULB.

03/09/2020 5:30 PM

SHAON SEN  
(AD DIR(SUDA))

**Note No. #19**

As proposed.

04/09/2020 10:34 AM

SANTANU MUKHERJEE  
(DIR(SUDA))

**Note No. #20**

FO kindly release the fund

04/09/2020 2:19 PM

SHAON SEN  
(AD DIR(SUDA))

**Note No. #21**



(SMM-WBSULM(NULM)(SUDA))

**Note No. #16**

07/08/2020 4:49 PM

SHAON SEN  
(AD DIR(SUDA))**Note No. #17**

**Sub: Release of fund (final installment) for construction 50 bedded shelter unit under the scheme Shelter for Urbane Homeless (SUH) under DAY-NULM in favour of Bankura Municipality.**

A 50 bedded shelter unit under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM at Bankura Municipality with approved cost of **Rs. 113.27 Lakh** (excluding DPR preparation cost) was approved by Project Sanction Committee (PSC) in its 6 th meeting. Out of which Civil, S&P, Electrical work cost is Rs 100.36 Lakh, Cost for furniture & Utensils is Rs. 8.71 Lakh, WBSUEDCL Service connection cost is Rs. 0.50 Lakh, Fire fighting cost is Rs. 0.40 Lakh & Contingency Rs. 3.30 Lakh.

It may be further noted that beyond this Project Cost of SUH, additional Rs. 124.34 Lakh was sanctioned from Municipal Affairs Dept beyond NULM fund on 20.12.2016 based on the revised DPR as vetted by Executive Engineer, MED, Bankura Division & estimated cost comes to Rs. 217.66 Lakh. As this amount was sanctioned by the Municipal Affairs Dept. and subsequent fund had been release to the ULB, therefore the UC of this amount has been submitted to the concerned Dept by the Bankura Municipality. There is no such connection with this revised amount with the NULM fund as the project was sanctioned Rs. 113.27 Lakh.

Based on this approval, fund to tune of **Rs. 90.60 Lakh** was released in favour of Bankura Municipality in two installments. Now Concerned ULB has submitted the Utilization Certificate. As per report available at this office, construction work of this shelter unit is done 80%. Fund has been released as per NULM guidelines Central: State share is 60: 40.

Utilization Certificate of 2 nd installment of construction cost to the tune of **Rs. 45.30 Lakh** have been received by this office in GFR 12C duly signed by Chairman, BOA, Bankura Municipality, Finance Officer Bankura Municipality & authenticated by Executive Engineer, MED Bankura Division as per prevailing norms. A requisition of fund of 3 rd or final installment has been submitted by the concerned ULB. (Copy placed in the C.P. side)

As per field implementation guidelines of SUH, further installment may be released after receiving of 70% utilization of previous installments. Here 100% UC of previous



# WEST BENGAL STATE URBAN LIVELIHOOD MISSION

(Under Municipal Affairs Department, Government of West Bengal)

"ইলগাস ভবন", এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা ৭০০ ১০৬, পশ্চিমবঙ্গ।

"ILGUS BHAVAN", H-C Block, Sector-III, Bidhannagar, Kolkata 700 106, West Bengal.

SUDA-376/2019/৭৪৭০

Date: 19/02/2020



## Memorandum

Release of fund to Bankura Municipality for construction of shelter for Urban Homeless under DAY-NULM

Funds shown herein are being released electronically in favour of Bankura Municipality for 'construction of shelter for urban homeless' under DAY-NULM. This release is the 2<sup>nd</sup> installment.

Utilisation Certificate of the funds received from SUDA may please be sent to this office in GFR-12C and uploaded at [sudawb.org](http://sudawb.org) → e-services positively within 90 days.

SL NO.	Name of ULB	Amount (Rs. In lakh)		Total
		Central Share	State Share	
I.	Bankura Municipality	27.18	18.12	45.30

  
Finance Officer, SUDA  


দুরভাষ: ২৩৫৮ ৬৪০৩/৬৪২১/৫৭৬৭, ফ্যাক্স : ২৩৫৮৫৮০০

Tel: 2358-6403/6421/5767, Fax: 2358-5800, E-Mail: [wbsulm@gmail.com](mailto:wbsulm@gmail.com)

SUDA-376/2019/9470/1(2)



19.02.2020

Copy for information to:

1. Chairman / Executive Officer of Bankura Municipality.

He/she is requested to verify the respective Account of NULM of ULBs that the sanctioned amount has duly been credited. For any discrepancy, he/she is requested to report the same immediately to SUDA.

2. SMM, S&SI, NULM.

  
Finance Officer, SUDA  


## STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-376/2019/ ৭৭০১

ক্রমিক নং .....

তারিখ 14.02.2020


From : Director, SUDA

To : The Manager,  
State Bank of India,  
Salt Lake City, Kolkata - 700 091.**Sub: Electronic Transfer of Fund debiting this office  
Current Account No. 37715094723****Shelter for Urban Homeless under NULM**


Sir,


You are requested to kindly arrange for electronic transfer of funds as per details given below debiting the amounts from this office Current Account No.37715094723 lying with your branch in respect of **construction cost of SUH under DAY-NULM.**

Sl. No.	Name of Payee	Amount (In Rs.)	Payees' Bank Details
01	Bankura Municipality	45,30,000.00	Punjab National Bank, Bankura Branch, A/C No. 1295000100112958, IFS Code. PUNB0129500
TOTAL		45,30,000.00	
(Rupees forty five lakh thirty thousand only)			

  
(Petrus Anuranjan Soreng)  
Finance Officer  
SUDA

  
13/02/2020

  
(Debarati Dutta Gupta)  
Director  
SUDA



দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408







# Office of the Municipal Councillors of Bankura

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 , Mobile: 09434115191

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)

: [senguptamahaprasadcm@yahoo.in](mailto:senguptamahaprasadcm@yahoo.in)

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org)

From: *Sri Mahaprasad Sengupta*

Chairman, Bankura Municipality

Memo. No. / VIII-14

Dated, Bankura : / /19.

To  
The Executive Engineer,  
M.E.Dte., Bankura Division,  
Kenduadihi,  
Bankura.



*AD(TC)*

Ref:- Application submitted by Sri Kartick Sen vide this office memo no.- 5672/m, dated-24/09/2019 and your letter no.- MED/BKU/455/NULM-1/2015, dated 17/09/2019.

Sub:- Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM. Layout Plot No. 817(RS), Mouza- Bankura, JL No. 211, Bankura.

Sir,

You please find herewith the copy of the letter submitted by Kartick Sen, the Agency of the above subjected works which speaks itself. This is forwarded for your information and take necessary action form your end.

Your early action may solicit to resume the work.

Thanking you.

Annexure :- As Stated.

*SKT*  
Chairman  
Bankura Municipality

Memo no:- *2240* (3)/VIII-14, Dated:- *26/09/19*.

Copy forwarded for information,

- ✓ The Director SUDA, Bidhan Nagar, Salt Lake, Kolkata 700106.
2. The Chief Engineer, M.E.Dte., Bikash Bhaban, Kolkata 700067.
3. The Superintending Engineer, M.E.Dte.(South Circle), Kousallya, Khargapur.

*26/09/19*  
Chairman  
Bankura Municipality

*28/09/19*  
Chairman  
Bankura Municipality

M 5672  
24.9.19

# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Ref. No. ....

Date 24-09-2019

TO  
The Chairmen  
Bankura Municipality

Sub:- Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM, Layout Plot No. 817 (RS), Mouza – Bankura , JL No 211, Bankura

Ref:- Your office memo No- 2144/VIII-14 Dated- 20-09-2019

মাননীয় মহাশয়,

আপনার নিকট জানাই যে, গত ইংরেজি ০৫/০৯/২০১৯ তারিখের নির্দেশ অনুযায়ী ১২/০৯/২০১৯ তারিখ হইতে কাজ শুরু করিয়াছি। বর্তমানে আপনার চিঠির পরিপেক্ষিতে জানাই যে উক্ত কাজটি সম্পন্ন করিতে, প্রতাহ কাজ করিলে, কমপক্ষে ৩১.০৩/২০২০ তারিক পর্যন্ত সময় প্রয়োজন। মহাশয়ের নিকট আবেদন যাহাতে উক্ত সময় পর্যন্ত অতিরিক্ত সময় দেওয়া হয়, তাহার প্রয়োজনীয় ব্যবস্থা গ্রহন করিবেন।

ধন্যবাদান্তে

বিনীত

KARTICK SEN

  
Proprietor

Copy forwarded for information,

1. The Superintending Engineer, M.E. Dte (South Circle), Kousallya Kharapur
2. The Executive Engineer, M.E. Dte. Bankura Division, Kenduadihi, Bankura

S. A. E. (P.W.D.) to  
ref for 24.09.19



UD/00/2019/12920

**GOVERNMENT OF WEST BENGAL**  
**OFFICE OF THE CHIEF ENGINEER**  
**Municipal Engineering Directorate**

Bikash Bhawan, South Block (1<sup>st</sup> Floor) Salt Lake, Kolkata – 700091.

Phone No: (033)2337-1331/ (033)2358-3347 \ Fax: (033) 2337-5474

E-mail: ce\_medte@yahoo.com

S. Dey S.M.A.  
Needs a further  
discussio

24.09.19

No. ME/ 665/1M-54/2014 Pt. VII

Dated: 23/09/19

From : The Chief Engineer  
M. E. Dte.  
Bikash Bhavan

To : Sri Joly Choudhuri  
Joint Secretary, UD & MA Deptt.  
& Addl. Mission Director, WBSULM,  
Government of West Bengal,  
Nagarayan, DF-8, Sector-I,  
Salt Lake City, Kolkata – 700064.



3830  
23/9/19

**Sub : NULM Project under Bankura Municipality**

Sir,

This has a reference to the meeting held on 30.08.2019 regarding review on NULM projects and the project concern of Bankura was referred by the concerned Junior Engineer of Bankura Municipality with the comment that the execution of the work will be resumed by the contractor immediately, though the agency had submitted letter earlier with the consent that he will not execute further works until and unless the balance materials are supplied by the Department, for obvious reasons of change of drawing etc. etc. after issuance of work order.

Based on the facts and deeds, the time passed since inception of work, impact on schedule of rates etc. etc. the matter was taken up with the concerned Superintending Engineer and all correspondences in this respect are enclosed herewith for a close view with the aspect that if the work is suspended for the issue and a further time lapse of minimum 6 months is taken for just measurement, settlement of payment and estimation of balance work and processing of tender and if in that case, the rate becomes higher then also it will become questionable and also if the agency demands for excess payment for issuance of materials for deviation of drawing w.r.t the drawing referred in the NIT, then also the legal aspect will obviously support the claim of the agency. On that ground the balance materials may be supplied, I think, based on the ground reality for the interest of public supporting by a notesheet with any financial implication for the same or not and in so many occasions it is adopted for the interest of public and may it be judged from PWD officials point of view, if deemed so.

Yours faithfully,

- Encl : i) Minutes of meeting held on 30.08.19  
ii) MED/SE(S)/153/NULM-1/15 Pt. I dt. 21.08.19  
iii) ME/509/1M-54/2014 Pt. IV dt. 21.08.19  
iv) ME/240/1M-54/2014 Pt. IV dt. 14.06.19

Chief Engineer, MED

**Minutes of the review meeting on physical & financial progress of sanctioned shelter units under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM**

**Date:** 30.08.2019

**Time:** 02 pm

**Venue:** SUDA Conference Hall

**Officials Present:**

- 1) Sri Joly Chaudhuri, WBCS (Exe)..... Jt. Secretary, UD & MA
- 2) Sri Kaushik Das.....Secretary, MED
- 3) Sri Amit Das.....Chief Engineer, MED
- 4) Sri Soumen De.....SMM- S & SI, WBSULM

**Others Present:**

- 1) Superintendent Engineers & Executive Engineers, MED
- 2) ULB representatives (Municipal Engineers/ Nodal staff looking after SUH)

Sri Joly Chaudhuri, Addl. Mission Director, WBSULM presided at the meeting.

**Agenda: Present physical & financial progress of ongoing work of SUH & tentative date of completion of ongoing project.**

After detail deliberation the following decisions have been taken.

SI No.	Name of ULB	Decision points	Remarks
1	Kolkata	a. Functionalization of the completed shelter unit at 13,Rajamanindra Road(1 <sup>st</sup> floor) at Ward no-5	a. Shelter to be made functional within Sept, 2019
		b. Completion of SUH at Latafat Hosein Road at Ward no 49 & SUH at Ward no-122	b. It is suggested to complete the construction works & to procure furniture & utensils for the aforementioned SUHs by Nov,2019
2	Howrah	a. Alternative land identified	a. Soil investigation report to be submitted to EE, MED within 20.09.2019 & prepare DPR and submit within 30 <sup>th</sup> Sep, 2019.
		b. Submission of full UC of the completed shelter unit	b. Final UC to be submitted by HMC within 15.09.2019
3	Asansol	a. Initiatives regarding functionalization of newly constructed shelter unit Raniganj	a. SUH at Raniganj to be operationalization immediately.



		b. Completion of construction of Kulti SUH	b. SUH Kulti to be made functional within 31 st Oct, 2019. An abandoned building just beside the under construction SUH to be demolished immediately.
		c. NOC for alternative land at Asansol	c. Secretary, AMC informed to take appropriate action for NOC for alternative land for SUH, Asansol
4	Chandernagar	a. Submission of final UC	a. Final bill of construction work of SUH to be raised immediately.
		b. Necessary repair works in functional SUH building	b. Repair work of the SUH to be taken up immediately.
6	Berhampore	a. Submission of final UC	a. Final bill of construction work of SUH to be raised immediately.
		b. Initiatives regarding functionalization of shelter unit	b. EO, Berhampore informed about functionalization of the SUH at the earliest. Timeline 15.09.2019
7	Barrakpore	a. Resume the construction work of SUH and necessary action for remaining work under the technical supervision of MED	a. EO, Baraackpore informed about construction work b. It was directed to EO, Barrackpore that a declaration will be submitted by municipality the regarding liability of execution of existing works
8	Halisahar	a. Expedite the construction work b. Submission of pending UC	a. EO, Halisahar directed to take necessary action for functionalization of the shelter unit & to float the tender for boundary wall of SUH
10	Bhatpara	a. Progress of construction work	a. ULB representative informed that the construction work will be resumed from 03.09.2019
		b. Submission of pending UC	b. ULB representative informed to submit UC as per the progress of work
11	Bankura	a. Resumption of the construction work b. Mitigate the issues related construction work with the contractor	a. SAE, Bankura municipality informed that the construction agency has agreed to start the work from next week
12	Uttarpara-Kotrang	a. Resumption of the construction work	a. EE, MED informed that necessary instruction has been given to concerned agency to start the work immediately.
13	Titagarh	a. Completion of tender process	a. NIT to be invited centrally from MED

15	Barasat	a. Completion of the construction work within the timeline	a. EE, MED informed that finishing works in process and the construction work will be completed within 30.09.2019 b. ULB representative directed to procure the furniture & utensils at the earliest and to inaugurate the shelter unit within October,19 c. EE, MED informed that an estimate for additional fund for installation of ornamental grill & drainage in SUH was submitted.
16	North Dum Dum	a. Completion of tender process	a. NIT to be initiated centrally from MED
17	Jiaganj-Azimganj	a. Report regarding deviation of work	a. CE, MED was requested to submit the report at the earliest b. Concerned EE, MED directed to send the detail report regarding the deviation
18	Balurghat	a. Early functionalization of the completed SUH by 15 th September b. Submission of UC	a. ULB representative to meet A.D.M Dakshin Dinajpur District regarding the problem of functionalization of SUH and report back on 03.09.2019 b. EE, MED to send the final UC of construction work
19	Tarakeswar	a. Early functionalization of the completed SUH by 15 th Sep,19 b. Submission of UC	a. . EO, Tarakeswar directed to take necessary action for functionalization of the shelter unit within 15.09.2019 b. Concerned Municipal Engineer suggested to complete the billing process of construction work and to submit the UC 15.09.2019
20	Madhyamgram	a. Completion of construction	a. AE, Madhyamgram Municipality informed about the progress of work b. Construction work will be completed within 30 th Nov,19
21	Dum Dum	a. Completion of construction work within the timeline	a. Concerned Municipal Engineer informed about the progress of work & also informed that for construction of the building a road was diverted and necessary fund will required for restoration work. It was suggested to submit the estimate of this work to the UD & MA Dept. through RSP
22	Naihati	a. Resumption of the construction work	a. Construction work has resumed and is in progress




23	Kaliyaganj	a. After completion of tender process construction work should be completed within the timeline	NIT to be initiated centrally from MED
24	Beldanga	a. After completion of tender process construction work should be completed within the timeline	a. NIT to be initiated centrally from MED
25	Islampur	a. Expedite the construction work	a. EE, MED to submit revised estimate of SUH as per site requirement to SUDA through Chief Engineer, MED within 15.09.2019.
		b. Submission of pending UC	b. EE, MED was requested to submit updated UC of SUH within 15.09.2019
26	Santipur	a. Submission of pending UC	a. EE, MED to send the bill within 10.09.2019 to ULB for submission of UC
		b. Expedite the construction work	b. Completion of construction work 31 st Dec, 2019

#### Miscellaneous

1. Progress of tender process for construction work of Boundary Wall of SUH has been reviewed and concerned ULBs were informed to complete the work within timeline
2. It was directed to submit the necessary estimate for installation of ornamental grill of SUH where it is required.
3. A detailed deliberation was made on the process of fund release to MED for centrally executed construction work of SUH. CE, MED informed that MED has no such dedicated bank account to release fund and release of payment. It is decided that suitable action in this regard will be taken the Department.
4. All Executive Engineers, concerned Division, MED were requested to send the revised plan & estimates of SUH to SUDA through Chief Engineer, MED

The meeting ended with a vote thanks to and from the Chair.

  
 16/09/19  
 Joly Chaudhuri  
 Joint Secretary, UD & MA Dept.  
 & Adl. Mission Director, WBSULM

1-54/14 P.E - VII



739584/2019/SEC(MED)

29.8.19

Government of West Bengal  
Office of the Superintending Engineer (South Circle)  
Municipal Engineering Directorate  
Koushalya, P.O: Kharagpur, Dist: Paschim Medinipur

No MED / SE(S) / 159 / NULM-1 / 15 Pt. I

Dated 21.08.2019

Chief Engineer  
Municipal Engineering Directorate  
Bikash Bhavan (South Block), 2<sup>nd</sup> Floor  
Salt Lake City  
Kolkata-700091


Sub: Reply on the Stalemate of NULM building within Bankura Municipality  
Ref: ME/509/1M-54/2014, Pt-IV, Dated 21.08.2019

Sir

Points raised by you in your letter referred to above vis-à-vis the replies have been furnished below:

Sl No	Points raised	Reply
1	Whether BOQ quantity of reinforcement for the work has been consumed...	Out of 55.50MT of BOQ quantity, 56.49MT has already been consumed.
2	Relaxation of which rule has been asked for?	Agreement for the work was entered with the clause of departmental supply. Departmental supply for the same work will contradict the agreement. A note of consent from the Authority will obviate such contradiction and the Audit query in future.
3	Whether 6754-PW/L&A/2M-312/2017, dated 18.12.2017 can be made use of in favour of departmental supply of reinforcement	6754-PW/L&A/2M-312/2017, dated 18.12.2017 has modified the Rules 238 and 239 of PWD Code which deal with excess quantity/supplementary/substitute items of a work. Application of the modified rule can definitely be applied if and only if the contractor supplies the materials.
4	Suggestion	If the contractor does not come out of the idea of departmental supply, steps should be initiated as per tender clause for keeping the work suspended for more than 6 (six) months even after requesting several times by Division office to start the work.

Yours sincerely

 21/08/2019

Superintending Engineer, South Circle  
Municipal Engineering Directorate

Superintending Engineer  
South Circle, M.E. Dto.  
Govt. of West Bengal  
Dept of M.A.

C.E. on B. D. U.  
May 12/19, he sent  
2018



**GOVERNMENT OF WEST BENGAL**  
**OFFICE OF THE CHIEF ENGINEER**  
**Municipal Engineering Directorate**

Bikash Bhawan, South Block (1<sup>st</sup> Floor) Salt Lake, Kolkata – 700091

Phone No: (033)2337-1331/ (033)2358-3347 Fax: (033) 2337-5474

E-mail: ce\_medte@yahoo.com

No. ME/ 509/14-54/2014 Pt-IV

Dated 21/08/19

From: The Chief Engineer,  
Municipal Engineering Directorate.


To: The Superintending Engineer,  
South Circle,  
M. E. Dte.

**Sub: Stalemate of NULM building within Bankura Municipality**

**Ref: Your office memo no. MED/SE(S)/82/NULM-1/15 Pt. I dt. 20.06.2019**

With reference to the subject cited above he is requested to let this office know the following :

- i) Whether the agency executed supplied the quantity(s) in full with respect to BOQ (as per contract agreement) for the items for which departmental supply have asked by the agency or not.
- ii) It was referred vide your aforesaid memo as “ Relaxation in respect of departmental supply of the balance reinforcement should come from the competent authority so that it can be given effect to.” ‘Relaxation’ of which rule is asked for. Document containing such rule should be enclosed which will be required to forward to the competent authority.
- iii) Finally let it be informed that is it clear to you that provision of issuance of deptt. supply in addition to the contract provision of agency supply, in excess of the desired quantity as per agreement can't be made for the interest of work or as per Order no. 6754 – PW/L&A/2M-312/2017 dt. 18.12.2017?? If so, in that case what is your suggestion as concerned SE of the project, i) to escalate the matter to higher authority or ii) to make an amicable earliest solution of the same. For your information, already a period of five months have been lost on this issue only. Please convey your message positively by 22.08.19.

  
21.08.19  
Chief Engineer, MED

No. ME/ 509/1/14-54/2014 Pt-IV

Dated

Copy forwarded for information to:-

1. The Executive Engineer, Bankura Division, MED

  
21.08.19  
Chief Engineer, MED



Government of West Bengal  
Office of the Superintending Engineer (South Circle)  
Municipal Engineering Directorate  
Koushalya, P.O: Kharagpur, Dist: Paschim Medinipur

No MED / SE(S) 1821 NULM-1 / 15 Pt. I

Dated 20.06.2019

✓ Chief Engineer  
Municipal Engineering Directorate  
Bikash Bhavan (South Block), 2<sup>nd</sup> Floor  
Salt Lake City  
Kolkata-700091

Sub: **Stalemate of NULM building within Bankura Municipality**  
Ref: ME/240/1M-54/2014, Pt-VI, Dated 14.06.2019

Sir

In my earlier communications, I have clearly stated that the running agency has categorically demanded for departmental supply for the balance quantity of reinforcement which is more or less 23MT. I have also stated that departmental supply and supply by the contractor can not operate simultaneously in a tender. PWD Order No 6754-PW/L&A/2M-312/2017, dated 18.12.2017 has nothing to do with the instant case. Relaxation in respect of departmental supply of the balance reinforcement should come from the competent Authority so that it can be given effect to.

Yours sincerely

*[Signature]* 20<sup>06</sup> 2019  
Superintending Engineer, South Circle  
Municipal Engineering Directorate

Superintending Engineer  
No MED / SE(S) 1821 NULM-1 / 15 Pt. I  
South Circle, M.E. NULM  
Govt. of West Bengal  
Copy to: Dept of M.A.

Dated 20.06.2019

Executive Engineer, Bankura Division, M E Directorate.

Superintending Engineer, South Circle  
Municipal Engineering Directorate

C.S. MB STB

By *[Signature]* he seen  
18/7.

**GOVERNMENT OF WEST BENGAL**  
**OFFICE OF THE CHIEF ENGINEER**  
**Municipal Engineering Directorate**

*Bikash Bhawan, South Block (1<sup>st</sup> Floor) Salt Lake, Kolkata – 700091*

*Phone No: (033)2337-1331/ (033)2358-3347 \ Fax: (033) 2337-5474*

*E-mail: ce\_medte@yahoo.com*

No. ME/ 240/IM-59/14 Pt - VI

Dated: 14.06.19.

From : The Chief Engineer  
M. E. Dte.  
Bikash Bhawan, Salt Lake,  
Kolkata


To : The Superintending Engineer,  
South Circle, M. E. Dte.

**Sub : Report of the present status of NULM building within Bankura Municipality**

**Ref : (1) MED/SE(S)/69/NULM-1/15 Pt. -I dt. 11.06.19**  
**(2) MED/SE(S)/30/NULM-1/15 Pt. -I dt. 26.04.19**  
**(3) MED/BKU/202/NULM-1/15 Pt. -II dt. 18.04.19**

With reference to the subject cited above he is requested to take necessary action to complete the work within the tendered amount observing rules 238 & 239 of PWD code as amended vide G.O. No. 6754-PW/ L & A/2M-312/2017 dt. 18.12.2017.

He is also requested to do the needful so that the agency would resume the work without further delay. This may be noted that if the situation demands, for the interest of work, for saving of time and in anticipation of assessing the gravity of the situation towards enhancement of cost for termination of contract, joint measurement and selection of new agency, some relaxations may always be acceptable for the interest of work, may it be for the issuance of reinforcement or any others. However, as an acting in charge of Superintending Engineer concerned for the work in concern he is supposed to take actions accordingly. Regarding completion value of the revised work concerned, the memo no. MED/BKU/202/NULM-1/15 Pt. -II dt. 18.04.19, as referred above, from the Executive Engineer concerned, is vital and the concerned evaluation document from Executive Engineer's end may please be consulted with, if possible, with the agency also for the interest of work.

  
14.06.19  
Chief Engineer, MED



**GOVERNMENT OF WEST BENGAL**  
**OFFICE OF THE CHIEF ENGINEER**  
**Municipal Engineering Directorate**

Bikash Bhawan, South Block (1<sup>st</sup> Floor) Salt Lake, Kolkata - 700091

Phone No: (033)2337-1331/ (033)2358-3347 \ Fax: (033) 2337-5474

E-mail: ce\_medte@yahoo.com

No. ME/

Dated:

From : The Chief Engineer  
M. E. Dte.  
Bikash Bhawan, Salt Lake,  
Kolkata

To : The Superintending Engineer,  
South Circle, M. E. Dte.

**Sub : Report of the present status of NULM building within Bankura Municipality**

**Ref : (1) MED/SE(S)/69/NULM-1/15 Pt. -I dt. 11.06.19**  
**(2) MED/SE(S)/30/NULM-1/15 Pt. -I dt. 26.04.19**  
**(3) MED/BKU/202/NULM-1/15 Pt. -II dt. 18.04.19**

With reference to the subject cited above he is requested to take necessary action to complete the work within the tendered amount observing rules 238 & 239 of PWD code as amended vide G.O. No. 6754-PW/ L & A/2M-312/2017 dt. 18.12.2017.

He is also requested to do the needful so that the agency would resume the work without further delay other-wise ~~penal action to be taken as per contract agreement.~~

*within may be  
intercept of work, as for saving of time and  
in anticipation of assessing the gravity of the situation  
towards enhancement of cost for termination  
of contract, joint measurement  
and selection of new agency, some relaxations  
may always be acceptably for the interest  
of work, may it be for the resumption of reinforcement  
or any others. However, as an acting  
incharge of SE concerned for the  
work in concern, he is supposed to  
take actions accordingly. Regarding completion  
value of the work concerned, the memo  
no 202, dated 18.04.19, as referred above, from  
the EE concerned, is vital and the concerned  
evaluation document from EE's end may pls  
be consulted with, if possible, with the  
agency also for the interest of work.*



UD/21/2019/01293 27.02/05/19



Government of West Bengal  
Office of the Superintending Engineer (South Circle)  
Municipal Engineering Directorate  
Koushalya, P.O: Kharagpur, Dist: Paschim Medinipur

No MED / SE(S) / 30 / NULM-1 / 15 Pt. I

Dated 26.04.2019

Chief Engineer  
Municipal Engineering Directorate  
Bikash Bhavan (South Block), 2<sup>nd</sup> Floor  
Salt Lake City  
Kolkata-700091

*Sumit*  
*Pls discuss. Pls draft a reply.*  
Sub: Report on the present status of NULM building within Bankura Municipality

Please find enclosed herewith the Status Report of NULM building within Bankura Municipality along with a report from the Executive Engineer, Bankura Division, M E Directorate.

Yours sincerely

*King* 26/04/2019  
Superintending Engineer, South Circle  
Municipal Engineering Directorate  
SUPERINTENDING ENGINEER  
South Circle, M. E. Directorate  
Deptt. of Municipal Affairs  
Govt. of West Bengal

*e B MEDU*  
*May 1st/13th*  
*6/13/19*

REPORT ON THE PRESENT STATUS OF NULM WITHIN BANKURA MUNICIPALITY

Ref: ME/79/1/1M-54/2014, Pt-IV, Dated 17.04.2019

The site that was allotted for construction of the NULM building was not free from encumbrances and there were temporary stalls on the site. Clearance of the site was made after 6 months and so even though the Work Order was issued on 22.05.2017, actual work for foundation took place sometime in January, 2018. So the contractor had to suffer for such lapse of time. Thereafter, base on pile load test conducted on a test pile, the foundation design was changed from pile foundation to raft foundation and the height of the building was modified from (G+4) to (G+2) with increased floor area to provide the same facilities of the model plan of NULM. Such increased area of the building with modified foundation **has caused a substantial increase in steel consumption** which according to the contractor works against him. The contractor has now stopped any further work of the building and asking for departmental supply of the balance reinforcement beyond the tendered quantity. In this context it is to be stated that the Tender Form which is an essential part of the agreement between the Tender Inviting Authority and the contractor allows for change in drawing and design, if required. Regarding departmental supply of steel material, such request on the part of the contractor cannot be entertained because in a particular tender, **departmental supply and own supply cannot operate simultaneously without infringing the financial rules.** The real issue is that the contractor won the contract offering 13.95% less without knowing that recent GO restricts the total expenditure of any work within tendered amount and late realization of the spirit of the GO pinches the contractor the most; otherwise there is hardly any merit in what the contractor says in the letter.

why?

Do more  
any clause  
to refrain  
the contractor  
from demanding  
such?

cause of  
change of  
designs.

Contractual  
quantity  
estimate

Work  
order  
supply  
by both  
drawings

2  
whether  
the rev.  
plan was  
by the  
contractor  
by the  
Deptn.

*[Signature]* 26/04/2019  
 SUPERINTENDING ENGINEER  
 South Circle, M.E. Directorate  
 Deptt. of Municipal Affairs  
 Govt. of West Bengal

UD/21/2011/1111

Govt. of West Bengal  
DEPARTMENT OF MUNICIPAL AFFAIRS  
MUNICIPAL ENGINEERING DIRECTORATE  
Office of the Executive Engineer  
Bankura Division  
Kenduadihi, dist.- Bankura - 722102

No. MED.BKI 209/NULM-1/15 Pt-II

Date:- 25.04.2019

From: The Executive Engineer  
Bankura Division  
M.E. Dte.  
Bankura

To: The Superintending Engineer  
South Circle, M.E. Dte.

**Sub.** - Present status of work "Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality Under NULM. Lay out Plot No. 817 (RS), Mouza - Bankura, JL No - 211 Bankura."

**Ref.** - Work Order No. 618 VIII-14 Dated-22.05.2017

Sir,


With reference to the above, I am to inform the present status report of the said work as follows.

1. Work order issued to the agency on 22.05.2017 vide Bankura Municipality memo no-618.VIII-14 dt. 22.05.2017.
2. Work started (pilling work) on 02.01.2018 after dismantling of temporary stalls. Such delay in starting the work is due to want of clear site free from encroachment.
3. After completion of pilling work, load test was done on 04.04.2018 but result of the same is not found satisfactory. Then, the design is modified to Raft foundation with reducing vertical height from five storied to three storied and by increasing floor area providing same facilities. Again the concerned agency resumed the work on 10.04.18.
4. Due to change in design and enhancement of floor area, total quantity of steel reinforcement is 20.0 MT (approx) up to ground floor roof level where as as per tender including ground floor and 1<sup>st</sup> floor it was 36.0 MT only. Therefore the excess steel reinforcement is, 36-36=20.0 MT, but overall expenditure after completion of work will remain within tendered amount on the basis of savings of other components like pilling work due to reducing of its diameters (500 mm dia instead of 550 mm dia) and length (1132.0 m instead of 1250.0 m) by adopting augur boring method instead of DMC method.
5. The progress of work is now stagnant after completion of ground floor roof since 05.03.2019.

This is for your kind information and taking necessary action please.

Thanking you,

Yours faithfully,

  
Executive Engineer  
Bankura Division, M.E. Dte.  
Govt. of West Bengal  
25/04/19



o/c

GOVERNMENT OF WEST BENGAL  
OFFICE OF THE EXECUTIVE ENGINEER, BANKURA DIVISION  
MUNICIPAL ENGINEERING DIRECTORATE  
KENDUADIHI, BANKURA  
U.D. & M.A. DEPARTMENT

Ph. No.: 03242-250922

Memo No. - MED/BKU/202/NULM-1/15 Pt. II

Date: 18.04.2019

From: The Executive Engineer,  
Bankura Division,  
M. E. Dte.

To: The Chairman,  
Bankura Municipality  
Bankura.

**Sub:** Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM. Layout Plot no. 817 (RS), Mouza- Bankura, JL no.211, Bankura.

**Ref:** (i) Your Letter no- 0081/VIII-14 dated 12.04.2019.  
(ii) Your Letter no- no 48(4)/VIII-14 dated 06.04.2019.


Sir,

With reference to the above, this is to inform you that the concerned agency did not resume the work till this date. In this context, it is to mention here that any additional work due to change in design & drawing is to be done by the concerned agency on the same conditions in all respects on which he agreed to do the main work as per clause of contract.

It is to be noted that inspite of changing in drawings, the said work will be completed within tendered amount.

Thanking you.


Yours faithfully,

  
Executive Engineer  
Bankura Divn. (Works)  
Bankura Division  
M.E. Directorate  
Govt. of West Bengal  
Date:- 18.04.2019

Memo No. MED\BKU\202/NULM-1/15 Pt. II

Copy forwarded for information & necessary action to :

1. The Superintending Engineer (South Circle) M.E Dte.

  
Executive Engineer  
Bankura Divn. (Works)  
Bankura Division  
M.E. Directorate  
Govt. of West Bengal





Government of West Bengal  
Office of the Superintending Engineer (South Circle)  
Municipal Engineering Directorate  
Koushalya, P.O: Kharagpur, Dist: Paschim Medinipur

No MED / SE(S) / 69 / NULM-1 / 15 Pt. I

Dated 11.06.2019

Chief Engineer

Municipal Engineering Directorate

Bikash Bhavan (South Block), 2<sup>nd</sup> Floor

Salt Lake City

Kolkata-700091


Sub: Report on the claims of agency of NULM building within Bankura Municipality

Ref: ME/211/1/1M-54/2014, Pt-VI, Dated 06.06.2019

Sir

I have already submitted a detail report on the present status of the NULM building within Bankura Municipality as an enclosure to my letter No MED / SE(S) / 30 / NULM-1 / 15 Pt. I, dated 26.04.2019. In the said report, I have categorically stated that the demand on the part of the contractor to supply balance quantity of steel has been beyond the terms of the contract. So nothing more is required to be stated. However, I have asked the Executive Engineer to further communicate with the contractor regarding resuming the work immediately failing which relevant clause as per contract will be invoked against the contractor. With this I am once again enclosing the earlier report for your ready reference, please.

Yours sincerely

  
11/06/2019  
Superintending Engineer, South Circle  
Municipal Engineering Directorate  
Superintending Engineer  
No MED / SE(S) / 69 / NULM-1 / 15 Pt. I  
Govt. of West Bengal  
Copy to: Dept of M.A.

Dated 11.06.2019

Executive Engineer, Bankura Division, M E Directorate. He is requested to act as per telephonic directions given to him in this regard.

Superintending Engineer, South Circle  
Municipal Engineering Directorate

2019-2020

SUPERINTENDING ENGINEER  
South Circle, M.E. Directorate  
Dept. of Municipal Affairs  
Govt. of West Bengal

*[Handwritten signature]*  
26/04/2019

says in the letter.

GO pinches the contractor the most; otherwise there is hardly any merit in what the contractor the total expenditure of any work within tendered amount and late realization of the spirit of the the contractor won the contract offering 13.95% less without knowing that recent GO restricts cannot operate simultaneously without infringing the financial rules. The real issue is that cannot be entertained because in a particular tender, departmental supply and own supply Regarding departmental supply of steel material, such request on the part of the contractor Tender Inviting Authority and the contractor allows for change in drawing and design, if required. it is to be stated that the Tender Form which is an essential part of the agreement between the departmental supply of the balance reinforcement beyond the tendered quantity. In this context contractor has now stopped any further work of the building and has been asking for increase in steel consumption which, according to the contractor, works against him. The NULM. Such increased area of the building with modified foundation has caused a substantial (G+4) to (G+2) with increased floor area to provide the same facilities of the model plan of changed from pile foundation to raft foundation and the height of the building was modified from of time. Thereafter, based on pile load test conducted on a test pile, the foundation design was foundation took place sometime in January, 2018. So the contractor had to suffer for such lapse after 6 months and so even though the Work Order was issued on 22.05.2017, actual work for The site that was allotted for construction of the NULM building was not free from encumbrances and there were temporary stalls on the site. Clearance of the site was made

Ref: ME/79/1/1M-54/2014, Pt-IV, Dated 17.04.2019

**REPORT ON THE PRESENT STATUS OF NULM WITHIN BANKURA MUNICIPALITY**

To  
The Chairman  
Bankura Municipality  
Sub: Constr  
of Banku  
No. \_\_\_\_\_  
Contractor & Ge

2019



UD/21/2019/01158 27.16/04/19  
SB**KARTICK SEN**

Govt. Contractor &amp; General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Ref. No. ....

Date .....

To  
The Chairman  
Bankura Municipality

Sub: Construction of 50 beded five storied building and ancillary work for shelter for urban homeless withhim jurisdiction of Bankura Municipality under NULM, Layout plot No-817(R.S), Mouza- Bankura JI No-211 Bankura.

Ref:- NIT NO WBMDA/CM/BM/24/MULM/2016-17 of office memo no - 3106/VIII-14 Dated -21/01/2017 .

Ref:- 48/VIII-14 Dated-06/04/2019

মাননীয় মহাশয়

আপনার নিকট জানাই যে উপরোক্ত কাজের জন্য ইংরেজী 22.05.2017 তারিখে ওয়ার্ক অর্ডার লইয়া 12.06.2017, 06.07.2017, 07.08.2017, ও 09.11.2017 তারিখ পর্যন্ত বারংবার চিঠি দিয়ে জানাই যে উক্ত জায়গাটি পরিষ্কার করে Layout দেওয়ার ব্যবস্থা করা হোক, কিন্তু অভ্যন্তর দুঃখের সাথে জানাই যে অফিস হইতে আমার চিঠির কোন প্রত্যুত্তর দেওয়া হয় নাই।

দীর্ঘদিন পরে গত ইংরেজী 21.11.2017 তারিখে আপনার চেয়ারে S.E, E.E, A.E, S.A.E, (M.E. Det) ও আমি উপস্থিত হইয়া উক্ত কাজের বিভিন্ন আলোচনার পর সিদ্ধান্ত হয় যে উক্তস্থানে 500 mm dai Ayar pilling হইবে এবং আমাকে অতিরিক্ত G.S.T দেওয়া হইবে, সরকারি আদেশনামা 6943 - F (V) dated 31.11.2017 অনুসারে। প্রসঙ্গক্রমে উল্লেখ থাকে যে অফিসের নানা চালবাহানা সত্ত্বেও মাত্র 24 ঘন্টার মধ্য কাজ শুরু করতে বলা হয়। অন্যথা আমার বিরুদ্ধে আইনালুগ ব্যবস্থা গ্রহণ করা হইবে। আমি আপনার আদেশমতে 23.03.2018 তারিখ হইতে বাঁকুড়ার M.E Det অফিসের তত্ত্বাবধানে আগর পাইলের কাজ শুরু করি এবং উক্ত কাজ সময় মতো শেষ হয়।

23.03.2018 তারিখে 5 নম্বর লোড টেস্টের পর দেখা যায় উক্ত স্থানে পাঁচতলা বিল্ডিং নির্মাণ সম্ভব নয় এবং আমাকে মৌখিক ভাবে কাজ বন্ধ রাখবার নির্দেশ দেওয়া হয়। দীর্ঘ দিন পর গত ইংরেজী 03.05.2018 তারিখে মৌখিক ভাবে জানানো হয় যে উক্ত স্থানে প্রায় দ্বিগুণ জায়গা লইয়া তিন তলা বিল্ডিং নির্মাণ করিতে হইবে এবং S.E (South circle M.E Det) অফিসের অনুমোদিত নকশা দেওয়া হয়। কিন্তু আজ পর্যন্ত কোন রূপ পরিবর্তিত এস্টিমেট দেওয়া হয় নাই। যা হইতে আমার পক্ষে বোঝা সম্ভব নয় যে কাজের জন্য কোন নির্মাণ সামগ্রী কতটা প্রয়োজন। যাহা টেন্ডারের শর্ত লংঘন করে। আমি বাধ্য হইয়া পুনরায় 10.05.2018 তারিখ হইতে কাজ শুরু করি এবং ওয়ার্ক অর্ডার এর নির্দিষ্ট সময়ের মধ্যে এক তলার ছাদ ঢালাই এর কাজ সম্পন্ন করি এবং লক্ষ্য করিলাম টেন্ডারের যে পরিমাণ রডের উল্লেখ আছে তাপ্রায় সব শেষ। এমতাবস্থায় ওয়ার্ক অর্ডারের সময় পার হওয়া সত্ত্বেও বাকি কাজ সম্পন্ন করার জন্য অফিস হইতে অতিরিক্ত রড সরবরাহের আবেদন জানাই। কিন্তু 06.04.2019 তারিখে অফিস হইতে জানানো হয় রড সরবরাহ সম্ভব নয় এবং ওয়ার্ক অর্ডার এর নির্দিষ্ট সময় পার হওয়া সত্ত্বেও সাত দিনের মধ্যে কাজ শুরু করার নির্দেশ দেওয়া হয়, যাহা টেন্ডারের শর্ত লঙ্ঘন করে।

মহাশয়ের নিকট বিনীতভাবে জানাতে চাই যে বাকি কাজ সম্পন্ন করতে যে পরিমাণ টেন্ডারের বাইরে অতিরিক্ত রড প্রয়োজন তা আমি কিভাবে কোথায় পাব। সুতরাং মহাশয় নিকট পুনরায় বিনীত আবেদন যে যদি অফিস হইতে টেন্ডার এর বাইরে অতিরিক্ত রড সরবরাহের ব্যবস্থা না করা হয় তাহলে আমার পক্ষে আর কাজ করা সম্ভব নয়, সুতরাং আজ পর্যন্ত আমি যা কাজ করিয়াছি তাহার যথাযথ পরিমাপ করিয়া, পেমেন্টের সুব্যবস্থা করিয়া আমাকে উক্ত কাজ হইতে অবহিত দেওয়ার আদেশদানে মর্জি হবেন।

ধন্যবাদান্তে

আপনার একান্ত অনুগত

Copy forwarded for information,

1. The Director SUDA, Bidhannagar, Salt Lake, Kolkata 700108
2. The chief Engineer M.E.Det, Bikash Bhaben Kolkata 700067
3. The Superintending Engineer M.E.Dte. (south Circle) Kousliya Kharapupur

**KARTICK SEN**

Proprietor

No. ME/ 79/1/14-54/2014 Pt-12 Dated: 17/04/19

Copy forwarded for information and taking necessary action to:-

1. The Superintending Engineer, South Circle, M. E. Dte.- He is requested to submit a report as early as possible.

17.04.19  
Chief Engineer, M. E. Dte.



o/c  
**KARTICK SEN**

Govt. Contractor & General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Date 12-06-2017

M 2141  
12.06.17

*[Signature]*

To,  
The Executive Engineer,  
MED, Bankura Division  
Bankura

**Sub:-** Prayer for handing over the clear site along with Layout of the Building.

**Ref:-** Work Order No. 618/VII-14 dt.22/05/2017 against NIT no.  
WBMAD/CM/BM/24/NULM/2016-17 VIED OFFICE MEMO NO.  
3106/VIII-14 dt 21/01/2017

Respected Sir,

I the under signed have received the above stated reference work, so, I, would like to request your kind self to hand over me the clear site as well as arrange for layout of the above stated work at the earliest. Please do the needful and oblige.

Thanking You,  
Yours Faithfully.

*[Signature]*

Copy To :-

1) Chairman, Bankura Municipality



**KARTICK SEN**

Govt. Contractor & General Order Supplier

RAJGRAM,  
BANKURA (W.B.)  
Mobile : 9832694123  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

05-07-2017

To,  
The Chairman,  
Bankura Municipality,  
Bankura

Sub :- Construction of 50 bedded five storied Building and ancillary work for shelter for Urban Homeless within Jurisdiction at Bankura Municipality under NULM. Lay out Plot No.- 817 (R.S.) , Mouza - Bankura, J.L. No.- 211 Bankura.

Ref. - Work order No.- 618 / VIII-14 dated 22/05/2017

মাননীয় মহাশয়,  
আপনার অবগতির জন্য জানাই যে উক্ত কাজের জন্য Lay out দেওয়ার জন্য আবেদন করিয়াছিলাম গত ইংরেজী 12-06-2017 তারিখে, কিন্তু আজ পর্যন্ত Lay out দেওয়া হয় নাই।

মহাশয়ের নিকট আবেদন যাহাতে উক্ত কাজের তাড়াতাড়ি Lay out দেওয়া হয়, তাহার প্রয়োজনীয় ব্যবস্থা গ্রহন করিলে উপকৃত হইব।

ধন্যবাদান্তে,  
KARTICK SEN  
Proprietor

অনুলিপি প্রেরিত হইল :-  
(1) The Executive Engineer , M.E.D.  
Kenduadihi, Bankura.

1

# KARTICK SEN

Govt. Contractor & General Order Supplier

5/10/17

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Date . 07.08.2017


The Chairman  
Bankura Municipality  
Bankura

For construction of a beddhal five storied building and ancillary work for shelter for Urban Homeless within jurisdiction of Bankura Municipality under NULM. Lay out plot No 81T (R.S) Mouza-Bankura, J.I. No- 211 Bankura.

Ref :- work order No 618/VIII-14 dated 22/05/2017

ଆବଦାନ ସହାୟତା,

ଆବଦାନ ସହାୟତା ଏବଂ ଶ୍ରମିକମାନଙ୍କ ପାଇଁ ଉପଯୁକ୍ତ ଏବଂ Lay out ନିର୍ମାଣ ଏବଂ ଆବେଦନ ଅଧିକାରୀଙ୍କୁ ଏକ ହାତପତ୍ର ୦-୭-୨୦୧୭ ତାରିଖ, ବିଷୟ ଉପର ଲେଉଟ ନିର୍ମାଣ ଏବଂ ଲାଭ  
ନିର୍ମାଣ ସହାୟତା ଏବଂ ଆବେଦନ - ୨୪୨୩୦୦  
୦୦୦ ନିର୍ମାଣ ସହାୟତା Lay out ନିର୍ମାଣ ଏବଂ  
ନିର୍ମାଣ ସହାୟତା ଏବଂ ଆବେଦନ - ନିର୍ମାଣ - ନିର୍ମାଣ  
୨୨୪,

କାର୍ତ୍ତିକ ସେନ,  
KARTICK SEN  




2017 MAD-99513.1

9363/M. Dt. 09.11.17

# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM  
BANKURA (W.B.)

Mobile : 9232694223

Email : kartick37@yahoo.com

karticksen75@gmail.com

Date 09.11.2017

To  
The Chairman  
Bankura Municipality  
Bankura

Sub:- Acceptance cum work order for construction of 50 bedded five storied building and ancillary work shelter for urban homeless within jurisdiction of Bankura municipality under NULM. Layout p. no.817(R.S), mouza-Bankura, JI no.211 Bankura .

Ref:- NJT NO.WBMAD/CM/BM/24/NULM/2016-17 of office memo no. 3106/VIII-14 Dated-21/01/2017  
Ref:-Your latter of acceptance cum work order no.618/VIII-14 Dated-22/05/2017

Sir,

I would like to inform you that the work order for the above mentioned work. Thought issued 22/05/2017 but could not taken up for want of clear site free from encroachment not made available to me. I must mention that the estimated amount put to tender being Rs.1,84,07,355.00 was made basing on 3% . But the Govt. of India introduced G.S.T. form 1<sup>st</sup> July 2017. So as per pre G.S.T. contract agreement which exclusive of VAT need to be revised of contractual value in the contact due to impact of change in tax rate.

So I would request you to kindly revise the project value with a G.S.T. rate of 6% CGST and 6% SGST exclusive of VAT 3% . As otherwise it would adversely affected to the agency. Kindly decide and communicate your decision earliest to help me to commence the work.

Thanking You

Yours Faithfully

*Kartick Sen*

Copy Forwarded to information

1. The Superintendent Engineer M.E.Dte. Khargapur
2. Executive Engineer, M.E.Dte. Bankura

Received. Two copy SE & EE





## Office of the Municipal Councillors of Bankura

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 , Mobile: 09434115191

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)

[senguptamahaprasadcm@yahoo.in](mailto:senguptamahaprasadcm@yahoo.in)

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org)

From: *Sri Mahaprasad Sengupta*

Chairman, Bankura Municipality

Memo. No. **2689** / VIII-14 (NULM)

Dated, Bankura : 22/11/17.

✓  
To  
L. Mick Sen  
Pajagram  
Bankura.

Ref:- Memo No. – MED/BKU/ 534 /NULM-1/15, Dated – 21/11/2017

Sub:- Construction of 50 Bedded five storied Building under NULM within jurisdiction of Bankura Municipality.

Dear,

With the above reference you are hereby directed to start the work of NULM Project as early as possible because the work order had been issued to you on dated 25/05/2017 and almost six months have passed away. In this connection the photocopy of the letter as received from the Superintending Engineer, South Circle, M. E. Directorate, against your prayer dated 09/11/2017 for the revised project value with a G.S.T. rate has been enclosed herewith.

You are also directed to submit the work programme within 24 hours after receiving this letter otherwise this Municipality will impose penal action towards termination of contract as per finance rule.

*Mick*  
22-11-17  
Chairman  
Bankura Municipality

Enclosure :- photocopy of the letter as received from the Superintending Engineer, South Circle, M. E. Directorate.

Memo no:- (4)/VIII-14(NULM), Dated:- / /17.

Copy forwarded for information and take necessary action from your end.

1. The Director, SUDA, ILGUS BHAVAN, HC Block, Sector – III, Bidhannagar, Kolkata 700106, West Bengal.
2. The Secretary, Department of UD & MA, Government of West Bengal, Town & Country Planning Branch, Government of West Bengal, Nagarayan, DF-8, Sector-I, Bidhan Nagar, Kolkata - 700064
3. The Superintending Engineer (South), Municipal Engineering Directorate (South Circle), Kousaniya, P.O. Khargpur, Dist:- Paschim Midnapur.
4. The Executive Engineer, M.E.Dte., Bankura Division, Kenduadihi, Bankura.

*sb*  
Chairman  
Bankura Municipality



Municipal Engineering Directorate  
Koushallya, P.O: Kharagpur, Dist: Paschim Medinipur

No. MED/SE (S) / 612 / NULM - 1 / 15

Dated: 21.11.2017

From: Superintending Engineer  
South Circle

To: The Executive Engineer  
Bankura Division, M.E. Div  
Bankura

Sub: Construction of 50 bedded five storied Building under NULM within Bankura Municipality

Ref: Work Order No 618/III-14 dated 22.05.2017

Agency memo No Nil dated 09.11.2017

Memo No 2575/III-14(NULM) dated 13.11.2017 of the Chairman of Bankura Municipality

His memo No MED/BKU/527/NULM-1/2015 dated 16.11.2017

It is unfortunate to record that the Agency is deferring his Program time and again on different reasons. As a result, it is difficult to draw a firm conclusion in respect of the fate of the contract.


However, the Finance department of Govt. of West Bengal vide its Notification No 6943-F(Y) dated 13.11.2017 has modified its earlier Notification No 5050-F(Y) dated 16.08.2017.

Now, in terms of Notification No 6943-F(Y) dated 13.11.2017, enhanced percentage up to maximum ceiling of 9.50% on the value of goods as agreed upon in the contract may be allowed to the Contractor in case of composite supply of works contract as defined in Clause (119) of Section 2 of West Bengal Goods and Service Tax Act, 2017 subject to condition that

1. The Agency would submit valid papers/documents in support of its claim and
2. The goods in question fall under GST rate of 18%.
3. If the goods rate falls below 18% rate, then enhanced rate would be proportionately reduced.

Now, he is requested to ask the concerned Agency in writing whether he is agreeable to undertake the work without further delay and to complete the same in time. Otherwise he is requested to recommend the Chairman of Bankura Municipality to terminate the Contract along with penal measure as per condition of the Contract. Xerox copy of the said Notification is enclosed herewith.


Encl: As stated above

  
(Superintending Engineer)  
South Circle, M.E. Div  
Govt. of West Bengal  
Dated: 21.11.2017

No. MED/SE (S) / 612 (2) / NULM - 1 / 15

Copy forwarded for information to:

1. The Chairman, Bankura Municipality, Bankura
2. Karick Sen Raigam, Bankura

  
(Superintending Engineer)  
South Circle, M.E. Div  
Govt. of West Bengal  
Dated: 21.11.2017



# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM

BANKURA (W.B.)

Mobile : 9232694223

Email : kartick37@yahoo.com

karticksen75@gmail.com

M 10597

Date 08-12-2017

8-12-17

To,  
The Chairman,  
Bankura Municipality,  
Bankura.

Sub: Construction of 50 Bedded five storied Building and ancillary work for shelter for Urban Homeless within jurisdiction of Bankura Municipality under NULM. Lay out Plot no. - 817(R.S.), Mouza-Bankura, J.L. No. 211 Bankura.

Ref. : A) Work Order No.- i) 618/VIII-14, dated- 22.05.17 & ii) MED/BKU/95/NULM-1/2015, dt. 25.05.17.

B) NIT No. -WBMAD/CM/BM/24/NULM/2016-2017.

With due respect, I beg to state that as per above reference order I take over the site and going to start the work on execution of 500mm dia. Agar pilling work as per discussion on 21.11.2017 at your Office Chamber with the presence of S.E., E.E., and A.E. of MED of concern Division for Agar pilling instead of DMC pilling, it is observed that the depth are not going as desired after below 5 to 7 metre.

So, please give me the necessary instruction for this situation, keeping in view that huge materials for the said work are stacked in the said site.

Thanking you,

Yours faithfully,

(Kartick Sen)

Copy forwarded for information and necessary action to

- 1) The Superintending Engineer, South Circle, M.E. Dte. Khargapur, Paschim Medinipur
- 2) The Executive Engineer, Bankura Division, M.E.Dte. Kenduadihi, Bankura-722102.



# KARTICK SEN

Govt. Contractor & General Order Supplier

8/0 8824/M. Dt. 07.03.19

RAJGRAM

BANKURA (W.B.)

Mobile : 9282694223

Email : kartick37@yahoo.com

kartick75@gmail.com

Date 07-03-2019

To,  
The Chairman,  
Bankura Municipality,  
Bankura.

Sub: Construction of 50 Bedded five storied Building and ancillary work for shelter for Urban Homeless within jurisdiction of Bankura Municipality under NULM. Lay out Plot no. - 817(R.S.), Mouza-Bankura, J.L. No. 211 Bankura.

Ref. : A) Work Order No.- i) 618/VIII-14, dated- 22.05.17 & ii) MED/BKU/95/NULM-1/2015,  
dt. 25.05.17.

B) NIT No. -WBMAD/CM/BM/24/NULM/2016-2017.

Sir,

With due respect, I beg to state that as per above reference order I would like to inform you that the above stated work has been commenced on 23/11/17 after a long period of about 6(six) months due to vacant the site from your department and letter on due to some technical reasons and revised drawing and design I have to stop the work as per verbal direction from your office though I have completed the roof of the ground floor within the stipulated time period and consumed more or less the schedule quantity of reinforced steel .

In this connection it may be noted that the stipulated time period is over and in the mean time market price of the construction materials are higher than the schedule rate.

So, it is not possible to continue the said work either the material (steel) not supplied from the department.

Thanking you,

Yours faithfully,

  
(Kartick Sen)

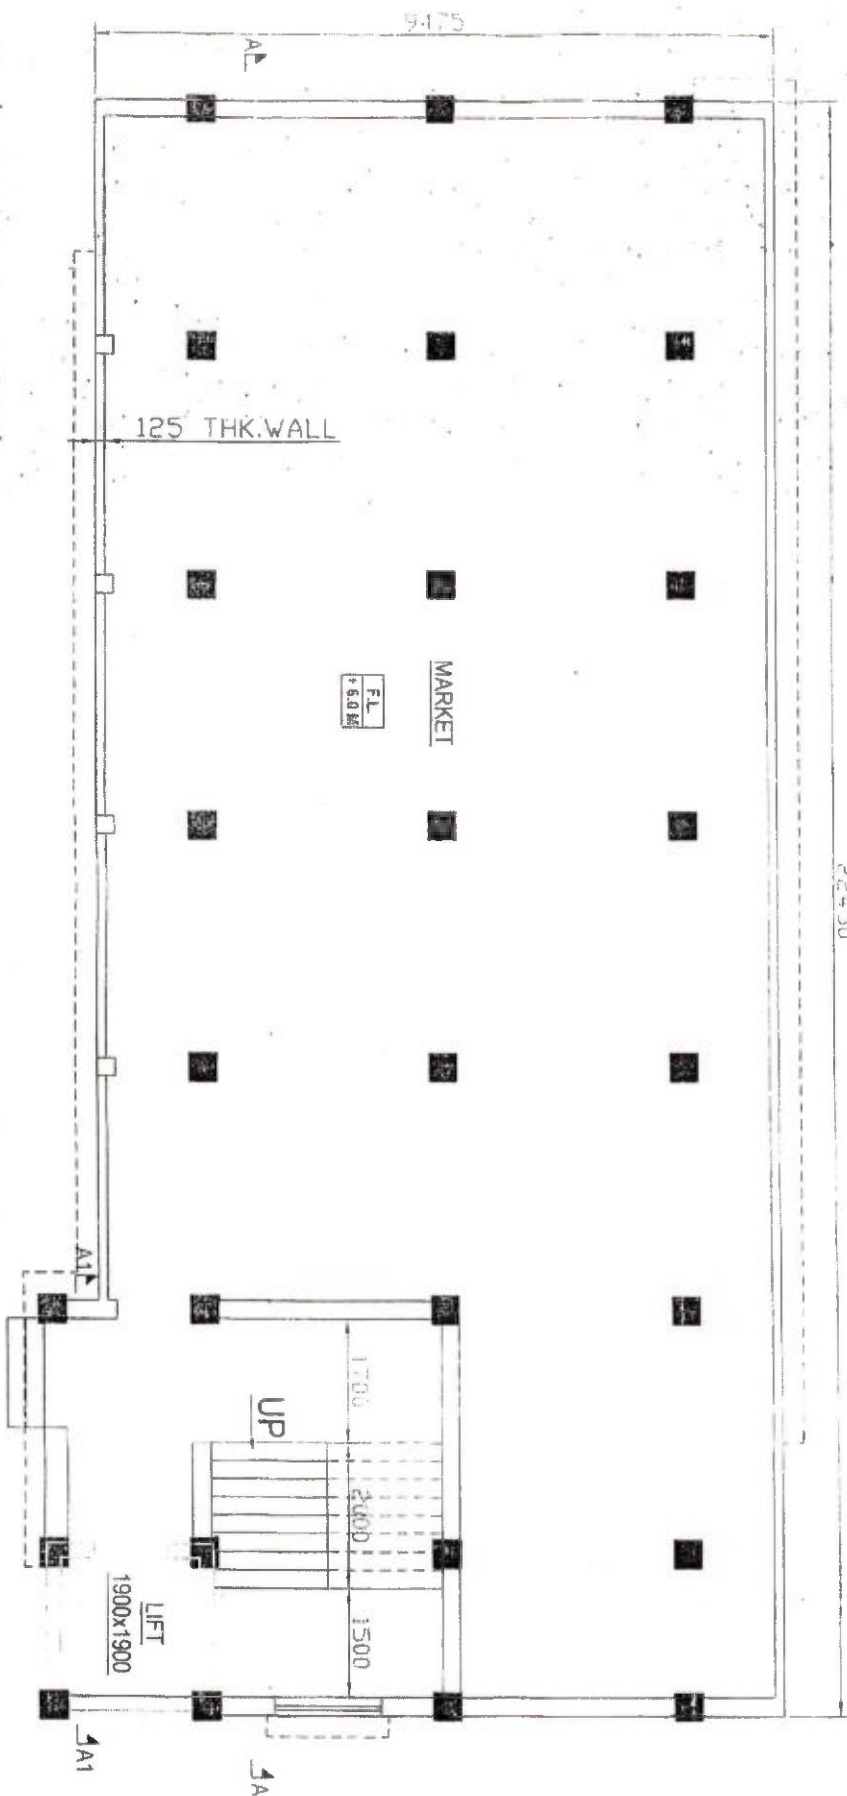
Copy forwarded for information and necessary action to :

1) The Executive Engineer, Bankura Division, M.E.Dte. Kenduadihi, Bankura-722102.



11

22450




### GROUND FLOOR PLAN

*Handwritten notes:*  
 23. 11. 16  
 (Signature)  
 20/11/16

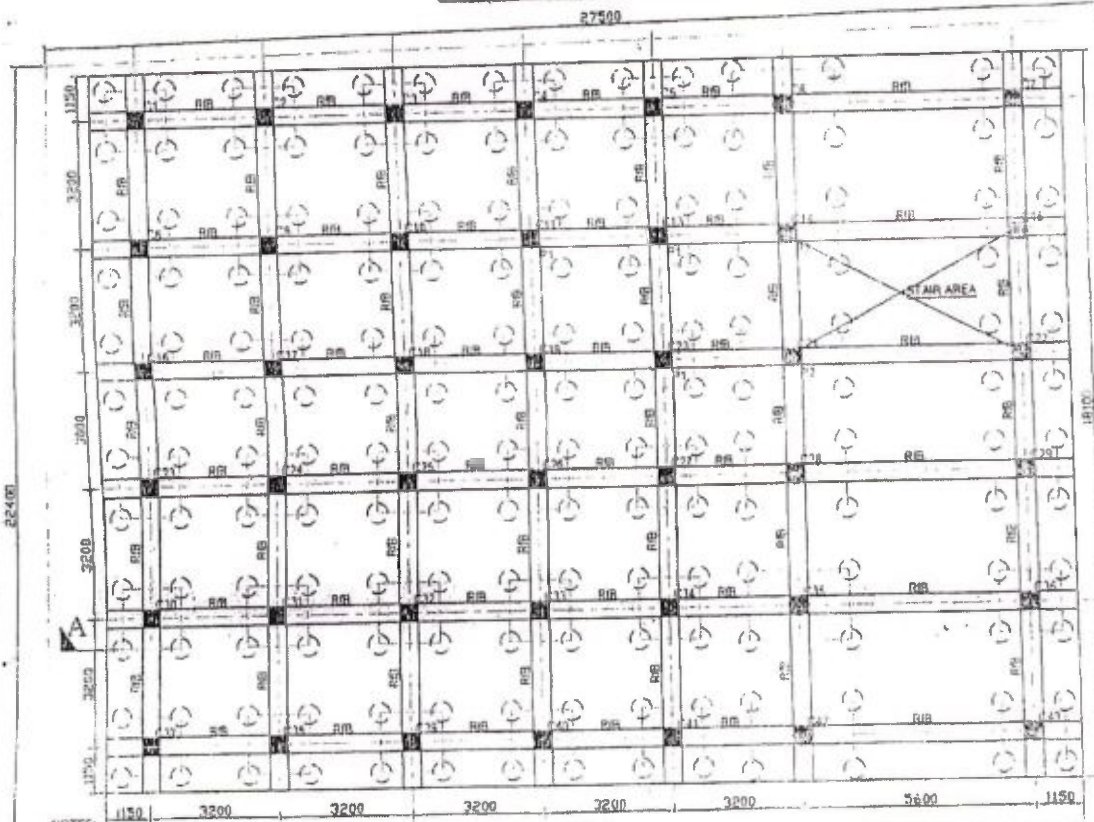
CONSTRUCTION OF 50 BEDED FIVE STOREIED SHELTER FOR  
 URBAN HOMELESS UNDER NULM [PLOT NO. 817 (R.S)]  
 WITHIN BANKURA MUNICIPALTY

DRG. NO. MED/BKUNULM07-2016





SECTION AT A-A  
TYP. SECTION OF RAFT FOUNDATION



NOTES:

1. All dimensions are in mm and work in meter.
2. If concrete is of 15% to 20% grade concerning to IS 1784 - 1979 or later.
3. R.C.C. will be nominal mix of (1:2:4).
4. R.C.C. will be M-25 Grade Controlled Concrete.
5. Lap length of the bars shall be as per IS 456-2000 or latest.
6. Extra bars shall be provided around opening as per standard practice.
7. All concrete will be machine mixed and machine vibrated.
8. Potable water will be used for mixing the concrete.
9. Calculation of work will be as per all relevant IS codes.
10. Details of R.C.C. raft slab shall be given in sheet 2 of 2 (R-2014).

M-25 Grade Controlled Concrete MARK-RIB

100 Ø EXISTING PILE BOUNDARY LINE

MAIN ENTRY  
3400  
WIDE ROAD

7500  
CONSTRUCTION OF 50 BEDDED THREE STORED SHELTER FOR URBAN HOMELESS UNDER NULM (PLOT NO 817 (R.S)) WITHIN BANKURA MUNICIPALITY

SHEET 01 OF 2

*Bhalla*  
5/7/18  
Assistant Engineer  
Bankura Division (Works)  
M.E. Directorate  
Group of Works Branch

may be approved  
*Bhalla*  
16/11/18  
Assistant Engineer  
South Circle, M.E. Div  
Dept. of Municipal Affairs  
Bankura

*Approved*  
SUPERINTENDING ENGINEER  
South Circle, M.E. Directorate  
Dept. of Municipal Affairs  
Govt. of West Bengal



Kalyan J.S. De SMM

# Office of the Municipal Councillors of Bankura

From: *Mahaprasad Sengupta*

CHAIRMAN, BANKURA MUNICIPALITY

Office: 250367,250344,254804

Fax: 03242-259269/250367

Resi: 03242-253338 Mobile: 94341151

E-mail: senguptamahaprasadcm@yahoo.

:bankuramunicipality@rediffmail.com

Website:www.bankuramunicipality.org

Memo No: 1234/BM/19-20



Date: 02.08.2019

*AD (JCT)*  
*MDY*

To  
The Director  
State Urban Development Agency (SUDA)  
"ILGUS BHAVAN"  
HC Block, Sector III  
Bidhannagar  
Kolkata-700106

Sub: Utilization certificate against fund received in the F.Y. 2016-17 for Shelters for Urban Homeless (SUH) under NULM, Bankura Municipality.

Sir,

Enclosing herewith the utilization certificate in the prescribed form no. SR 330A in respect of Government Grant for Shelters for Urban Homeless (SUH) under NULM duly received by this Municipality during the year 2016-17 G.O. No. & date of which are given below for favour of your kind information and taking necessary action please.

Sl No.	G.O. No.	Date	Amount(₹)	Remarks
1	SUDA-23/2014(pt.)/048	19.07.2016	45,30,000.00	Shelters for Urban Homeless (SUH), NULM

Yours faithfully

*Muy 02.08.19*  
Chairman  
Bankura Municipality  
Chairman  
Bankura Municipality

*Basundharas*  
02.08.2019

*Basundharas*  
02.08.2019  
Manager  
SD&I, NULM  
Bankura Municipality



# FORM-330A

of the Treasury Rules, West Bengal and the Subsidiary Rules  
made thereunder, Volume-I

## FORM OF UTILISATION CERTIFICATE

Certified that out of ₹ 45,30,000.00 (Rupees Forty Five Lakh Thirty Thousand only) sanctioned during the year 2016-17 towards of Grants-in-aid in favour of Bankura Municipality under the Department of Municipal Affairs, Govt. of West Bengal order no. given in the margin and a sum of ₹ 45,30,000.00 (Rupees Forty Five Lakh Thirty Thousand only) has been utilized for which it was sanctioned and the balance of ₹ Nil only remains unutilized in 2019-2020.

	G.O. No. and Date	Amount (Rs.)	Scheme Name
1.	SUDA-23/2014(pt.)/048, Dated 19.07.2016	45,30,000.00	Shelters for Urban Homeless (SUH), NULM
<b>Total</b>		45,30,000.00	

2. Certified that I have satisfied myself that the condition of which the fund was sanctioned have been duly fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose it was sanctioned.

### Kinds of Checks Exercised:-

1. Voucher
2. Cash Book
3. Ledger
4. Statement of Expenditure
5. Statement of Fund Received

*M. Y. 02.08.19*  
Chairman  
Bankura Municipality  
Chairman  
Bankura Municipality

*B. S. Basundharadas*  
02.08.2019

*B. S. Basundharadas*  
02.08.2019  
Manager  
SD&I, NULM  
Bankura Municipality





# Office of the Municipal Councillors of Bankura

S. De SMM

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 , Mobile: 09434115191

From: Sri Mahaprasad Sengupta 22/09/19

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)

: [senguptamahaprasadcm@yahoo.in](mailto:senguptamahaprasadcm@yahoo.in)

Chairman, Bankura Municipality

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org).

Memo. No. /VIII-14

Dated, Bankura : / /19.

To  
The Executive Engineer,  
M.E.Dte., Bankura Division,  
Kenduadihi,  
Bankura.



AD (JC)

Ref:- Application submitted by Sri Kartick Sen vide this office memo no.- 5003/m, dated-12/09/2019 and your letter no.- MED/BKU/435/NULM-1/15 Pt.-II, dated 05/09/2019.

Sub:- Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM. Layout Plot No. 817(RS), Mouza- Bankura, JL No. 211, Bankura.

Sir,

You please find herewith the copy of the letter submitted by Kartick Sen, the Agency of the above subjected works which speaks itself. This is forwarded for your information and take necessary action form your end.

Your early action may solicit to resume the work.

Thanking you.

Annexure :- As Stated.

SIT  
Chairman  
Bankura Municipality

Memo no:- 2081 (3)/VIII-14, Dated:- 16 / 09 / 19.

Copy forwarded for information,

1. The Director SUDA, Bidhan Nagar, Salt Lake, Kolkata 700106.
2. The Chief Engineer, M.E.Dte., Bikash Bhaban, Kolkata 700067.
3. The Superintending Engineer, M.E.Dte.(South Circle), Kousallya, Khargapur.

MAY 16 09 19  
Chairman  
Bankura Municipality

16/09/19

Chairman  
Bankura Municipality

M 5007 5003  
0120919

# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Ref. No. ....

Date 12-09-2019

TO  
The Chairmen  
Bankura Municipality

Sub:- Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM, Layout Plot No. 817 (RS), Mouza – Bankura , JL No 211, Bankura

Ref:- Your office memo No- 1702/VIII-14 Dated- 05-09-2019

মাননীয় মহাশয়,

আপনার নিকট জানায় যে, উপরোক্ত কাজের বিষয়ে বিভিন্ন সময়ে আবেদন করিয়াছিলাম। কিন্তু লক্ষ্য করিলাম যে, সেই সমস্ত বিষয়গুলি যথাযথ ন্যায় বিচার না করিয়া আমাকে ৭ দিনের মধ্যে পুনরায় কাজ শুরু করিবার আদেশ দেওয়া হয় নতুবা আমার বিপক্ষে দৃষ্টান্ত মূলক শাস্তি গ্রহন করা হইবে।

মহাশয়ের নিকট জানাই যে, আপনার আদেশে ভীত-সঙ্কস্ত হইয়া আমি ইংরেজী ১২-০৯-২০১৯ তারিখে হইতে কাজটি পুনরায় শুরু করিতে বাধ্য হইলাম। প্রসঙ্গক্রমে উল্লেখ থাকে যে আইনঞ্জের পরামর্শ মতো আদালতের আশ্রয় লইতে পারি।

ধন্যবাদান্তে  
বিনীত

KARTICK SEN  
Proprietor

S.A.E (PWD) to report.  
MY 120919





# Office of the Municipal Councillors of Bankura

From: *Mahaprasad Sengupta*

CHAIRMAN, BANKURA MUNICIPALITY

Office: 250367, 250344, 254804

Fax: 03242-259269/250367

Resi: 03242-253338 Mobile: 9434115191

E-mail: senguptamahaprasadcm@yahoo.in  
:bankuramunicipality@rediffmail.com

Website: www.bankuramunicipality.org

Memo No: 1129/BM/2019-20

Date: 26.07.2019

To  
The Director, SUDA  
&  
Mission Director, WBSULM  
ILGUS BHAVAN, H-C Block,  
Sector III, Bidhannagar, Kolkata-700106



*AMD (SC)*

Sub: Permission for payment of ₹ 1, 95,460.00 only from interest amount of NULM Fund.

Sir,  
This is to inform that the following expenditure were incurred for the construction of 5(five) storied building for SUH under NULM, Bankura Municipality but these are not included in Project DPR.

- |  |                |
|--|----------------|
| 1) Mobilization and demobilization, Boring, Sample Tests etc. on dt.03.10.2016   | ₹ 61,000.00    |
| 2) Expenditure for advertisement published on 28.01.2017 at Sambad Pratidin & other news papers regarding tendering of construction on dt.23.03.2017 | ₹ 45,980.00    |
| 3) Soil testing expenditure to find load bearing capacity on dt.04.12.2018   | ₹ 88,480.00    |
|  | ₹ 1, 95,460.00 |

In these circumstances you are requested to permit the undersigned to expend the same from the interest amount of NULM Fund.

Your early instruction in this matter is highly solicited.

Thanking you

Yours faithfully

*Mley*  
26.07.19

Chairman  
Bankura Municipality  
Chairman  
Bankura Municipality

*Basundharas*  
Manager 26.7.19  
SD&I, NULM  
Bankura Municipality

*Basundharas*  
26.07.2019



**GOVERNMENT OF WEST BENGAL**  
**OFFICE OF THE CHIEF ENGINEER**  
**Municipal Engineering Directorate**

Bikash Bhawan, South Block (1<sup>st</sup> Floor) Salt Lake, Kolkata – 700091.

Phone No: (033)2337-1331/ (033)2358-3347 Fax: (033) 2337-5474

E-mail: ce\_medte@yahoo.com

S.D. Saha  
01.08.19

No. ME/ 404/1M-54/14 Pt-VI

Dated

01.08.2019

From: The Chief Engineer,  
Municipal Engineering Directorate.



AMD (CE)

To: The Director, SUDA,  
ILGUS Bhawan,  
Salt Lake, Kolkata

Sub: - Report regarding Cause of delay for SUH under NULM project within Bankura Municipality.

Ref: - Memo no. MED/BKU/329/NULM-I/15 Pt-II dated 15.07.2019.

Madam,

I am to submit herewith a self explanatory letter of Executive Engineer, Bankura Division regarding cause of delay for SUH under NULM project within Bankura Municipality for your kind perusal and record please for further reference.

Yours faithfully,

Encl: - As stated above.

01.08.19  
Chief Engineer, M. E. Dte.

GOVERNMENT OF WEST BENGAL  
OFFICE OF THE EXECUTIVE ENGINEER, BANKURA DIVISION  
MUNICIPAL ENGINEERING DIRECTORATE  
KENDUADIHI, BANKURA  
U.D. & M.A. DEPARTMENT

Ph. No.: 03242-250922

NULM

Memo No. - MED/ BKU/ 229/NULM-1/15 pt-II

Date: 15/07/19

CE  
PI Sec  
29/7

EE-1  
Scanned by  
Pl forwarded to  
the Director, BKU.

To: The Chief Engineer,  
Municipal Engineering Directorate  
Bikash Bhavan, Saltlake, kol-91

**Sub:** Cause of delaying for SUH under NULM project within Bankura Municipality.

**Ref:** Your office Memo no :- ME/313/1(5)/1M-54/2014 dt- vi of 11.07.2019.

M.E./1M-54/14, P.E-Y/

Sir,

With reference to the above , I am furnishing the replies of the following questionnaires .

1. Time required for technical sanction –
 

(a)Date of submission of S.E level ?	-	26.12.2016 .
(b)Date of Approval of SE. Level ?	-	04.01.2017 .
2. Time schedule mentioned in NIT for Completion ? - 550 days .
3. As per work order , date of completion ? - 22.11.2018 .
4. How long period the execution is being proportionately delayed as on date ? since work order.
5. What is the reason for delaying ? (a)for 1<sup>st</sup> three month after issuing W.O. , work could not be started due to some encroachment at site.  
(b) for balance period , delayed was done by the agency.
6. Is there MED involved for delaying or not.  
IF yes , what one the causes of delaying? - NO
7. For delaying on the part of agency , what action you have taken , step by step , still to as on date as per clauses of contract?
  - i) After the site free from encroachment , the agency was asked to start the work (vide memo no- MED/BKU/440/NULM-I/2015 dt – 22.09.2017.
  - ii) Inspite of the above correspondence , the agency did not take any initiation to start the work , then recommendation letter for imposing pannel action of


Digitized by  
Municipal Engineering Directorate  
Bankura Division  
Municipal Engineering Directorate  
Govt of West Bengal

C.E. MEDS  
My kindly  
26/7

- contract against the agency is issued to the chairman, Bankura Municipality ( vide memo no - - MED/BKU/517/NULM-I/2015 dt- 10.11.2017 )
- iii) The agency raised the claim of enhancement of rate due to G.S.T. and finally on the issuance of chairman's letter, the agency started the work at the end of November 2018 (Agency's letter no nil, dated of -08.12.2017).
- iv) Some drawings / design were changed due to site condition but progress of work was not hampered due to such changes.
- v) Work has been stopped after completion of ground floor roof casting on from 12.03.2019.
- vi) The agency was again asked to resume the work otherwise penal action as per contract would be recommended against him. (vide this office memo no- MED/BKU/220/NULM-I/15 dt - 13.05.2019)
- vii) In spite of several correspondances, the agency did not take any initiation to resume the work . Finally recommendation for imposing penal action of contact against the concerned agency is <sup>issued</sup> used to the Municipality on 04.07.2019 (vide this office memo no- MED/BKU/314/NULM-I/15 , dt- ii , of 04/07/2019).
- 8 Have you conducted any review meeting since last 3 - 4 month/ monthly? - Yes , last review meeting was on 26.06.2019 in the chamber of the chairman , B.M . Municipality .
- 9 Please ensure the revised date of completion as EIC? February 2020.

Thanking you.

Yours faithfully,

  
Executive Engineer  
Bankura Division  
Bankura Divn. (Works),  
M.E. Dte  
M.E. Directorate  
Govt. of West Bengal

Copy forwarded for information & necessary action to the:-

Date : -

1. The Superintending Engineer, South Circle, M.E.Dte. , Kharagpur

Executive Engineer  
Bankura Division  
M.E. Dte





# রাজ্য নগর উন্নয়ন সংস্থা

## STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-23/2014(MPR-1)/5119

02.08.2019

ক্রমিক নং .....

তারিখ .....

**From: Joint Secretary, UD & MA Dept.  
& Addl. Mission Director, WBSULM**

**To : Chairman,  
Bankura Municipality**

**Sub: Regarding construction of 50 bedded shelter unit at Bankura Municipality under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM**

**Ref memo no. 940/VIII-14 dated: 15.07.2019**

**Ref memo no. MED/BKU/321/NULM-1/15 Pt-II dated: 10.07.2019 of EE, MED, Bankura Division**

Sir,

In reference to the aforesaid letters you are requested to take appropriate action as recommended by Executive Engineer, Bankura Division, MEDte against the concerned agency as the agency did not take any initiation to resume the work.

This is for your information and necessary action.

Yours faithfully,

*Choudhury*  
02/08/19

**Joint Secretary, UD & MA Dept.  
& Addl. Mission Director, WBSULM**

Memo. No. SUDA- 23/2014(MPR-1)/5119

Date: 02.08.2019

Copy forwarded to for information to

1. Secretary, MED
2. Chief Engineer, MED
3. Superintending Engineer, West Circle, MED
4. Executive Engineer, Bankura Division, MEDte.

*Choudhury*  
02/08/19

**Joint Secretary, UD & MA Dept.  
& Addl. Mission Director, WBSULM**

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408

## রাজ্য নগর উন্নয়ন সংস্থা

## STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ

“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA-23/2014(MPR-1)/5119

০৮.০৮.২০১৯

ক্রমিক নং .....

তারিখ .....

**From: Joint Secretary, UD & MA Dept.  
& Addl. Mission Director, WBSULM**

**To : Chairman,  
Bankura Municipality**

**Sub: Regarding construction of 50 bedded shelter unit at Bankura Municipality  
under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM**

**Ref memo no. 940/VIII-14 dated: 15.07.2019**

**Ref memo no. MED/BKU/321/NULM-1/15 Pt-II dated: 10.07.2019 of EE, MED,  
Bankura Division**

Sir,

In reference to the aforesaid letters you are requested to take appropriate action as recommended by Executive Engineer, Bankura Division, MEDte against the concerned agency as the agency did not take any initiation to resume the work.

This is for your information and necessary action.

Yours faithfully,

*[Signature]*  
০৮/০৮/১৯.

**Joint Secretary, UD & MA Dept.  
& Addl. Mission Director, WBSULM**

**Memo. No. SUDA-**

**Date: .08.2019**

**Copy forwarded to for information to**

1. Secretary, MED
2. Chief Engineer, MED
3. Superintending Engineer, West Circle, MED
4. Executive Engineer, Bankura Division, MEDte.

**Joint Secretary, UD & MA Dept.  
& Addl. Mission Director, WBSULM**

দূরভাষ : ২৩৫৮ ৬৪০৩ / ৫৭৬৭, ফ্যাক্স : ২৩৫৮ ৫৮০০

Tel : 2358 6403/5767, Fax : 2358 5800, E-mail : wbsudadir@gmail.com

Account Section : 2358 6408

draft

SUDA-23/2014(MPR-1)

.07.2019

**From: Joint Secretary, UD & MA Dept.  
& Adl. Mission Director, WBSULM**

**To: Chairman,  
Bankura Municipality**

**Sub: Regarding construction of 50 bedded shelter unit at Bankura Municipality under the scheme Shelter for Urban Homeless (SUH) under DAY-NULM**

**Ref memo no. 940/VIII-14 dated: 15.07.2019**

**Ref memo no. MED/BKU/321/NULM-1/15 Pt-II dated: 10.07.2019 of EE, MED, Bankura Division**

Sir,

In reference to the aforesaid letters you are requested to take appropriate action as recommended by Executive Engineer, Bankura Division, MEDte against the concerned agency as the agency did not take any initiation to resume the work.

This is for your information and necessary action

Yours faithfully,



**Joint Secretary, UD & MA Dept.  
& Adl. Mission Director, WBSULM**

**Date: .07.2019**

**Memo. No. SUDA-**

**Copy forwarded to for information to**

- 1. Secretary, MED**
- 2. Chief Engineer, MED**
- 3. Superintending Engineer, West Circle, MED**
- 4. Executive Engineer, Bankura Division, MEDte.**



**Joint Secretary, UD & MA Dept.  
& Adl. Mission Director, WBSULM**



## রাজ্য নগর উন্নয়ন সংস্থা

## STATE URBAN DEVELOPMENT AGENCY

“ইলগাস ভবন”, এইচ-সি ব্লক, সেক্টর-৩, বিধাননগর, কলকাতা-৭০০ ১০৬, পশ্চিমবঙ্গ  
“ILGUS BHAVAN”, H-C Block, Sector - III, Bidhannagar, Kolkata - 700 106, West Bengal

SUDA- 258/2018/

01.07.2019

ক্রমিক নং

From: Director, SUDA  
& Mission Director, WBSULM

তারিখ

To: Surender Kumar  
Under Secretary to the Govt. of India  
Ministry of Housing & Urban Affairs  
Room No. 215-B, Nirman Bhawan, New Delhi-110011

Sub: Reply of Lok Sabha question no. U2079 regarding “Street Vendor”  
Ref: H-11016/107/2018-UPA-II-UD(EFS-9056774)

Sir,

With above reference enclosed the reply of Lok Sabha Question No. U2079 regarding “Street Vendors” in West Bengal. This is for your kind information and further process.

Encl: As stated

Yours faithfully,

Director, SUDA  
& Mission Director, WBSULM  
West Bengal

Memo No. SUDA-258/2018

01.07.2019

Copy forwarded for information to

1. Jt. Secretary (J. Chaudhuri), UD & MA Department
2. Sr. P.A. to Principal Secretary, UD & MA Department

Director, SUDA  
& Mission Director, WBSULM



## Office of the Municipal Councillors of Bankura

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 , Mobile: 09434115191

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)

:[senguptamahaprasadcm@yahoo.in](mailto:senguptamahaprasadcm@yahoo.in)

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org).

From: *Sri Mahaprasad Sengupta*

Chairman, Bankura Municipality

Memo. No. 940 / VIII-14

Dated, Bankura : 15/07/2019.

To  
The Director, SUDA,  
ILGUS BHAVAN, H-C Block, Sector-III,  
Bidhan Nagar, Salt Lake,  
Kolkata 700106.  
West Bengal.



JD  
Soumen

Ref :-The review meeting dated – 05/07/2019 at SUDA Conference Hall & Memo no – MED/BKU/321/NULM-1/15 Pt-II, Dt.- 10/07/2019.

Sub:- Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM. Layout Plot No. 817(RS), Mouza- Bankura, JL No. 211, Bankura.

Sir,

With the above reference and as per review meeting on physical and financial progress of sanction shelter unit for urban Homeless (SUH) the progress of project work as follows.

1. Date 22/05/2017- Work Order Issued
2. Date 22/09/2017- The Site is clear and free from encroachment.
3. Date 13/11/2017- Agency claiming enhance rate due to GST. Then it was forwarded to Executive Engineer, M.E. Dte. for opinion on dated 13/11/2017. In this regard date 21.11.2017 the reply of S.E., M.E. Dte. (South Circle) has been received to this office.
4. Date 08/12/2017- Work Started after several verbal discussion & through different office meeting regarding piling work and as per site condition the drawing and design has been changed but no such revised drawing has been received to this office.
5. Date 06/04/2019- Agency has been directed to resume the work without any delay vide this office memo no 48/ VIII-14, Dated-06/04/2019
6. Date 08/04/2019- Agency applied for office supply of excess quantity of steel materials. But this office does not aware about the requirement of excess quantity of steel materials. The applied letter forwarded to Executive Engineer, M.E. Dte. for opinion.
7. Date 18/04/2019- Executive Engineer, M.E. Dte. opined that agency bound to do any additional work due to change of design & drawing within the limit of tendered amount, but this office does not aware till date about the actual changes of design & drawing as well as no such action taken reply has been received to this office.
8. Date 03/06/2019- Agency further applied for releasing from the tender contract up to work done due to departmental held up and the said application further forwarded to Executive Engineer, M.E. Dte. for opinion.
9. Date 04/07/2019 Executive Engineer, M.E. Dte. opined at last to impose penal action to the agency as per clause 2 & clause 3 of tender contract. But no revised and drawing and design has been submitted to this office till date also no such communication has been made with the agency for compromise.

Continue to .....page 2



## Office of the Municipal Councillors of Bankura

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 , Mobile: 09434115191

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)

:[senguptamahaprasadcm@yahoo.in](mailto:senguptamahaprasadcm@yahoo.in)

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org).

From: *Sri Mahaprasad Sengupta*

Chairman, Bankura Municipality

(2)

So, you are requested to kindly opine me what will be next step to be taken from this end for immediate starting of the said project work.

Your early action may solicit.

Thanking you.

*May 13.07.19*  
Chairman  
Bankura Municipality

*Blood*  
*13/07/19*  
Chairman  
Bankura Municipality

Memo no:- (1)/VIII-14, Dated:- / /19.

Copy forwarded for information,

1. The Principal Secretary, Department of UD & MA, Got. of W. B., Nagarayan, DF-8, Sector-I, Bidhan Nagar, Salt Lake, Kolkata – 700064.

*Salt*  
Chairman  
Bankura Municipality





## Office of the Municipal Councillors of Bankura

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 , Mobile: 09434115191

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)

:[senguptamahaprasadcm@yahoo.in](mailto:senguptamahaprasadcm@yahoo.in)

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org)

From: *Sri Mahaprasad Sengupta*

Chairman, Bankura Municipality

Memo. No. /VIII-14

Dated, Bankura : / /2019.

To  
The Director, SUDA,  
ILGUS BHAVAN, H-C Block, Sector-III,  
Bidhan Nagar, Salt Lake,  
Kolkata 700106.  
West Bengal.

Ref :-The review meeting dated – 05/07/2019 at SUDA Conference Hall & Memo no – MED/BKU/321/NULM-1/15 Pt-II, Dt.- 10/07/2019.

Sub:- Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM. Layout Plot No. 817(RS), Mouza- Bankura, JL No. 211, Bankura.

Sir,

With the above reference and as per review meeting on physical and financial progress of sanction shelter unit for urban Homeless (SUH) the progress of project work as follows.

1. Date 22/05/2017- Work Order Issued
2. Date 22/09/2017- The Site is clear and free from encroachment.
3. Date 13/11/2017- Agency claiming enhance rate due to GST. Then it was forwarded to Executive Engineer, M.E. Dte. for opinion on dated 13/11/2017. In this regard date 21.11.2017 the reply of S.E., M.E. Dte. (South Circle) has been received to this office.
4. Date 08/12/2017- Work Started after several verbal discussion & through different office meeting regarding piling work and as per site condition the drawing and design has been changed but no such revised drawing has been received to this office.
5. Date 06/04/2019- Agency has been directed to resume the work without any delay vide this office memo no 48/ VIII-14, Dated-06/04/2019
6. Date 08/04/2019- Agency applied for office supply of excess quantity of steel materials. But this office does not aware about the requirement of excess quantity of steel materials. The applied letter forwarded to Executive Engineer, M.E. Dte. for opinion.
7. Date 18/04/2019- Executive Engineer, M.E. Dte. opined that agency bound to do any additional work due to change of design & drawing within the limit of tendered amount, but this office does not aware till date about the actual changes of design & drawing as well as no such action taken reply has been received to this office.
8. Date 03/06/2019- Agency further applied for releasing from the tender contract up to work done due to departmental held up and the said application further forwarded to Executive Engineer, M.E. Dte. for opinion.
9. Date 04/07/2019 Executive Engineer, M.E. Dte. opined at last to impose penal action to the agency as per clause 2 & clause 3 of tender contract. But no revised and drawing and design has been submitted to this office till date also no such communication has been made with the agency for compromise.

Continue to .....page 2



## Office of the Municipal Councillors of Bankura

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 , Mobile: 09434115191

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)

:[senguptamahaprasadcm@yahoo.in](mailto:senguptamahaprasadcm@yahoo.in)

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org).

From: *Sri Mahaprasad Sengupta*

Chairman, Bankura Municipality

(2)

So, you are requested to kindly opine me what will be next step to be taken from this end for immediate starting of the said project work.

Your early action may solicit.

Thanking you.

*Sd/-*

Chairman  
Bankura Municipality

Memo no:- *940/1* (1)/VIII-14, Dated:- *15/07/19*.

Copy forwarded for information,

1. The Principal Secretary, Department of UD & MA, Got. of W. B., Nagarayan, DF-8, Sector-I, Bidhan Nagar, Salt Lake, Kolkata – 700064.

*Mun/13.07.19*  
Chairman  
Bankura Municipality

*Khand*  
*13/07/19*

Chairman  
Bankura Municipality



Mas/

GOVERNMENT OF WEST BENGAL  
OFFICE OF THE EXECUTIVE ENGINEER, BANKURA DIVISION  
MUNICIPAL ENGINEERING DIRECTORATE  
KENDUADIHI, BANKURA  
U.D. & M.A. DEPARTMENT

Ph. No.: 03242-250922

Memo No. - MED/BKU/321/NULM-1/15 Pt-II Date: 10.07.2019

From: The Executive Engineer,  
Bankura Division,  
M. E. Dte.

To: The Director,  
SUDA,  
Bidhan nagar,  
Kolkata- 700106.

S. De ... S.M.M.  
Area put in concerned  
file.  
15.07.19

**Sub:** Present status of Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality UNDER NULM. Lay out Plot No. 817 (RS), Mouza- Bankura, JL No-211 Bankura.

Sir,

As per review meeting on physical & financial progress of sanctioned shelter unit for urban homeless (SUH) under DAY-NULM on 05.07.2019 at the conference hall of SUDA, I am to submit present status report of the above mentioned work as follows.

Sl.No.	Date --	Activities --
1.	22.05.2017 :-	Work Order issued with time period of 550 days. (Vide memo no-610/VIII-14 Dt. 22.05.2017)
2.	22.09.2017:-	Site is free from encroachment on august 2017 and this Office asked to the agency to start the work (Vide memo no - MED/BKU/440/NULM-1/2015 Dt. 22.09.2017.) therefore, <u>three months</u> were consumed without any work due to site encroachment.
3.	10.11.2017:-	Inspite of several correspondences, the agency did not take any initiation to start the work, therefore this office requested the Chairman, Bankura Municipality to issue a show cause notice for imposing penal action of contract against the agency. (Vide memo no - MED/BKU/517/NULM-1/2015 Dt. 10.11.2017.
4.	13.11.2017:-	The Chairman, Bankura Municipality forward the prayer of the agency claiming enhancement of rate due to GST. (Vide memo no - 2575/ VIII-14(NULM) Dt. 13.11.2017)
5.	21.11.2017:-	In reply of Chairman's letter, The S.E. (S.C) stated that Contractor's claim would be entertained as per financial rule (Notification no - 6943-F(Y) Dt. 13.11.2017) but he has to start the work and to complete in time- otherwise penal measure as per condition of contract is to be imposed by the Chairman, Bankura Municipality.

[ S.E's memo no- MED/SE(S)/642/NULM-1/15 Dt. 21.11.2017]



6. 22.11.2017:- The Chairman, Bankura Municipality, has asked to the concerned agency to start the work. (Vide memo no- 2689/VIII-14(NULM) Dt. 22.11.2017.
7. 08.12.2017:- Work started as per the concerned agency's memo no- - nil Dt.08.12.2017
8. 02.01.2018:- This office informed the S.E. (S.C) that pilling work by hydraulic pilling which was considered in the tender estimate is not possible due to adjacent dilapidated buildings and pilling by auger bore method is to be taken up and as per revised soil report , it is decided to expand the building horizontally. The S.E. (S.C) approved the revised drawing. (Vide memo no – MED/SE(S)/755/NULM-1/15 Dt. 03.01.2018.)
9. 05.01.2018 One copy of vetted modified drawing was forwarded to the Director of SUDA for information. (Vide memo no- MED/BKU/648/NULM-1/2015 Dt. 05.01.2018.
10. 15.11.2018:- This office again asked the concerned agency for his slow progress mentioning not to complete the work proportionate to the time.(Vide memo no – MED/BKU/496/NULM-1/15 Pt - II Dt. 13.05.2019 Dt. 15.11.2018
11. 12.03.2019 Work has been stopped after completion of ground floor roof casting. Required time extension is also issued to the agency.
12. 13.05.2019:- The agency is again asked to resume the work by this office. (Vide memo no- MED/BKU/220/NULM-1/15 Pt - II Dt. 13.05.2019)
13. 04.07.2019:- As the concerned agency did not take any initiation to resume the work, recommendation for imposing penal action of contract against the concerned agency, is issued to the Municipality. (Vide memo no-MED/BKU/314/NULM-1/15 Pt- II Dt. 04.07.2019.
14. 10.07.2019 The work is stopped till this date.

This is for your kind information please.

Thanking You,

Yours Faithfully,

Executive Engineer  
Bankura Division

M.E. Dte  
24-10-19

No - MED/BKU/321(U)/NULM-1/15 Pt-II

Copy forwarded for information and taking necessary action please:-

- ✓ 1) The Chief Engineer , M.E.Dte.
- 2) The Superintending Engineer ( S.C)
- 3) The Chairman, Bankura Municipality.

  
Executive Engineer  
Bankura Division  
10/07/19

No. ME/ 335/ 14-57/14 Pt-VI Dated:  
Copy forwarded for information and taking necessary action to:-

1. Sri Jolly Chowdhury, Joint Secretary, Department of UD & MA, Govt. of West Bengal, Nagarayan.

15.07.2019

  
Chief Engineer, M. E. Dte.

**GOVERNMENT OF WEST BENGAL**  
**OFFICE OF THE CHIEF ENGINEER**  
**Municipal Engineering Directorate**

Bikash Bhawan, South Block (1<sup>st</sup> Floor) Salt Lake, Kolkata – 700091

Phone No: (033)2337-1331/ (033)2358-3347 \ Fax: (033) 2337-5474

E-mail: ce\_medte@yahoo.com

2603  
05/07/19

No. ME/

Dated:

From : The Chief Engineer  
M. E. Dte.  
Bikash Bhavan, Salt Lake,  
Kolkata

S. Debnath  
9  
08/07/19

To : The Superintending Engineer,  
South Circle, M. E. Dte.

**Sub : Report of the present status of NULM building within Bankura Municipality**

**Ref : This office memo no. ME/240/1M-54/14 Pt. -VI dt. 14.06.19**

Inviting reference above I would like to inform you that a time of 20 days have been past from issuance of this letter and a report is hereby sought for about what actions you have taken so far, by 10.07.19 positively for the interest of work.

Sdt  
Chief Engineer, MED

No. ME/ 299/1/1M-54/14 Pt. -VI

Dated : 05.07.2019

Copy forwarded for information and necessary action to :

✓ 1. Sri Joly Choudhuri, Joint Secretary, UD&MA Deptt. Govt. of West Bengal.

S. Debnath  
05.07.19  
Chief Engineer, MED

Ma/1

GOVERNMENT OF WEST BENGAL  
OFFICE OF THE EXECUTIVE ENGINEER, BANKURA DIVISION  
MUNICIPAL ENGINEERING DIRECTORATE  
KENDUADIHI, BANKURA  
U.D. & M.A. DEPARTMENT

Ph. No.: 03242-250922

Memo No. - MED/BKU/321/NULM-1/15 Pt-II Date: 10.07.2019

From: The Executive Engineer,  
Bankura Division,  
M. E. Dte.

To: The Director,  
SUDA,  
Bidhan nagar,  
Kolkata- 700106.

C. D. S. M. M.  
H

**Sub:** Present status of Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality UNDER NULM. Lay out Plot No. 817 (RS), Mouza- Bankura, JL No-211 Bankura.

Sir,

As per review meeting on physical & financial progress of sanctioned shelter unit for urban homeless (SUH) under DAY-NULM on 05.07.2019 at the conference hall of SUDA, I am to submit present status report of the above mentioned work as follows.

- | Sl.No. | Date --       | Activities --   |
|--------|---------------|---|
| 1.     | 22.05.2017 :- | Work Order issued with time period of 550 days. (Vide memo no-610/VIII-14 Dt. 22.05.2017)   |
| 2.     | 22.09.2017:-  | Site is free from encroachment on august 2017 and this Office asked to the agency to start the work (Vide memo no – MED/BKU/440/NULM-1/2015 Dt. 22.09.2017.) therefore, <u>three months were</u> consumed without any work due to site encroachment.  |
| 3.     | 10.11.2017:-  | Inspite of several correspondences, the agency did not take any initiation to start the work, therefore this office requested the Chairman, Bankura Municipality to issue a show cause notice for imposing penal action of contract against the agency. (Vide memo no - MED/BKU/517/NULM-1/2015 Dt. 10.11.2017.                         |
| 4.     | 13.11.2017:-  | The Chairman, Bankura Municipality forward the prayer of the agency claiming enhancement of rate due to GST. (Vide memo no - 2575/ VIII-14(NULM) Dt. 13.11.2017)  |
| 5.     | 21.11.2017:-  | In reply of Chairman's letter, The S.E. (S.C) stated that Contractor's claim would be entertained as per financial rule (Notification no – 6943-F(Y) Dt. 13.11.2017) but he has to start the work and to complete in time- otherwise penal measure as per condition of contract is to be imposed by the Chairman, Bankura Municipality. |

[ S.E's memo no- MED/SE(S)/642/NULM-1/15 Dt. 21.11.2017]



6. 22.11.2017:- The Chairman, Bankura Municipality, has asked to the concerned agency to start the work. (Vide memo no- 2689/VIII-14(NULM) Dt. 22.11.2017.
7. 08.12.2017:- Work started as per the concerned agency's memo no- nil Dt.08.12.2017
8. 02.01.2018:- This office informed the S.E. (S.C) that pilling work by hydraulic pilling which was considered in the tender estimate is not possible due to adjacent dilapidated buildings and pilling by auger bore method is to be taken up and as per revised soil report , it is decided to expand the building horizontally. The S.E. (S.C) approved the revised drawing. (Vide memo no – MED/SE(SY)755/NULM-I/15 Dt. 03.01.2018.)
9. 05.01.2018 One copy of vetted modified drawing was forwarded to the Director of SUDA for information. (Vide memo no- MED/BKU/648/NULM-1/2015 Dt. 05.01.2018.
10. 15.11.2018:- This office again asked the concerned agency for his slow progress mentioning not to complete the work proportionate to the time.(Vide memo no – MED/BKU/496/NULM-1/15 Pt - II Dt. 13.05.2019 Dt. 15.11.2018
11. 12.03.2019 Work has been stopped after completion of ground floor roof casting. Required time extension is also issued to the agency.
12. 13.05.2019:- The agency is again asked to resume the work by this office. (Vide memo no- MED/BKU/220/NULM-1/15 Pt - II Dt. 13.05.2019)
13. 04.07.2019:- As the concerned agency did not take any initiation to resume the work, recommendation for imposing penal action of contract against the concerned agency, is issued to the Municipality. (Vide memo no-MED/BKU/314/NULM-1/15 Pt- II Dt. 04.07.2019.
14. 10.07.2019 The work is stopped till this date.

This is for your kind information please.

Thanking You,

Yours Faithfully,

Executive Engineer  
Bankura Division


M.E. Dte

24-10-7-19

No - MED/BKU/321(U)/NULM-1/15 Pt-II

Copy forwarded for information and taking necessary action please:-

- ✓ 1) The Chief Engineer , M.E.Dte.
- 2) The Superintending Engineer ( S.C)
- 3) The Chairman, Bankura Municipality.

  
Executive Engineer  
Bankura Division  
10/07/19

No. ME/ 33 / 14-54 / 14 Pt-VI Dated:  
Copy forwarded for information and taking necessary action to:-

1. Sri Jolly Chowdhury, Joint Secretary, Department of UD & MA, Govt. of West Bengal, Nagarayan.

15.07.2019

  
Chief Engineer, M. E. Dte.



## Office of the Municipal Councillors of Bankura

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 , Mobile: 09434115191

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)

:[senguptamahaprasadcm@yahoo.in](mailto:senguptamahaprasadcm@yahoo.in)

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org)

From: *Sri Mahaprasad Sengupta*

Chairman, Bankura Municipality

Memo. No. / VIII-14

Dated, Bankura : / /2019.



*J.D.*  
*ADP*  
*Soumitra Dk*

To  
Sri Kartick Sen,  
Rajagram,  
Bankura.

Ref :-This office memo no 8624/m, Dt.- 07/03/2019 & MED/BKU/183/NULM-1/15 pt.II, dated – 29/03/2019.

Sub:- Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM. Layout Plot No. 817(RS), Mouza- Bankura, JL No. 211, Bankura.

Sir,

With the above reference and opinion of the S.E.(South Circle) the for departmental supply of steel does not arise as per terms and condition. In this situation you are hereby directed to start the work within seven days after issue of this letter. Otherwise this municipality will take necessary action as per terms and condition of the contract.

*Salt*  
Chairman  
Bankura Municipality

Memo no:- 48 (4)/VIII-14, Dated:- 06/04/19.

Copy forwarded for information,

1. The Director SUDA, Bidhan Nagar, Salt Lake, Kolkata 700106.
2. The Chief Engineer, M.E.Dte., Bikash Bhaban, Kolkata 700067.
3. The Superintending Engineer, M.E.Dte.(South Circle), Kousallya, Khargapur.
4. The Executive Engineer, M.E.Dte., Bankura Division, Kenduadihi, Bankura.

*Maly 06/04/19*  
Chairman  
Bankura Municipality  
*Salt*  
Chairman  
Bankura Municipality  
*06/04/19*



## Office of the Municipal Councillors of Bankura

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 , Mobile: 09434115191

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)  
:senguptamahaprasadcm@yahoo.in

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org).

From: *Sri Mahaprasad Sengupta*

Chairman, Bankura Municipality

Memo. No. *0080* / VIII-14

Dated, Bankura : 12/04/2019.



To  
The Director, SUDA,  
ILGUS BHAVAN, H-C Block, Sector-III,  
Bidhan Nagar, Salt Lake,  
Kolkata 700106.  
West Bengal.

*Handwritten signature and initials*

Ref :- This office memo no 173/m, Dt.- 05/04/2019 & letter No. 48/VIII-14, dated 06/04/2019.

Sub:- Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM. Layout Plot No. 817(RS), Mouza- Bankura, JL No. 211, Bankura.

Sir,

With the above reference the Agency Sri Kartick Sen of above noted work submitted a letter which speaks itself. As a result the progress of work has been temporarily stopped. In this regard I am sending herewith the copy of the letter for your necessary opinion from your end for immediate starting of the said project work.

Thanking you.

Annexure :- As Stated.

*Handwritten signature and date 11-04-19*

Chairman  
Bankura Municipality

Memo no:- *(1)* / VIII-14, Dated:- / / 19.

Copy forwarded for information,

1. The Principal Secretary, Department of UD & MA, Got. of W. B., Nagarayan, DF-8, Sector-I, Bidhan Nagar, Salt Lake, Kolkata - 700064.

*Handwritten signature and date 11/04/19*

Chairman  
Bankura Municipality



*Handwritten signature*  
Chairman  
Bankura Municipality



173/11. Dt- 08/04/19.

# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Ref. No. /.....

Date 08-04-2019

To  
The Chairman  
Bankura Municipality

Sub: Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM, Layout plot No-817(R.S), Mouza- Bankura JI No-211 Bankura.

Ref:- NIT NO WBMDA/CM/BM/24/MULM/2016-17 of office memo no – 3106/VIII-14 Dated -21/01/2017 .

Ref:- 48/VIII-14 Dated-06/04/2019

মাননীয় মহাশয়

আপনার নিকট জানাই যে উপরোক্ত কাজের জন্য ইংরেজী 22.05.2017 তারিখে ওয়ার্ক অর্ডার লইয়া 12.06.2017, 06.07.2017, 07.08.2017, ও 09.11.2017 তারিখ পর্যন্ত বারংবার চিঠি দিয়ে জানাই যে উক্ত জায়গাটি পরিষ্কার করে Layout দেওয়ার ব্যবস্থা করা হোক, কিন্তু অত্যন্ত দুঃখের সাথে জানাই যে অফিস হইতে আমার চিঠির কোন প্রত্যুত্তর দেওয়া হয় নাই।

দীর্ঘদিন পরে গত ইংরেজী 21.11.2017 তারিখে আপনার চেম্বারে S.E, E.E, A.E, S.A.E, (M.E. Det) ও আমি উপস্থিত হইয়া উক্ত কাজের বিভিন্ন আলোচনার পর সিদ্ধান্ত হয় যে উক্ত স্থানে 500 mm dai Ayar pilling হইবে এবং আমাকে অতিরিক্ত G.S.T দেওয়া হইবে, সরকারি আদেশনামা 6943 – F (Y) dated 31.11.2017 অনুসারে। প্রসঙ্গক্রমে উল্লেখ থাকে যে অফিসের নানা চালবাহানা সত্ত্বেও মাত্র 24 ঘন্টার মধ্যে কাজ শুরু করতে বলা হয়। অন্যথা আমার বিরুদ্ধে আইনানুগ ব্যবস্থা গ্রহণ করা হইবে। আমি আপনার আদেশমতে 23.03.2018 তারিখ হইতে বাঁকুড়ার M.E Det অফিসের তত্ত্বাবধানে আগর পাইলের কাজ শুরু করি এবং উক্ত কাজ সময় মতো শেষ হয়।

23.03.2018 তারিখে 5 নম্বর লোড ট্রাক্টর পর দেখা যায় উক্ত স্থানে পাঁচতলা বিল্ডিং নির্মাণ সম্ভব নয় এবং আমাকে মৌখিক ভাবে কাজ বন্ধ রাখবার নির্দেশ দেওয়া হয়। দীর্ঘ দিন পর গত ইংরেজি 03.05.2018 তারিখে মৌখিক ভাবে জানানো হয় যে উক্ত স্থানে প্রায় দ্বিগুণ জায়গা লইয়া তিন তলা বিল্ডিং নির্মাণ করিতে হইবে এবং S.E (South circle M.E Det) অফিসের অনুমোদিত নকশা দেওয়া হয়। কিন্তু আজ পর্যন্ত কোন রূপ পরিবর্তিত এস্টিমেট দেওয়া হয় নাই। যা হইতে আমার পক্ষে বোঝা সম্ভব নয় যে কাজের জন্য কোন নির্মাণ সামগ্রী কতটা প্রয়োজন। যাহা টেন্ডারের শর্ত লঙ্ঘন করে। আমি বাধ্য হয়ে পুনরায় 10.05.2018 তারিখ হইতে কাজ শুরু করি এবং ওয়ার্ক অর্ডার এর নির্দিষ্ট সময়ের মধ্যে এক তলার ছাদ ঢালাই এর কাজ সম্পন্ন করি এবং লক্ষ্য করিলাম টেন্ডারের যে পরিমাণ রডের উল্লেখ আছে তাপ্রায় সব শেষ। এমতাবস্থায় ওয়ার্ক অর্ডারের সময় পার হওয়া সত্ত্বেও বাকি কাজ সম্পন্ন করার জন্য অফিস হইতে অতিরিক্ত রড সরবরাহের আবেদন জানাই। কিন্তু 06.04.2019 তারিখে অফিস হইতে জানানো হয় রড সরবরাহ সম্ভব নয় এবং ওয়ার্ক অর্ডার এর নির্দিষ্ট সময় পার হওয়া সত্ত্বেও সাত দিনের মধ্যে কাজ শুরু করার নির্দেশ দেওয়া হয়, যাহা টেন্ডারের শর্ত লঙ্ঘন করে।

মহাশয়ের নিকট বিনীতভাবে জানাতে চাই যে বাকি কাজ সম্পন্ন করতে যে পরিমাণ টেন্ডারের বাইরে অতিরিক্ত রড প্রয়োজন তা আমি কিভাবে কোথায় পাব। সুতরাং মহাশয় নিকট পুনরায় বিনীত আবেদন যে যদি অফিস হইতে টেন্ডার এর বাইরে অতিরিক্ত রড সরবরাহের ব্যবস্থা না করা হয় তাহলে আমার পক্ষে আর কাজ করা সম্ভব নয়, সুতরাং আজ পর্যন্ত আমি যা কাজ করিয়াছি তাহার যথাযথ পরিমাপ করিয়া, পেমেন্টের সুব্যবস্থা করিয়া আমাকে উক্ত কাজ হইতে অবহিত দেওয়ার আদেশদানে মর্জি হবেন।

ধন্যবাদান্তে

আপনার একান্ত অনুগত

KARTICK SEN

  
Proprietor

Copy forwarded for information,

1. The Director SUDA, Bidhannagar, Salt Lake, Kolkata 700106
2. The chief Engineer M.E.Det, Bikash Bhaban Kolkata 700067
3. The Superintending Engineer M.E.Dte. (south Circle) Kousliya Khargapur
4. The Executive Engineer M.E.Dte. Bankura Division, Kenduadihi Bankura

S. Chand  
S.A.E (P.W.D)  
for Referral  
11/4/19

The above stated work is totally supervised by the EIC, M.E Dte. Bankura Division. So it may necessary to take opinion from their end. Submitted for necessary order. Yes and send also Director SUDA 11/4/19



# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM

BANKURA (W.B.)

Mobile : 9232694223

Email : kartick37@yahoo.com

karticksen75@gmail.com

Ref. No. ....

Date .....

To  
The Chairman  
Bankura Municipality



JD  
Leop  
Sourav D

Sub: Construction of 50 bedded five storied building and ancillary work for shelter for urban homeless within jurisdiction of Bankura Municipality under NULM, Layout plot No-817(R.S), Mouza- Bankura JI No-211 Bankura.

Ref:- NIT NO WBMDA/CM/BM/24/MULM/2016-17 of office memo no – 3106/VIII-14 Dated -21/01/2017 .

Ref:- 48/VIII-14 Dated-06/04/2019

মাননীয় মহাশয়

আপনার নিকট জানাই যে উপরোক্ত কাজের জন্য ইংরেজী 22.05.2017 তারিখে ওয়ার্ক অর্ডার লইয়া 12.06.2017, 06.07.2017, 07.08.2017, ও 09.11.2017 তারিখ পর্যন্ত বারংবার চিঠি দিয়ে জানাই যে উক্ত জায়গাটি পরিষ্কার করে Layout দেওয়ার ব্যবস্থা করা হোক, কিন্তু অত্যন্ত দুঃখের সাথে জানাই যে অফিস হইতে আমার চিঠির কোন প্রত্যুত্তর দেওয়া হয় নাই।

দীর্ঘদিন পরে গত ইংরেজী 21.11.2017 তারিখে আপনার চেয়ারে S.E, E.E, A.E, S.A.E, (M.E. Det) ও আমি উপস্থিত হইয়া উক্ত কাজের বিভিন্ন আলোচনার পর সিদ্ধান্ত হয় যে উক্তস্থানে 500 mm dai Ayar pilling হইবে এবং আমাকে অতিরিক্ত G.S.T দেওয়া হইবে, সরকারি আদেশনামা 6943 – F (Y) dated 31.11.2017 অনুসারে। প্রসঙ্গক্রমে উল্লেখ থাকে যে অফিসের নানা চালবাহানা সত্ত্বেও মাত্র 24 ঘন্টার মধ্যে কাজ শুরু করতে বলা হয়। অন্যথা আমার বিরুদ্ধে আইনানুগ ব্যবস্থা গ্রহণ করা হইবে। আমি আপনার আদেশমতে 23.03.2018 তারিখ হইতে বাঁকুড়ার M.E Det অফিসের তত্ত্বাবধানে আগর পাইলের কাজ শুরু করি এবং উক্ত কাজ সময় মতো শেষ হয়।

23.03.2018 তারিখে 5 নম্বর লোড টেস্টের পর দেখা যায় উক্ত স্থানে পাঁচতলা বিল্ডিং নির্মাণ সম্ভব নয় এবং আমাকে মৌখিক ভাবে কাজ বন্ধ রাখবার নির্দেশ দেওয়া হয়। দীর্ঘ দিন পর গত ইংরেজী 03.05.2018 তারিখে মৌখিক ভাবে জানানো হয় যে উক্ত স্থানে প্রায় দ্বিগুণ জায়গা লইয়া তিন তলা বিল্ডিং নির্মাণ করিতে হইবে এবং S.E (South circle M.E Det) অফিসের অনুমোদিত নকশা দেওয়া হয়। কিন্তু আজ পর্যন্ত কোন রূপ পরিবর্তিত এন্টিমেট দেওয়া হয় নাই। যা হইতে আমার পক্ষে বোঝা সম্ভব নয় যে কাজের জন্য কোন নির্মাণ সামগ্রী কতটা প্রয়োজন। যাহা টেন্ডারের শর্ত লঙ্ঘন করে। আমি বাধ্য হয়ে পুনরায় 10.05.2018 তারিখ হইতে কাজ শুরু করি এবং ওয়ার্ক অর্ডার এর নির্দিষ্ট সময়ের মধ্যে এক তলার ছাদ ঢালাই এর কাজ সম্পন্ন করি এবং লক্ষ্য করিলাম টেন্ডারের যে পরিমাণ রডের উল্লেখ আছে তাপ্রায় সব শেষ। এমতাবস্থায় ওয়ার্ক অর্ডারের সময় পার হওয়া সত্ত্বেও বাকি কাজ সম্পন্ন করার জন্য অফিস হইতে অতিরিক্ত রড সরবরাহের আবেদন জানাই। কিন্তু 06.04.2019 তারিখে অফিস হইতে জানানো হয় রড সরবরাহ সম্ভব নয় এবং ওয়ার্ক অর্ডার এর নির্দিষ্ট সময় পার হওয়া সত্ত্বেও সাত দিনের মধ্যে কাজ শুরু করার নির্দেশ দেওয়া হয়, যাহা টেন্ডারের শর্ত লঙ্ঘন করে।

মহাশয়ের নিকট বিনীতভাবে জানাতে চাই যে বাকি কাজ সম্পন্ন করতে যে পরিমাণ টেন্ডারের বাইরে অতিরিক্ত রড প্রয়োজন তা আমি কিভাবে কোথায় পাব। সুতরাং মহাশয় নিকট পুনরায় বিনীত আবেদন যে যদি অফিস হইতে টেন্ডার এর বাইরে অতিরিক্ত রড সরবরাহের ব্যবস্থা না করা হয় তাহলে আমার পক্ষে আর কাজ করা সম্ভব নয়, সুতরাং আজ পর্যন্ত আমি যা কাজ করিয়াছি তাহার যথাযথ পরিমাপ করিয়া, পেমেন্টের সুব্যবস্থা করিয়া আমাকে উক্ত কাজ হইতে অবহিত দেওয়ার আদেশদানে মর্জি হবেন।

ধন্যবাদান্তে

আপনার একান্ত অনুগত

KARTICK SEN

Proprietor

Copy forwarded for information,

1. The Director SUDA, Bidhannagar, Salt Lake, Kolkata 700106
2. The chief Engineer M.E.Det, Bikash Bhaban Kolkata 700067
3. The Superintending Engineer M.E.Dte. (south Circle) Kousliya Khargapur
4. The Executive Engineer, M.E.Dte. Bankura Division, Kenduadihi Bankura

# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Date 12-06-2017

M 2141  
12-06-17

*[Signature]*

To,  
The Executive Engineer,  
MED, Bankura Division  
Bankura

**Sub:-** Prayer for handing over the clear site along with Layout of the Building.

**Ref:-** Work Order No. 618/VII-14 dt.22/05/2017 against NIT no.  
WBMAD/CM/BM/24/NULM/2016-17 VIED OFFICE MEMO NO.  
3106/VIII-14 dt 21/01/2017

Respected Sir,

I the under signed have received the above stated reference work, so, I, would like to request your kind self to hand over me the clear site as well as arrange for layout of the above stated work at the earliest. Please do the needful and oblige.

Thanking You,  
Yours Faithfully,

KARTICK SEN

*[Signature]*  
Proprietor

Copy To :-

- 1) Chairman, Bankura Municipality





# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile: 9232694223  
Email: kartick37@yahoo.com  
karticksen75@gmail.com

Date: 05-07-2017

To,  
The Chairman,  
Bankura Municipality,  
Bankura

Sub :- Construction of 50 bedded five storied Building and ancillary work for shelter for Urban Homeless within Jurisdiction at Bankura Municipality under NULM. Lay out Plot No.- 817 (R.S.) , Mouza - Bankura, J.L. No.- 211 Bankura.

Ref. :- Work order No.- 618 / VIII-14 dated 22/05/2017

মাননীয় মহাশয়,

আপনার অবগতির জন্য জানাই যে উক্ত কাজের জন্য Lay out দেওয়ার জন্য আবেদন করিয়াছিলাম গত ইংরেজী 12-06-2017 তারিখে, কিন্তু আজ পর্যন্ত Lay out দেওয়া হয় নাই।

মহাশয়ের নিকট আবেদন যাহাতে উক্ত কাজের তাড়াতাড়ি Lay out দেওয়া হয়, তাহার প্রয়োজনীয় ব্যবস্থা গ্রহন করিলে উপকৃত হইবে।

ধন্যবাদান্তে,

KARTICK SEN

  
Proprietor

অনুলিপি প্রেরিত হইল :-

(1) The Executive Engineer , M.E.D.  
Kenduadihi, Bankura.

# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Date ..07.08..2017.....

Ref No. ....

To,  
The Chairman  
Bankura Municipality  
Bankura.

Sub: Construction of 50 bedded five storied  
Building and ancillary work for shelter  
for Urban Homeless within jurisdiction  
at Bankura Municipality under NULM.  
Lay out plot No- 817 (R.S) Mouza-Bankura,  
J.L. No- 211 Bankura.

Ref :- work order No. 618/VIII-14 dated 22/05/2017

মাননীয় মহাস্বামী,

আপনার অসাময়িক জন্য প্রার্থনা যে উক্ত কাজের  
জন্য Lay out দেওয়ার জন্য আবেদন করিয়েছিলেন  
যা সংস্কৃতি 6-7-2017 তারিখে, কিছু কাজ পর্যন্ত  
Lay out দেওয়া হয়।  
মহাস্বামীর দেরি আবেদন মাফ  
করে কাজের তারিখ - Lay out দেওয়া হয়,  
তারপর প্রয়োজনীয় ব্যবস্থা গ্রহণ করিলে উক্ত  
কাজ।

কর্তৃকৃত,  
KARTICK SEN  
Proprietor

**KARTICK SEN**

Govt. Contractor &amp; General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Date 09.11.2017

To  
The Chairman  
Bankura Municipality  
Bankura

Sub:- Acceptance cum work order for construction of 50 bedded five storied building and ancillary work to shelter for urban homeless within jurisdiction of Bankura municipality under NULM. Layout plan no.817(R.S), mouza-Bankura, JI no.211 Bankura .

Ref:- NIT NO.WBMAD/CM/BM/24/NULM/2016-17 of office memo no. 3106/VIII-14 Dated-21/01/2017

Ref:-Your latter of acceptance cum work order no.618/VIII-14 Dated-22/05/2017

Sir,

I would like to inform you that the work order for the above mentioned work. Thought issued 22/05/2017 but could not taken up for want of clear site free from encroachment not made available to me. I must mention that the estimated amount put to tender being Rs.1,84,07,355.00 was made basing on 3% VAT. But the Govt. of India introduced G.S.T. from 1<sup>st</sup> July 2017. So as per pre G.S.T. contract agreement which is exclusive of VAT need to be revised of contractual value in the contract due to impact of change in tax rate.

So I would request you to kindly revise the project value with a G.S.T. rate of 6% CGST and 6% SGST excluding VAT 3% . As otherwise it would adversely affected to the agency. Kindly decide and communicate your value decision earliest to help me to commence the work.

Thanking You

Yours Faithfully

*Kartick Sen*

Copy Forwarded to information

1. The Superintendent Engineer M.E.Dte. Khargapur
2. Executive Engineer, M.E.Dte. Bankura

Received. Two copy SE & EE







## Office of the Municipal Councillors of Bankura

Office : 250367,250344,254804

Fax : 03242-259269 / 250367

Resi : 03242-253338 . Mobile: 09434115191

E-mail : [bankuramunicipality@rediffmail.com](mailto:bankuramunicipality@rediffmail.com)

: [senguptamahaprasadm@yahoo.in](mailto:senguptamahaprasadm@yahoo.in)

Website : [WWW.bankuramunicipality.org](http://WWW.bankuramunicipality.org).

From: *Sri Mahaprasad Sengupta*

Chairman, Bankura Municipality

Memo. No. **2689** / VIII-14 (NULM)

Dated, Bankura : **22/11/17**.

✓  
To  
Kartick Sen,  
Rajagram,  
Bankura.

Ref:- Memo No. – MED/BKU/ 534 /NULM-1/15, Dated – 21/11/2017

Sub:- Construction of 50 Bedded five storied Building under NULM within jurisdiction of Bankura Municipality.

Dear,

With the above reference you are hereby directed to start the work of NULM Project as early as possible because the work order had been issued to you on dated 25/05/2017 and almost six months have passed away. In this connection the photocopy of the letter as received from the Superintending Engineer, South Circle, M. E. Directorate, against your prayer dated 09/11/2017 for the revised project value with a G.S.T. rate has been enclosed herewith.

You are also directed to submit the work programme within 24 hours after receiving this letter otherwise this Municipality will impose penal action towards termination of contract as per finance rule.

*22/11/17*  
Chairman  
Bankura Municipality  
*22-11-17*  
Chairman  
Bankura Municipality

Enclosure :- photocopy of the letter as received from the Superintending Engineer, South Circle, M. E. Directorate.

Memo no:- (4)/VIII-14(NULM), Dated:- / /17.

Copy forwarded for information and take necessary action from your end.

1. The Director, SUDA, ILGUS BHAVAN, HC Block. Sector – III, Bidhannagar. Kolkata 700106. West Bengal.
2. The Secretary, Department of UD & MA, Government of West Bengal, Town & Country Planning Branch, Government of West Bengal, Nagarayan, DF-8, Sector-I, Bidhan Nagar, Kolkata - 700064
3. The Superintending Engineer (South), Municipal Engineering Directorate (South Circle), Kousallya, P.O. Khargpur, Dist:- Paschim Midnapur.
4. The Executive Engineer, M.E.Dte., Bankura Division, Kenduadihi, Bankura.

*sd*  
Chairman  
Bankura Municipality



(South Circle)

Municipal Engineering Directorate  
Koushallya, P.O: Kharagpur, Dist: Paschim Medinipur

No. MED/SE (S) / 612 / NULM - 1 / 15

Dated: 21.11.2017

From Superintending Engineer  
South Circle

To The Executive Engineer  
Bankura Division, M.E. Dte  
Bankura

Sub - Construction of 50 bedded five storied Building under NULM within Bankura Municipality.

Ref Work Oder No 618/VIII-14 dated 22.05.2017

Agency memo No Nil dated 09.11.2017

Memo No 2575/VIII-14(NULM) dated 13.11.2017 of the Chairman of Bankura Municipality

His memo No MED/BKU/527/NULM-1/2015 dated 16.11.2017

It is unfortunate to record that the Agency is deferring his Program time and again on different reasons. As a result, it is difficult to draw a firm conclusion in respect of the fate of the contract.


However, the Finance department of Govt. of West Bengal vide its Notification No 6943-F(Y) dated 13.11.2017 has modified its earlier Notification No 5050-F(Y) dated 16.08.2017.

Now, in terms of Notification No 6943-F(Y) dated 13.11.2017, enhanced percentage up to maximum ceiling of 9.50% on the value of goods as agreed upon in the contract may be allowed to the Contractor in case of composite supply of works contract as defined in Clause (119) of Section 2 of West Bengal Goods and Service Tax Act, 2017 subject to condition that:

1. The Agency would submit valid papers/documents in support of its claim and
2. The goods in question fall under GST rate of 18%
3. If the goods rate falls below 18% rate then enhanced rate would be proportionately reduced.

Now, he is requested to ask the concerned Agency in writing whether he is agreeable to undertake the work without further delay and to complete the same in time. Otherwise he is requested to recommend the Chairman of Bankura Municipality to terminate the Contract along with penal measure as per condition of the Contract. Xerox copy of the said Notification is enclosed herewith.

Encl: As stated above


  
(Superintending Engineer)  
Superintending Engineer  
South Circle, M.E. Dte.  
Govt. of West Bengal  
Dept. of M.A.

Dated: 21/11/2017

No. MED/SE (S) / 612 (2) / NULM - 1 / 15

Copy forwarded for information to:

1. The Chairman, Bankura Municipality, Bankura.
2. Karick Sen, Raigram, Bankura.

  
(Superintending Engineer)  
Superintending Engineer  
South Circle, M.E. Dte.  
Govt. of West Bengal  
Dept. of M.A.

Dated: 21/11/2017



# KARTICK SEN

Govt. Contractor & General Order Supplier

RAJGRAM  
BANKURA (W.B.)  
Mobile : 9232694223  
Email : kartick37@yahoo.com  
karticksen75@gmail.com

Date ... 08-12-2017

H 10597  
8 12 17

To,  
The Chairman,  
Bankura Municipality,  
Bankura.

Sub: Construction of 50 Bedded five storied Building and ancillary work for shelter for Urban Homeless within jurisdiction of Bankura Municipality under NULM. Lay out Plot no. - 817(R.S.), Mouza-Bankura, J.L. No. 211 Bankura.

Ref. : A) Work Order No.- i) 618/VIII-14, dated- 22.05.17 & ii) MED/BKU/95/NULM-1/2015, dt. 25.05.17.

B) NIT No. -WBMAD/CM/BM/24/NULM/2016-2017.

Sir,

With due respect, I beg to state that as per above reference order I take over the site and going to start the work on execution of 500mm dia. Agar pilling work as per discussion on 21.11.2017 at your Office Chamber with the presence of S.E., E.E., and A.E. of MED of concern Division for Agar pilling instead of DMC pilling, it is observed that the depth are not going as desired after below 5 to 7 metre.

So, please give me the necessary instruction for this situation, keeping in view that huge materials for the said work are stacked in the said site.

Thanking you,

Yours faithfully,

KARTICK SEN



(Kartick Sen)

Copy forwarded for information and necessary action to:

- 1) The Superintending Engineer, South Circle, M.E. Dte. Khargapur, Paschim Medinipur.
- 2) The Executive Engineer, Bankura Division, M.E.Dte. Kenduadihi, Bankura-722102.





# KARTICK SEN

Govt. Contractor & General Order Supplier

8/2 8624/M. Dt. 07-03-19  
RAJGRAM  
BANKURA (W.B.)  
Mobile : 9282694223  
Email : kartick37@yahoo.com  
kartickse75@gmail.com

Date 07-03-2019

To,  
The Chairman,  
Bankura Municipality,  
Bankura.

Sub: Construction of 50 Bedded five storied Building and ancillary work for shelter for Urban Homeless within jurisdiction of Bankura Municipality under NULM. Lay out Plot no. - 817(R.S.), Mouza-Bankura, J.L. No. 211 Bankura.

Ref. : A) Work Order No.- i) 618/VIII-14, dated- 22.05.17 & ii) MED/BKU/95/NULM-1/2015, dt. 25.05.17.

B) NIT No. -WBMAD/CM/BM/24/NULM/2016-2017.

Sir,

With due respect, I beg to state that as per above reference order I would like to inform you that the above stated work has been commenced on 23/11/17 after a long period of about 6(six) months due to vacant the site from your department and letter on due to some technical reasons and revised drawing and design I have to stop the work as per verbal direction from your office though I have completed the roof of the ground floor within the stipulated time period and consumed more or less the schedule quantity of reinforced steel .

In this connection it may be noted that the stipulated time period is over and in the mean time market price of the construction materials are higher than the schedule rate.

So, it is not possible to continue the said work either the material (steel) not supplied from the department.

Thanking you,

Yours faithfully,

  
(Kartick Sen)

Copy forwarded for information and necessary action to :

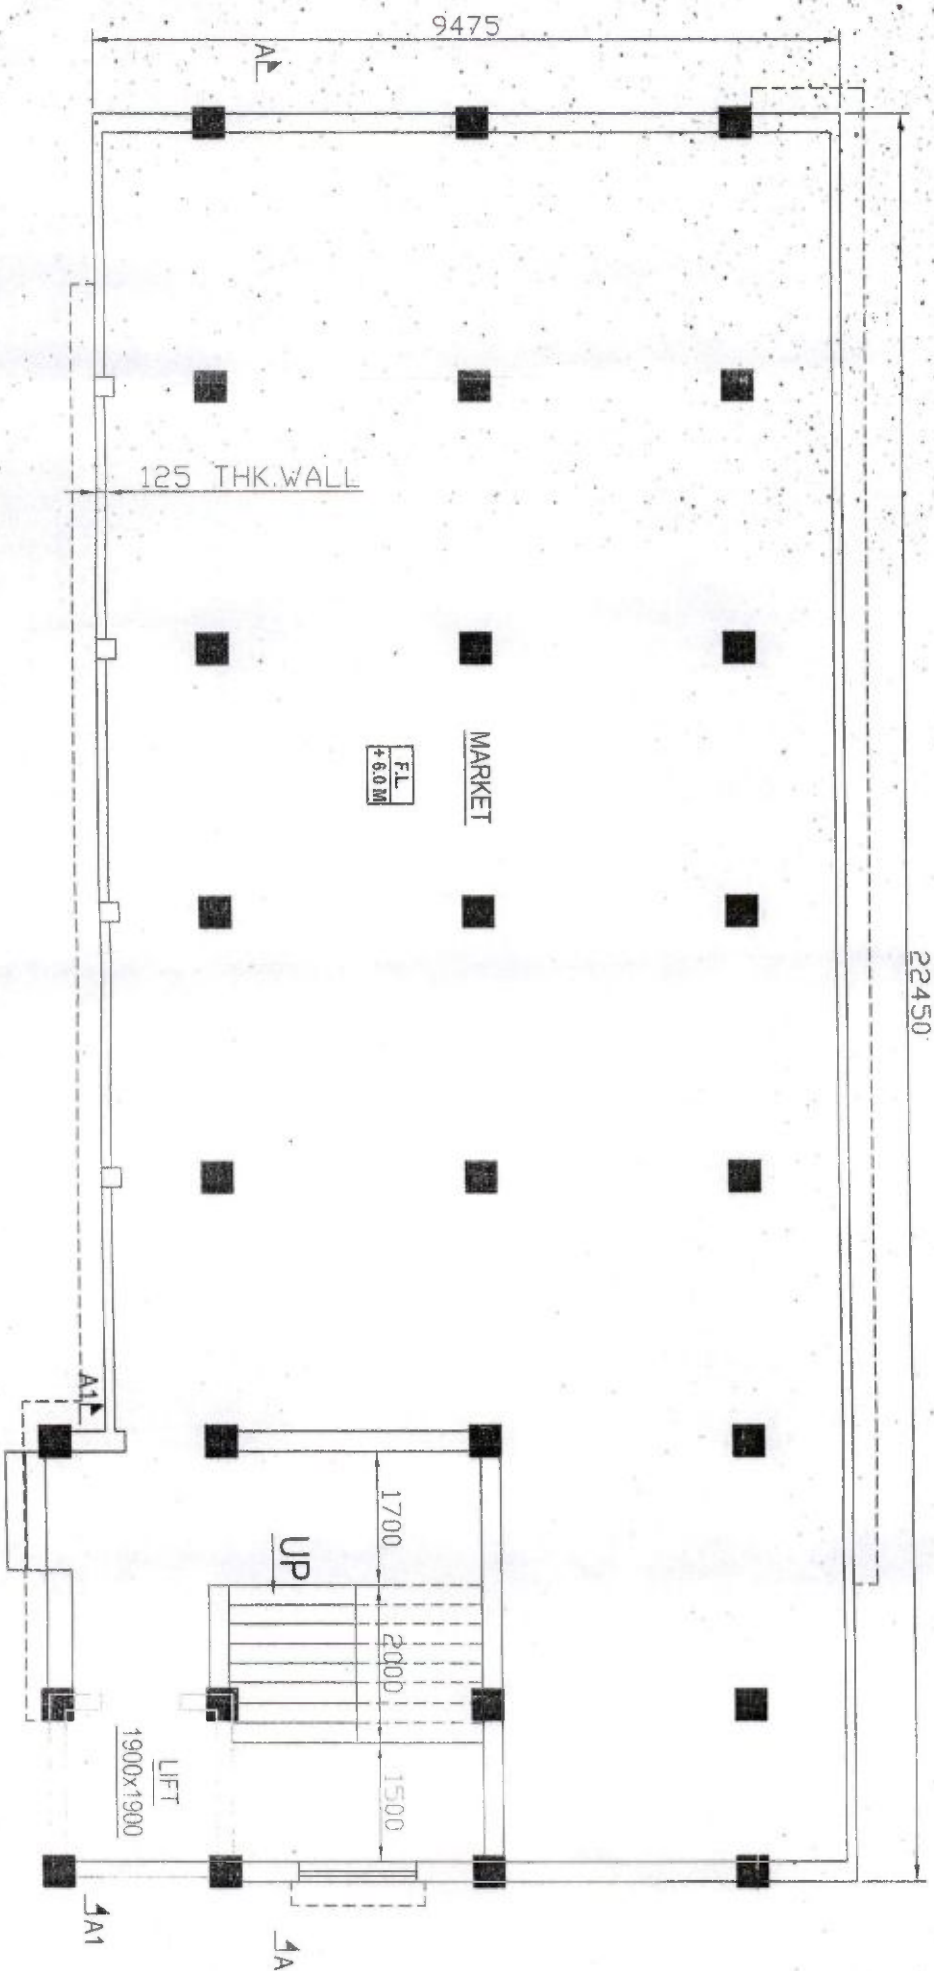
1) The Executive Engineer, Bankura Division, M.E.Dte. Kenduadihi, Bankura-722102.



*Handwritten:* 23.12.16  
*Signature:* [Signature]  
 Structural Engineer  
 M.E. Dhondore  
 11, 12, 13, 14, 15, 16, 17, 18, 19, 20, 21, 22, 23, 24, 25, 26, 27, 28, 29, 30, 31, 32, 33, 34, 35, 36, 37, 38, 39, 40, 41, 42, 43, 44, 45, 46, 47, 48, 49, 50, 51, 52, 53, 54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 64, 65, 66, 67, 68, 69, 70, 71, 72, 73, 74, 75, 76, 77, 78, 79, 80, 81, 82, 83, 84, 85, 86, 87, 88, 89, 90, 91, 92, 93, 94, 95, 96, 97, 98, 99, 100


*Handwritten:* DDN 26/12/16  
 Structural Engineer  
 M.E. Dhondore  
 11, 12, 13, 14, 15, 16, 17, 18, 19, 20, 21, 22, 23, 24, 25, 26, 27, 28, 29, 30, 31, 32, 33, 34, 35, 36, 37, 38, 39, 40, 41, 42, 43, 44, 45, 46, 47, 48, 49, 50, 51, 52, 53, 54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 64, 65, 66, 67, 68, 69, 70, 71, 72, 73, 74, 75, 76, 77, 78, 79, 80, 81, 82, 83, 84, 85, 86, 87, 88, 89, 90, 91, 92, 93, 94, 95, 96, 97, 98, 99, 100

### GROUND FLOOR PLAN

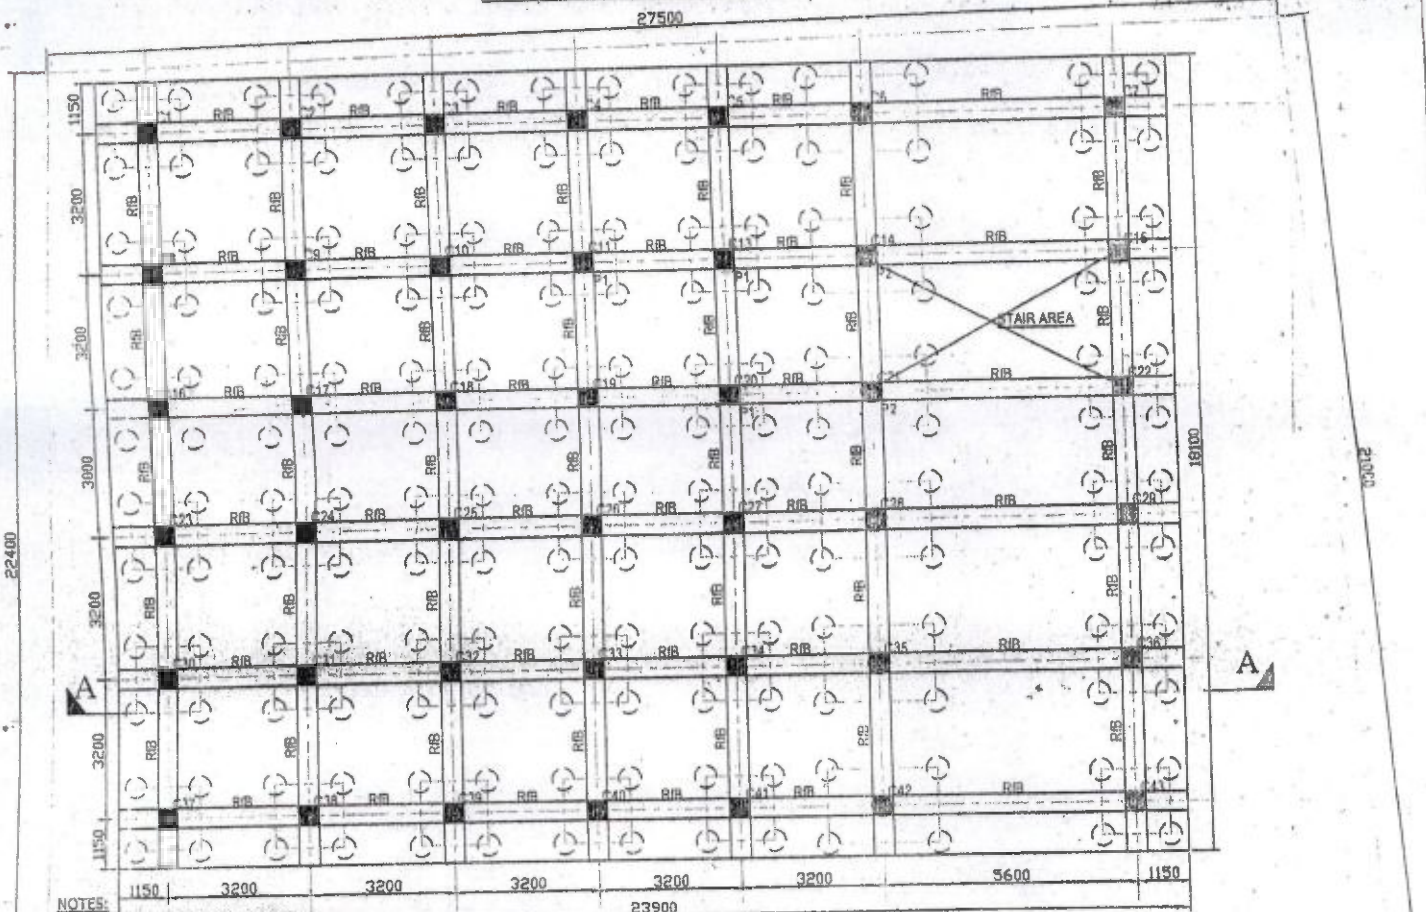


CONSTRUCTION OF 50 BEDED FIVE STORED SHELTER FOR  
 URBAN HOMELESS UNDER NULM [PLOT NO. 817 (R.S)]  
 WITHIN BANKURA MUNICIPALITY





SECTION AT A-A  
TYP. SECTION OF RAFT FOUNDATION



NOTES:  
 1: All dimensions are in mm and level in meter.  
 2: # denotes dia. of R.Y.S.D Bars Fe 500 grade conforming to IS 1786 - 1979 or latest.  
 3: R.C.C will be Nominal mix of (1:2:4)  
 4: R.C.C will be Normal-cure of (20-25) M-25 Grade Controlled Concrete  
 5: Lap length of the bars shall be as per IS 456-2000 or latest.  
 6: Extra bars shall be provided around opening as per standard practice.  
 7: All Concrete will be machine mixed and machine vibrated.  
 8: Potable water will be used for mixing the concrete.  
 9: Execution of work will be as per all relevant IS codes.  
 10: Details of R.C.C-raft slab & raft beam refer sheet 2 of 2 (R2-2018)

CONSTRUCTION OF 50 BEDDED THREE STORIED SHELTER FOR URBAN HOMELESS UNDER NULM [PLOT NO. 817 (R.S)] WITHIN BANKURA MUNICIPALITY  
 DRG NO. MED-BR/KUNIA/M07-2018  
 R2-2018

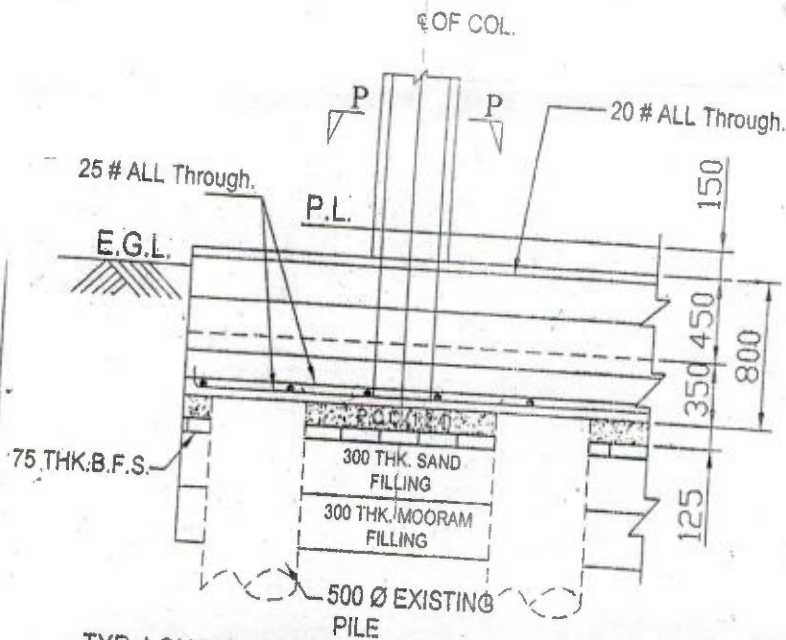
SHEET 01 OF 2

*Bluff*  
 5/11/18  
 Assistant Engineer  
 Bankura Division (Works)  
 M.E. Directorate  
 Govt. of West Bengal

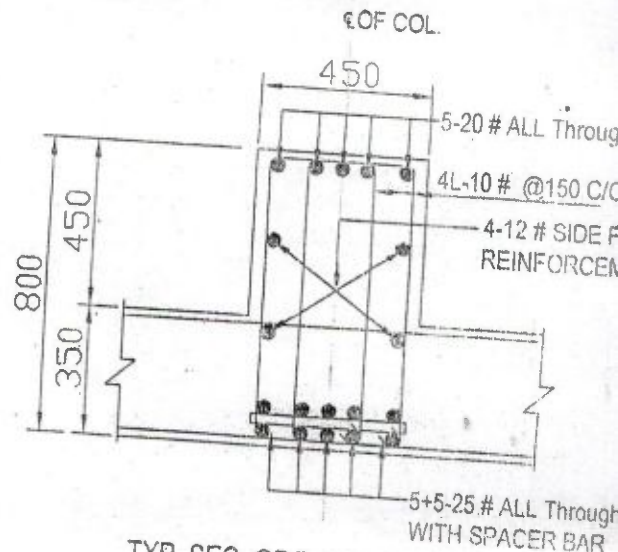
may be approved  
*Bluff*  
 16/11/18  
 ASSISTANT ENGINEER  
 South Circle, M.E. Div  
 Dept. of Municipal Affairs  
 Govt. of West Bengal

Approved  
 05/05/18  
 SUPERINTENDING ENGINEER  
 South Circle, M.E. Directorate  
 Dept. of Municipal Affairs  
 Govt. of West Bengal

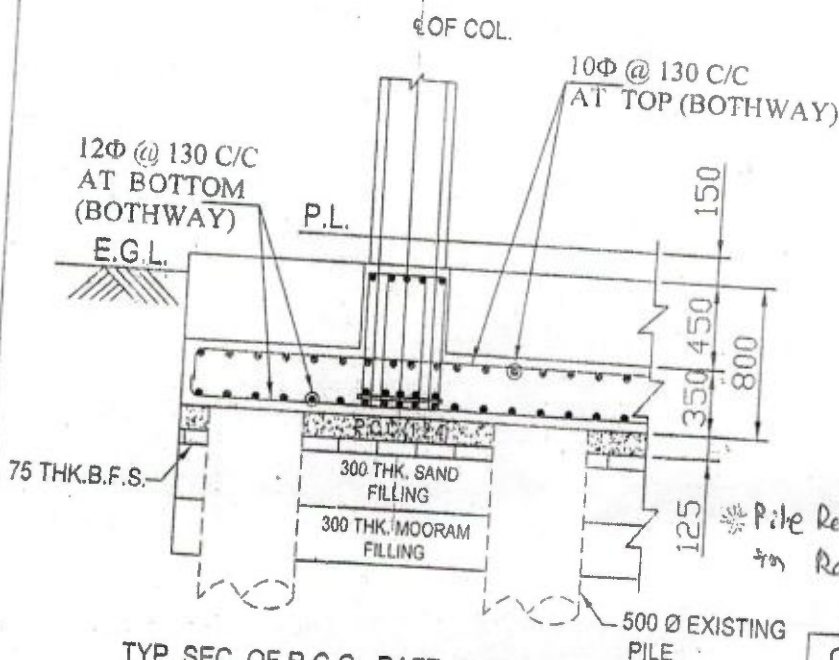





TYP. LONG SEC. OF R.C.C. RAFT BEAM FOUNDATION



TYP. SEC. OF R.C.C. RAFT BEAM MARK-RIB



TYP. SEC. OF R.C.C. RAFT SLAB FOUNDATION



SEC. AT P-P FOR COL. (400x400)

*\* Pile reinforcement must be embedded in Raft concrete*

SHEET 02 OF 2 (R2-2018)

*Doley 16/4/18*  
 ASSISTANT ENGINEER  
 South Circle, E. Dist.  
 Dept. of Public Works  
 Govt. of West Bengal

*5/9/18*  
 Assistant Engineer  
 Bankura Division (Works)  
 M.E. Directorate  
 Govt. of West Bengal

*may be approved*

*[Signature]*  
 16/4/18

*[Signature]*  
 SUPERINTENDENT  
 South Circle, E.  
 Dept. of Public Works

CONSTRUCTION OF 50 BEDED THREE  
 STORED SHELTER FOR URBAN  
 HOMELESS UNDER NULM [PLOT NO.  
 817 (R.S)] WITHIN BANKURA  
 MUNICIPALITY

DRG. NO. MEF

18-2018
